


Structure Notes: 1. PER TDOT D-CB-12LP / ASTM C913 SPEC'S.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO INVERT CHANNEL.
4. JBS 3123 MOD SINGLE SET BY ICAST
5. REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB - DBL MAT #5 BARS.
PER TDOT STD DRAWING D-CB-12LP.
- WALLS (As .62) #5 BARS AT 6" C.C.E.W.
- FLOOR (As .62) #5 BARS AT 6" C.C.E.W.

P2) 32" x 32" - CASTING HEIGHT - 7"
P1) 32" x 32" - BOX BASE 8inW, 8inF, Variable Ht - 45"
1) CASTING - JBS-3123 MODIFIED SET
1) 32" x 32" - Conseal CS-102 1.00"
2) Hole - 26
1) Hole - 6

0 lb
5872 lb
250 lb
0 lb
0 lb
0 lb


Structure Total: 6122 lb

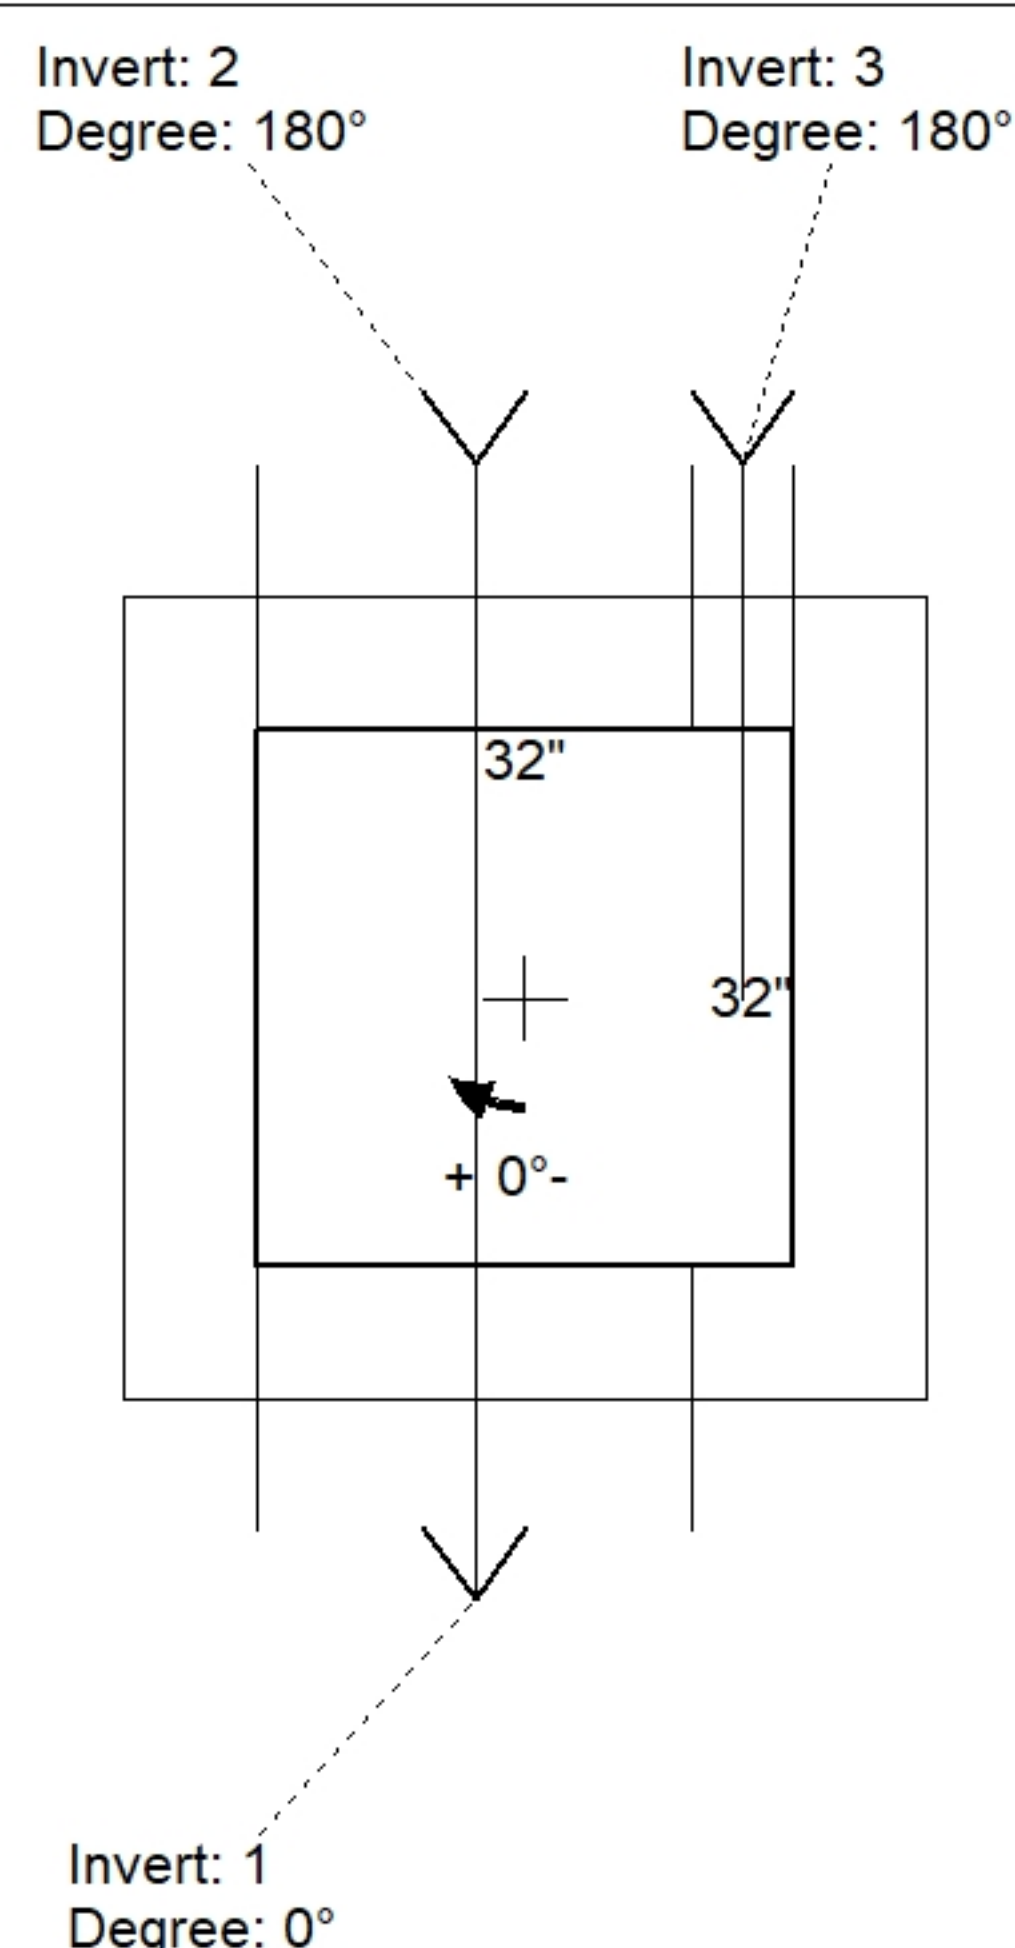

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	809.05'							
Reducer								
Invert 1	804.86'	0°	18" RCP B WALL	23"	26"	Hole 26	0"	P1
Invert 2	805.15'	180°	18" RCP B WALL	23"	26"	Hole 26	3.48"	P1
Invert 3	806.55'	180°	4" HDPE (perf pipe)	4.8"	6"	Hole 6	22.38"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

32" x 32" - CASTING HEIGHT - 7" - (P2)

32" x 32" - BOX BASE 8inW, 8inF, Variable Ht - 45" - (P1)

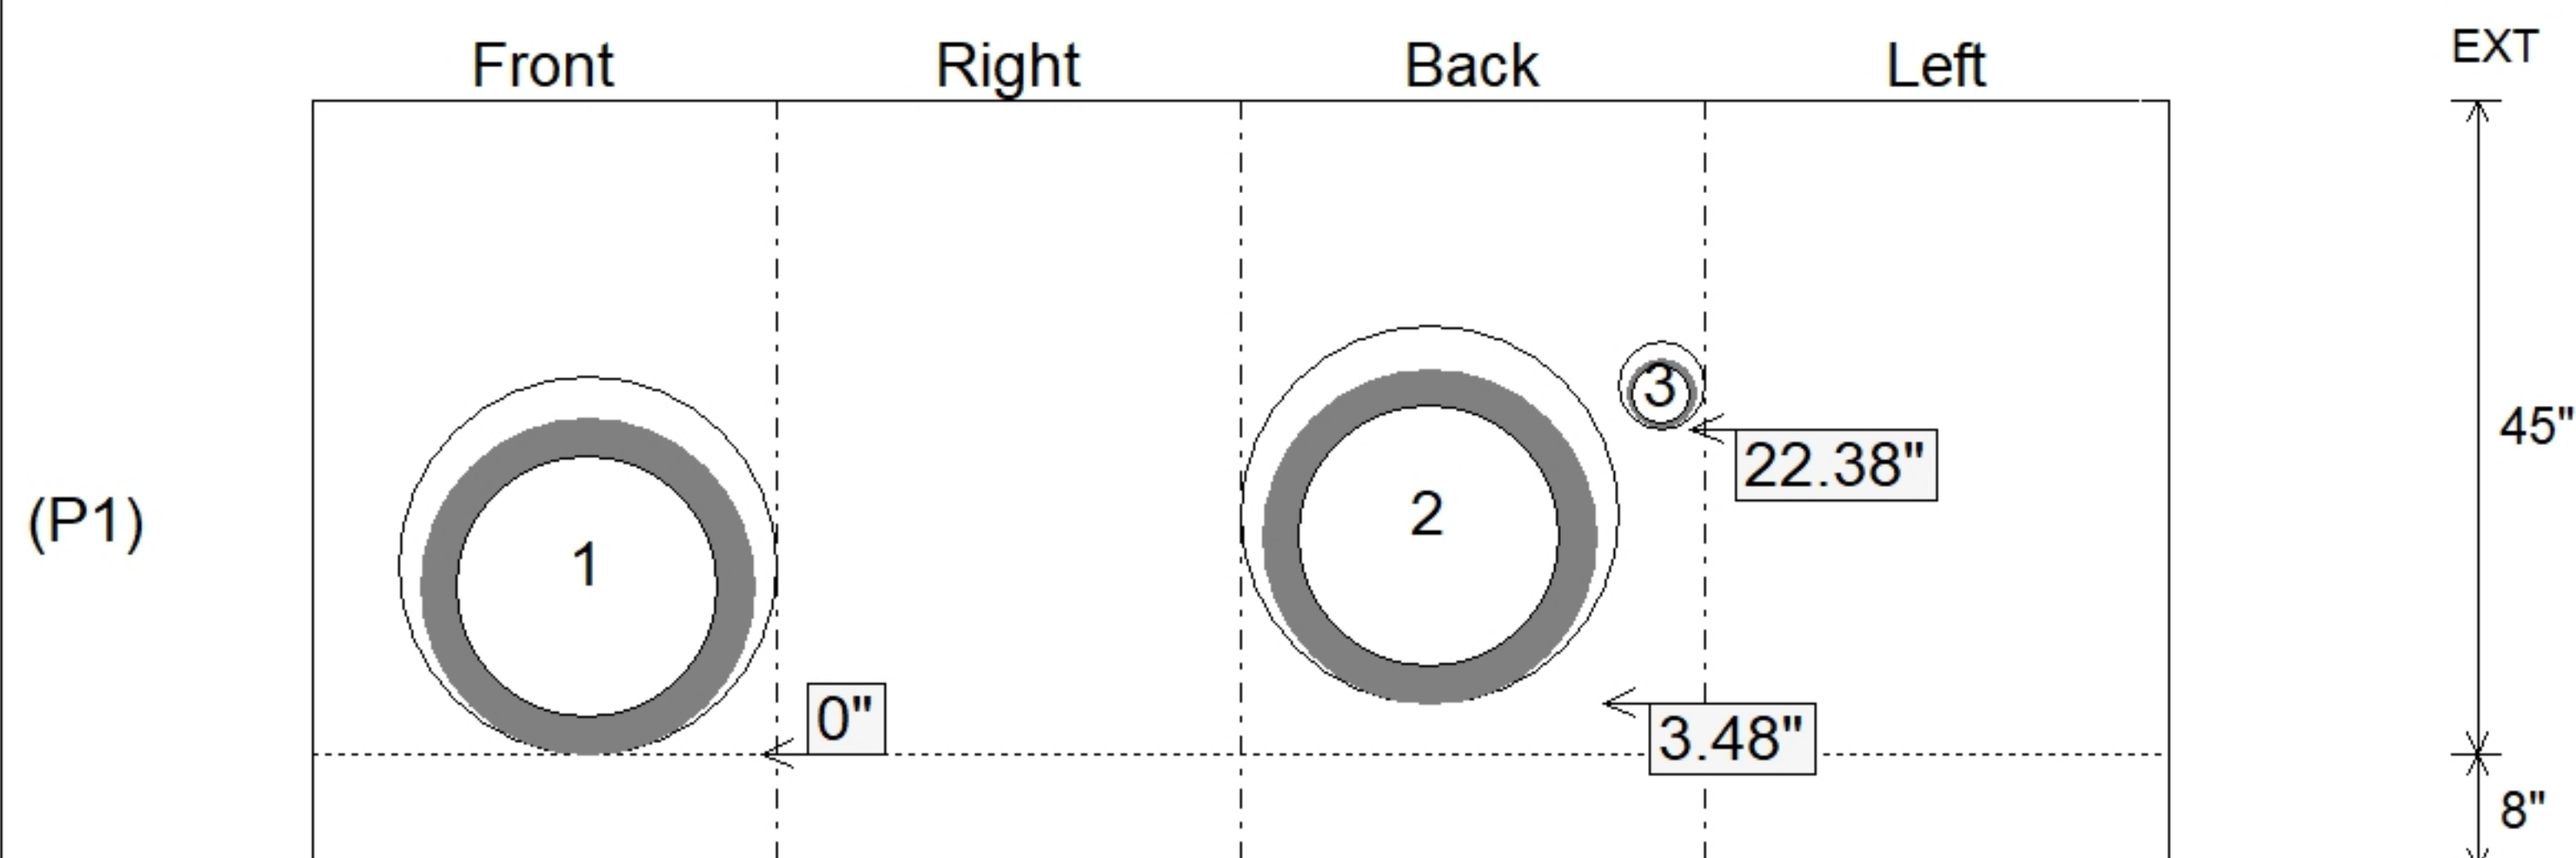

SUBMITTAL
APPROVED BY:
