





Structure Notes: 1. PER TDOT D-CB-12LP / ASTM C913 SPEC'S.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. JBS 3123 MOD SINGLE SET BY ICAST
4. REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB - DBL MAT #5 BARS.
PER TDOT STD DRAWING D-CB-12LP.
- WALLS (As .62) #5 BARS AT 6" C.C.E.W.
- FLOOR (As .62) #5 BARS AT 6" C.C.E.W.


P2) 32" x 32" - CASTING HEIGHT - 7"	0 lb
P1) 32" x 32" - BOX BASE 8inW, 8inF - 48"	5878 lb
1) CASTING - JBS-3123 MODIFIED SET	250 lb
1) 32" x 32" - Conseal CS-102 1.00"	0 lb
2) Hole - 32	0 lb
1) Hole - 6	0 lb
Structure Total:	6128 lb

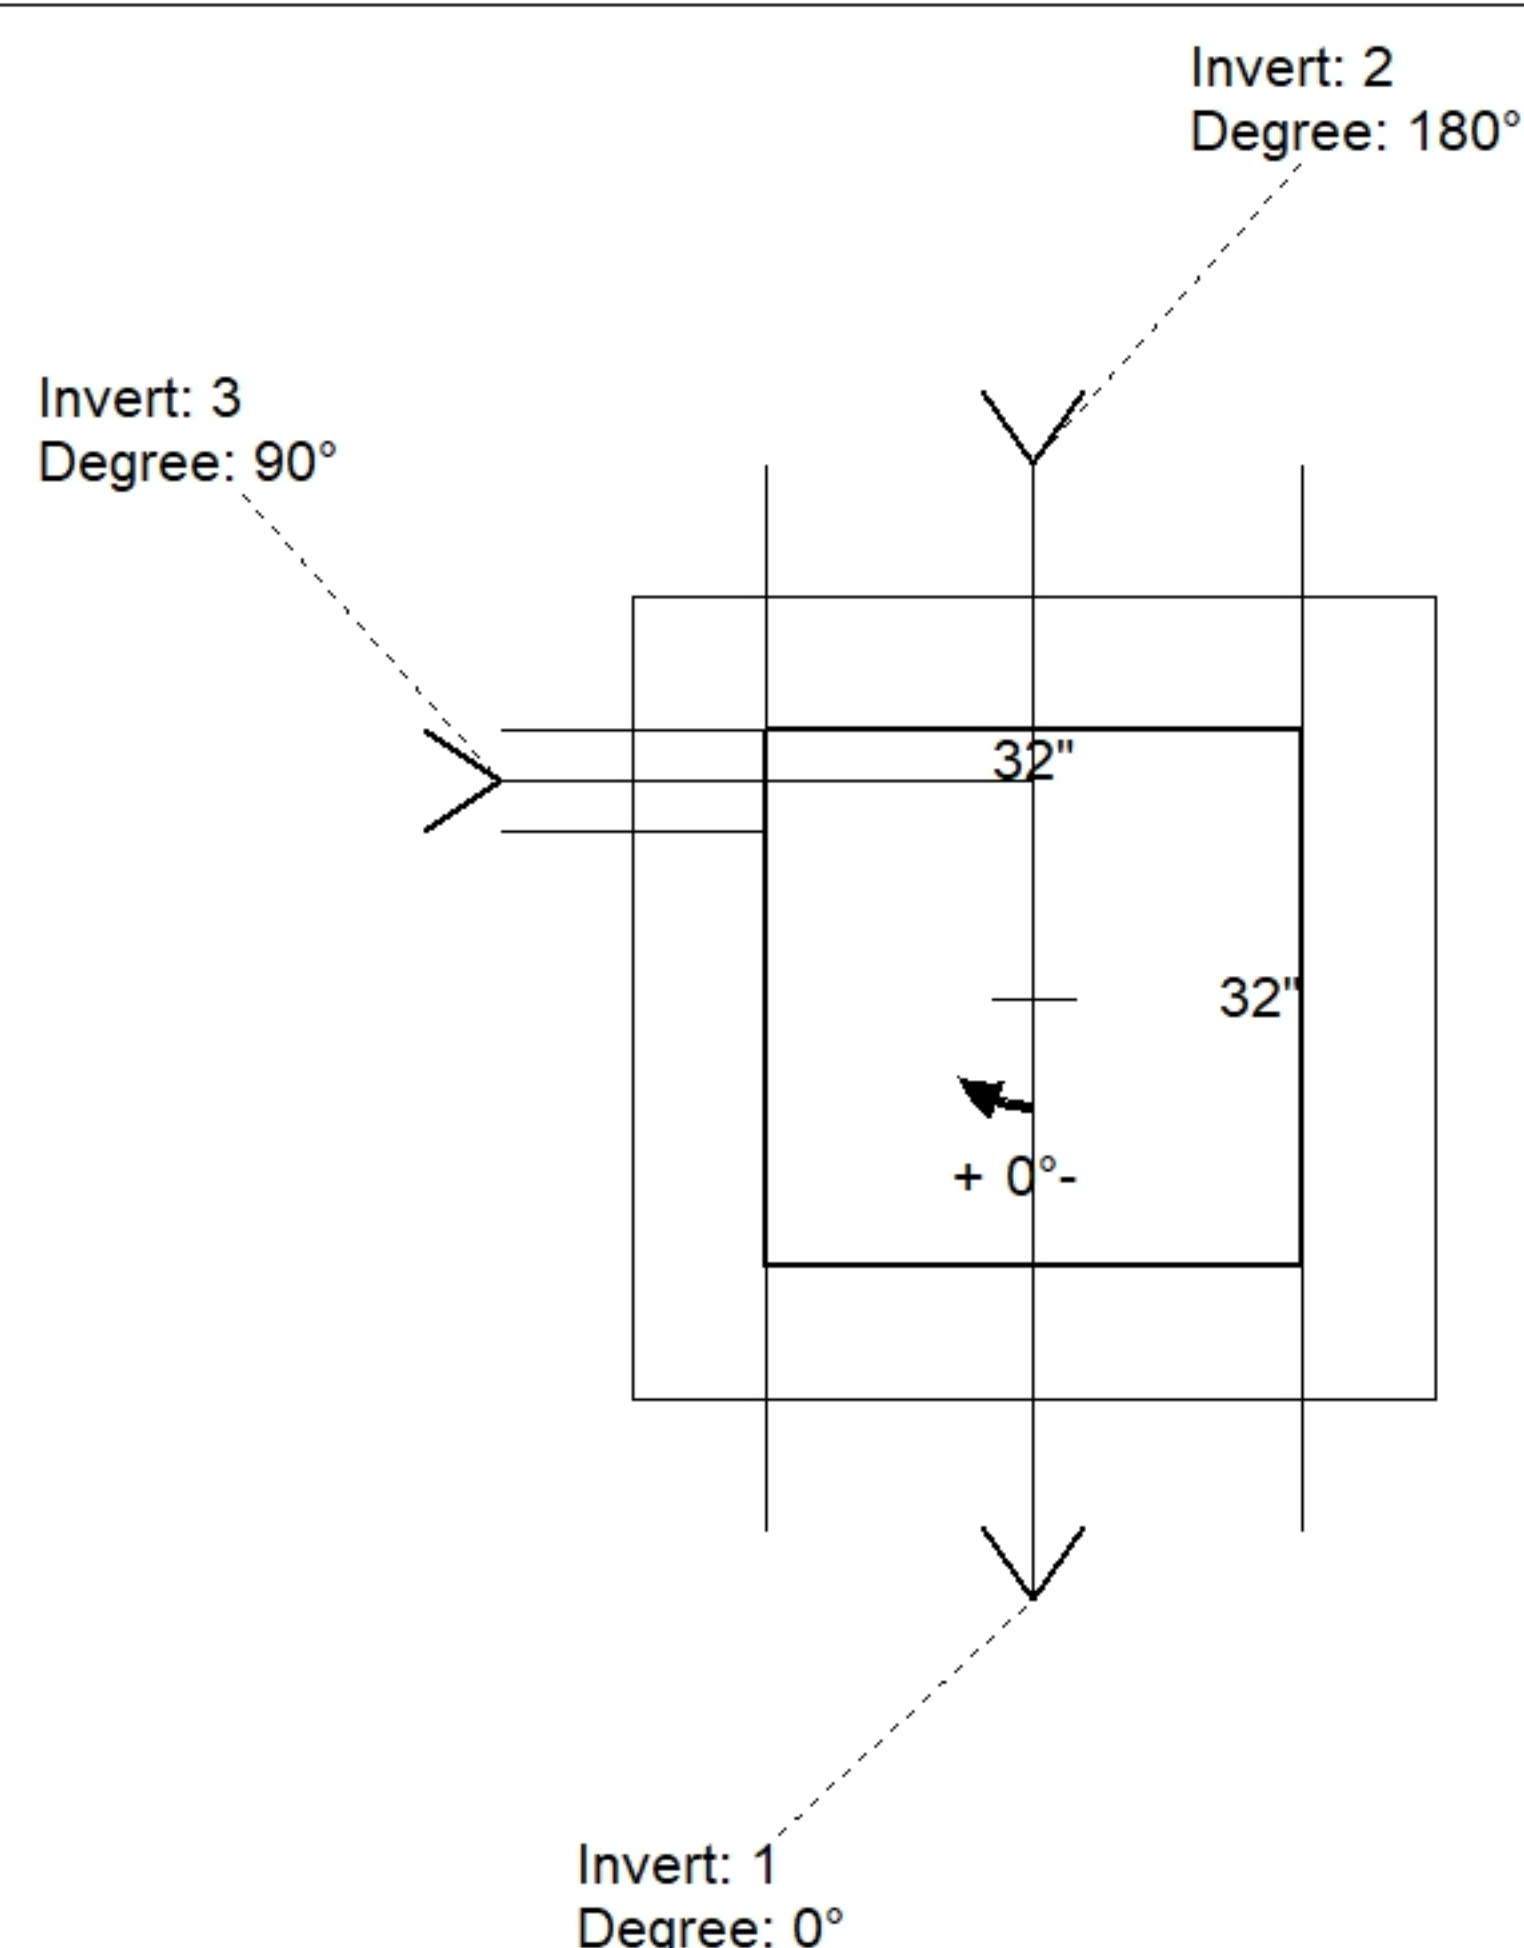

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	802.79'							
Reducer								
Invert 1	798.44'	0°	24" RCP B WALL	30"	32"	Hole 32	0"	P1
Invert 2	798.49'	180°	24" RCP B WALL	30"	32"	Hole 32	0.6"	P1
Invert 3	800.29'	90°	4" HDPE (perf pipe)	4.8"	6"	Hole 6	24.8"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

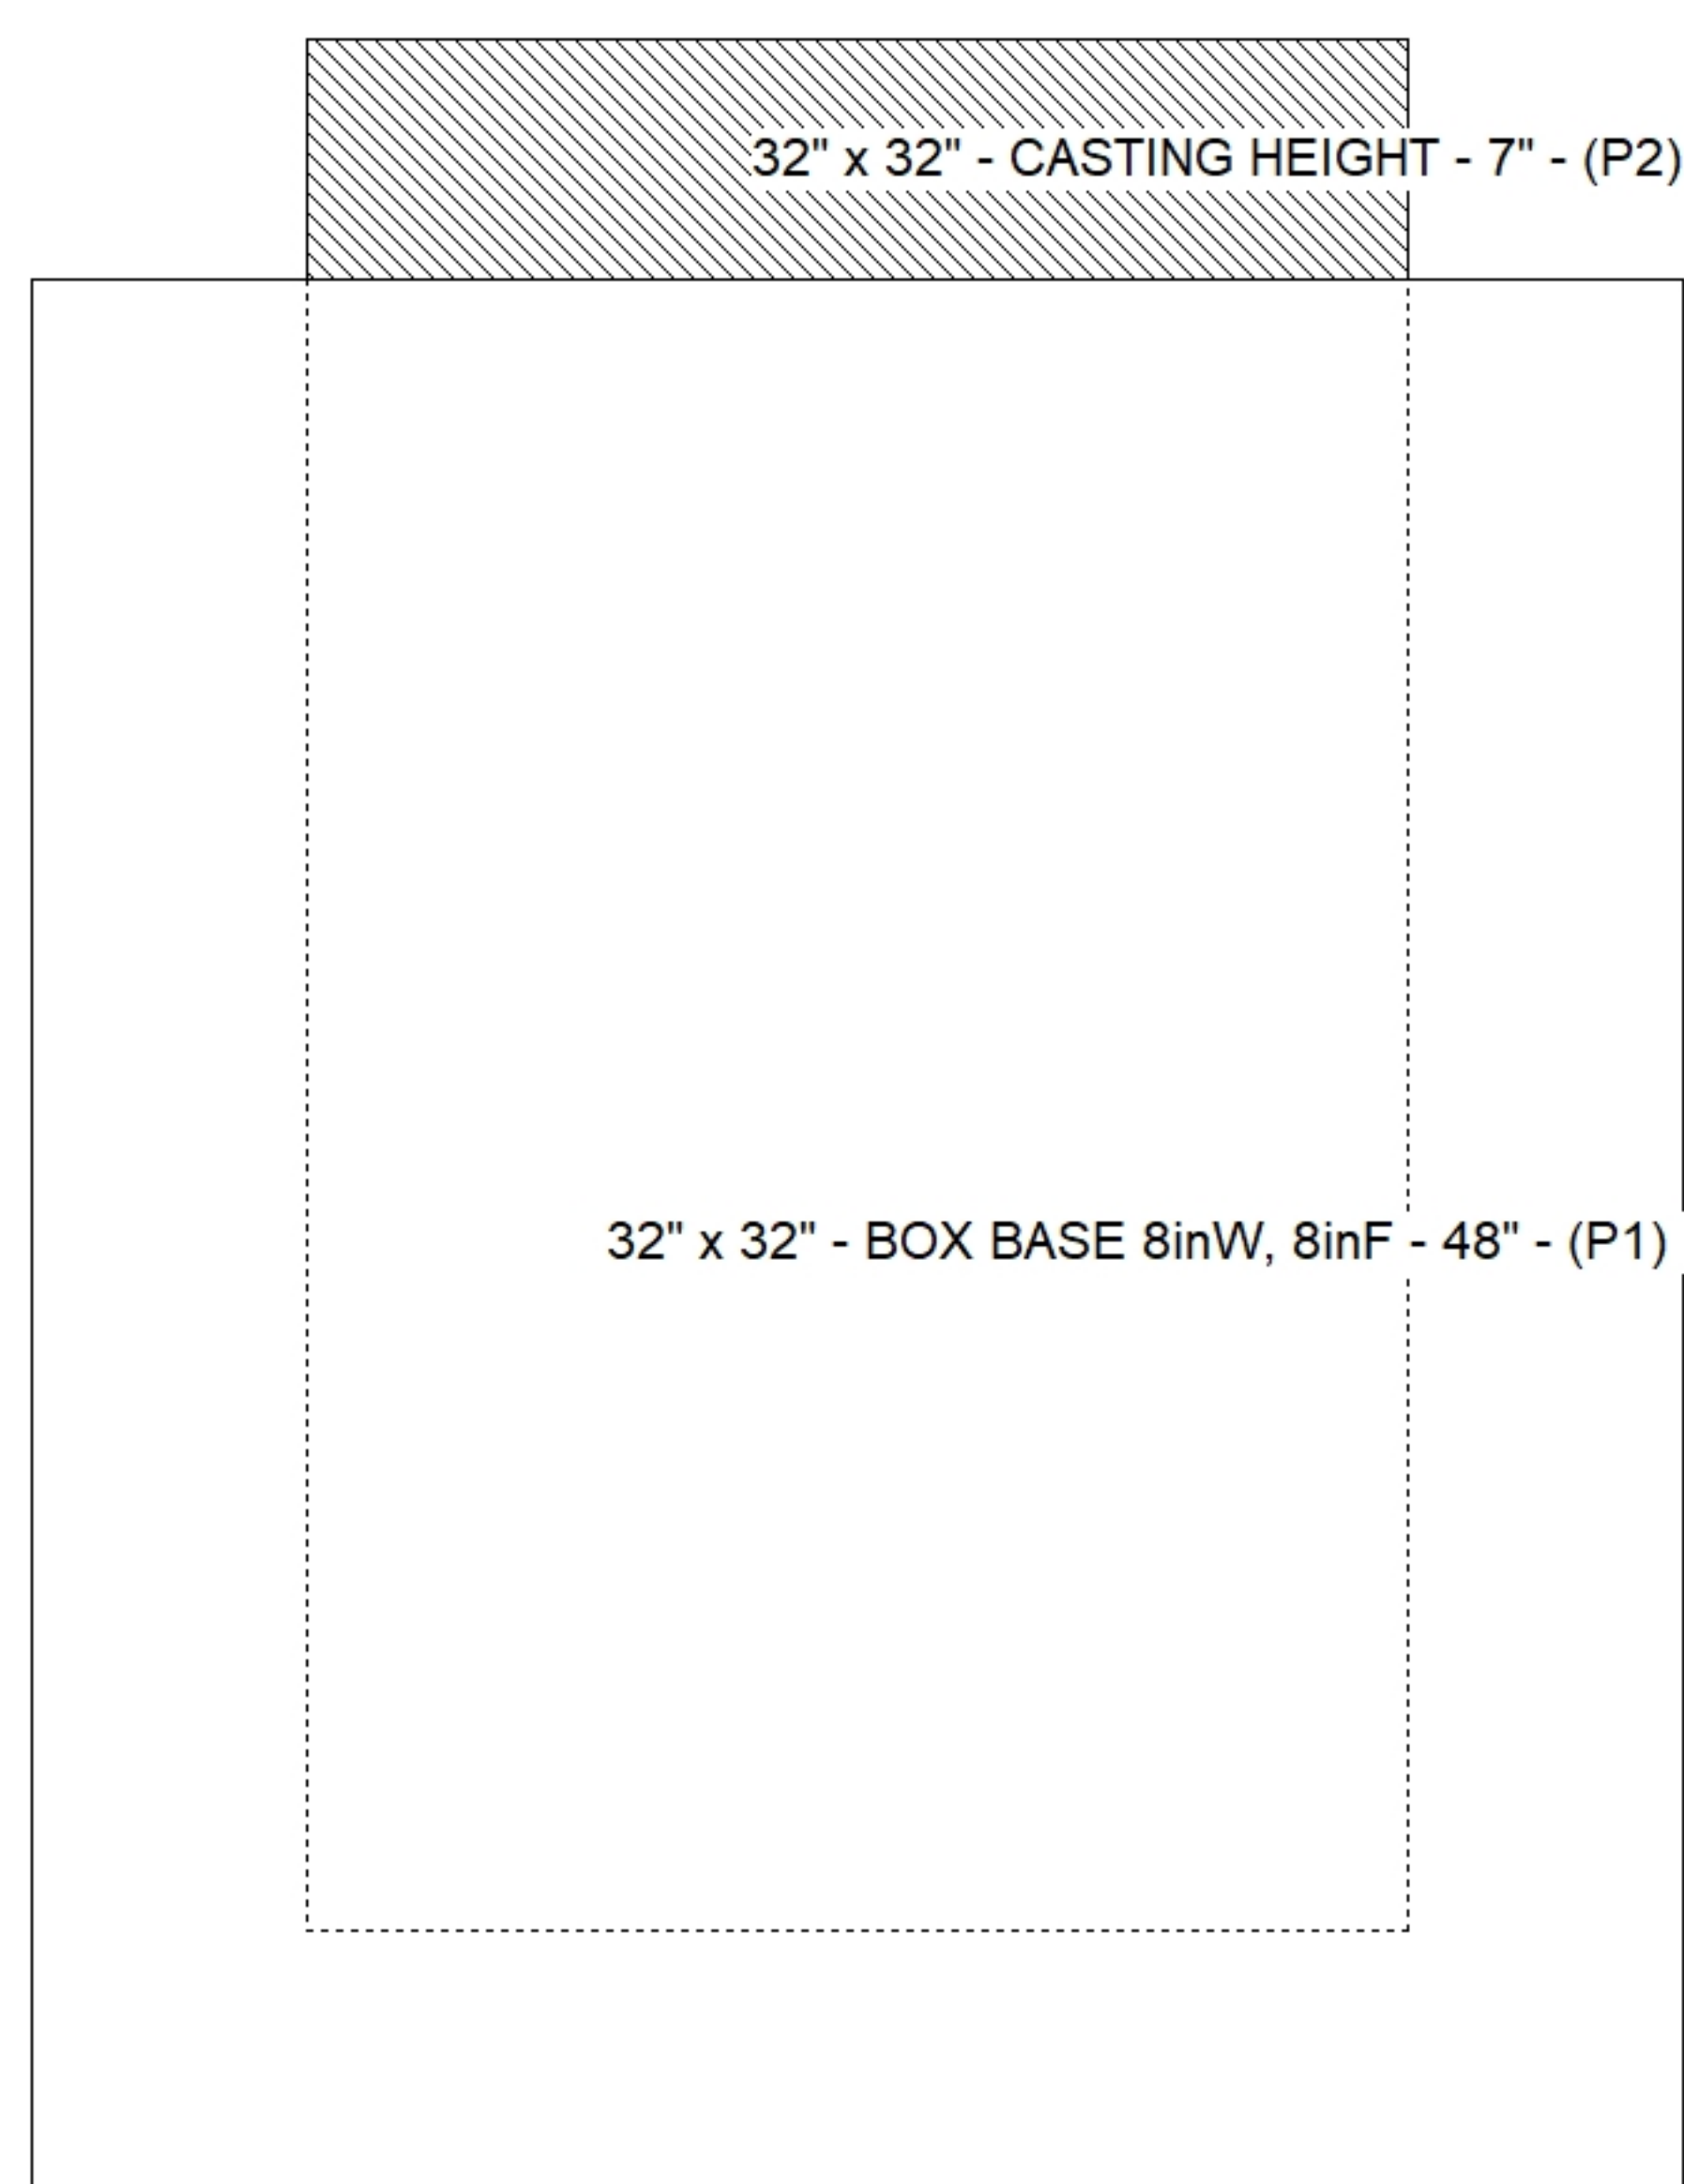

(P1)

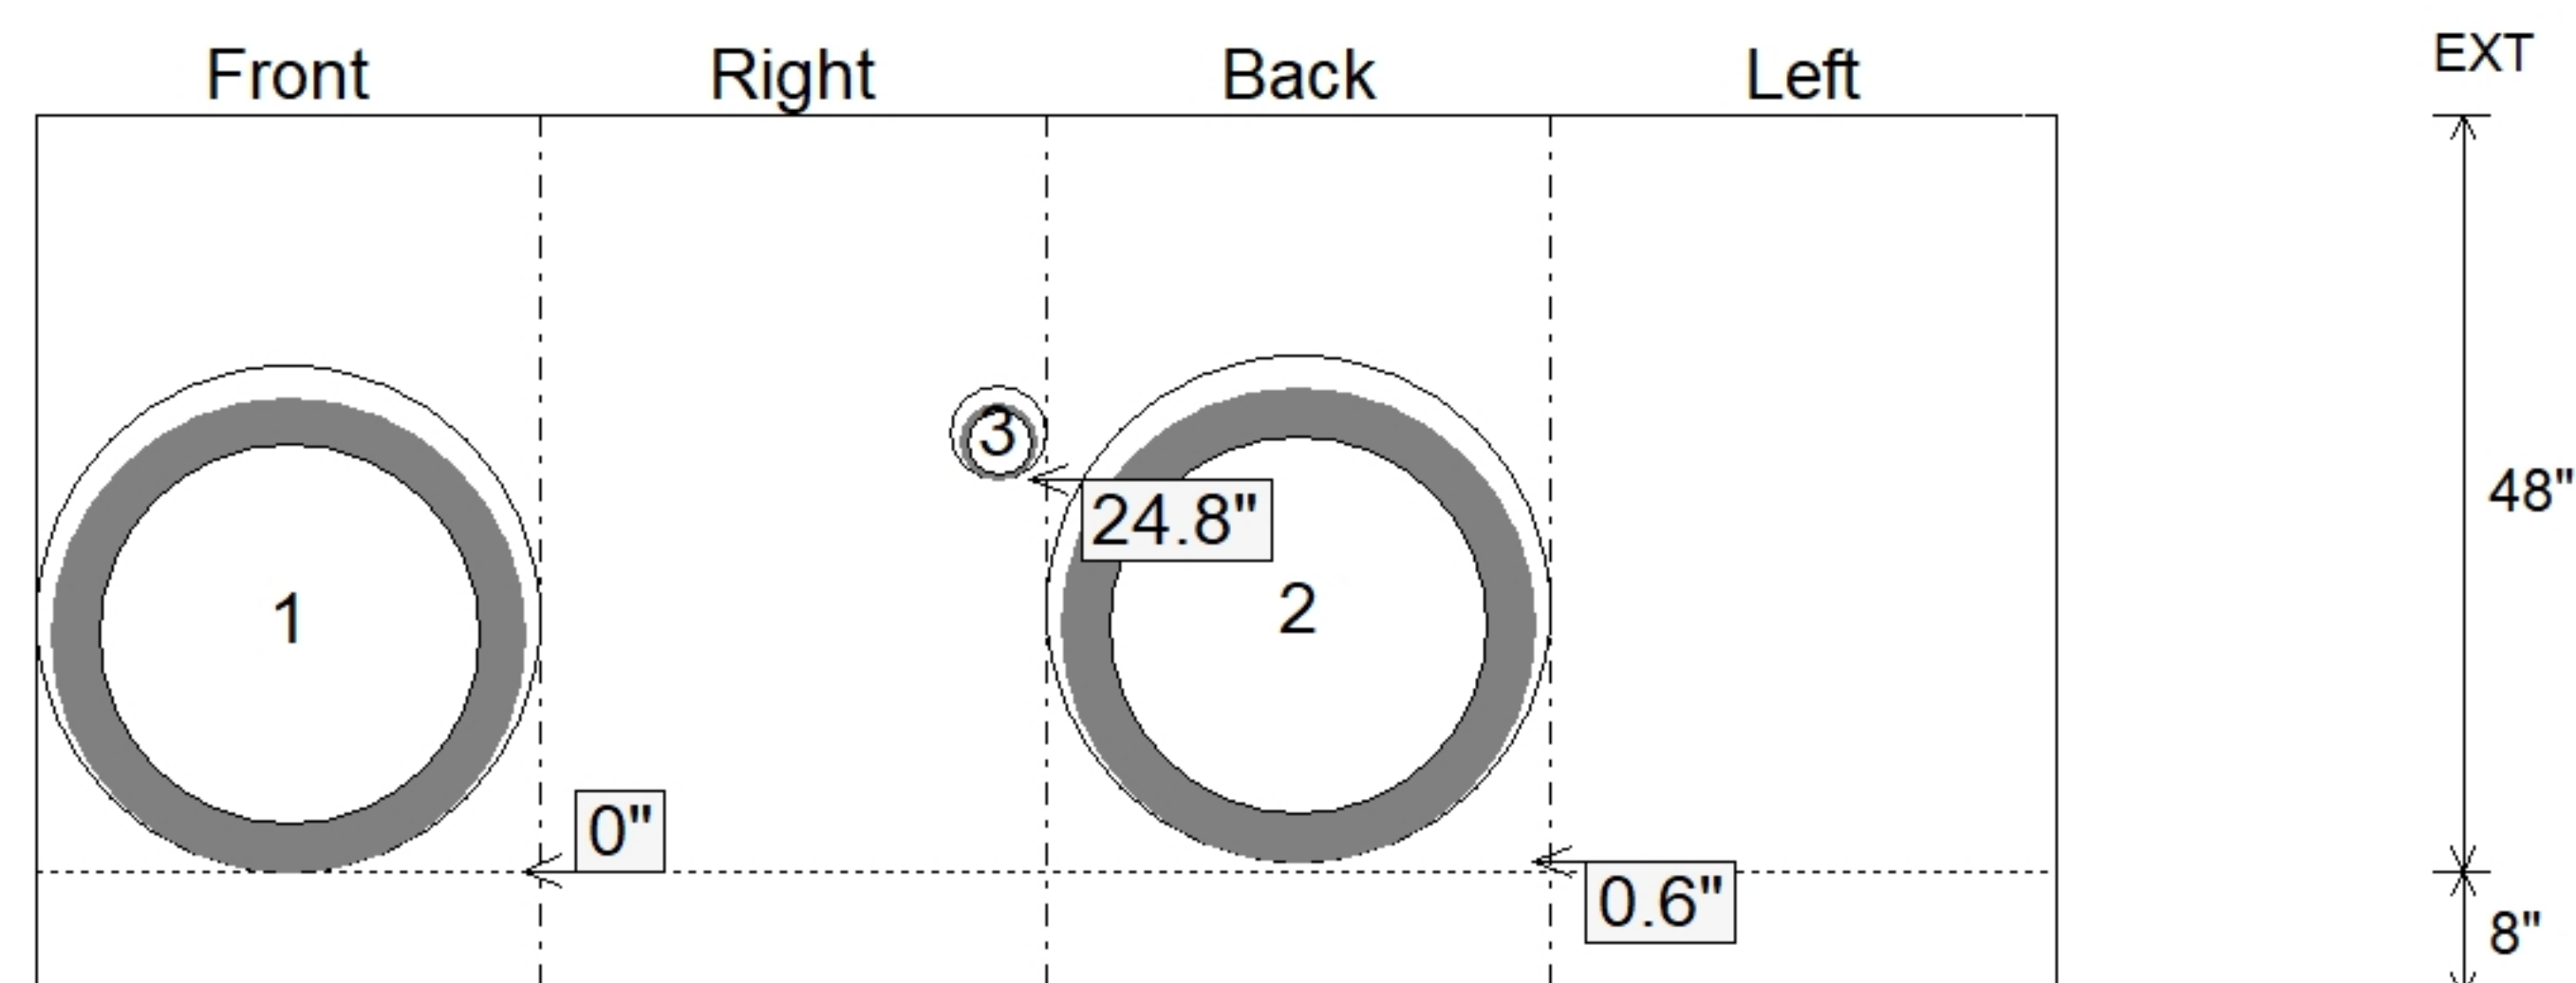

SUBMITTAL
APPROVED BY:
