

Job Name: 25-3062 Portland Bypass
Job Location: Portland, TN
Contractor: Scotty's Contracting & Stone, LLC

Plant: Beaver Dam
6/1/2026 8:24:17 AM

Tech: J. Coppage
PC: C. Goff



Structure ID: CB-31

P3 MH072LD10SP



MH FLAT TOP - TDOT NO 12 (28"x34" Hole)

- P4) 28" x 34" - CASTING HEIGHT - 7"
P3) 72" - MH FLAT TOP - TDOT NO 12 (28"x34" Hole) - 10"
P2) 72" - MH RISER SPECIAL/CUST. HT - 26"
P1) 72" - MH BASE - 72"
1) CASTING - JBS-3123 MODIFIED SET
2) 72" - Conseal CS-102 1.00"
1) 28" x 34" - Conseal CS-102 1.00"
2) Hole - 54
1) Hole - 6

0 lb	Structure Notes:
4406 lb	1. PER TDOT D-CB-12RB / ASTM C478 SPEC'S.
3774 lb	2. CONCRETE = 4,000 PSI AT 28 DAYS.
11420 lb	3. JBS 3123 MOD SINGLE SET BY ICAST
250 lb	4. REINFORCING PER ASTM A615 (GRADE 60).
0 lb	** PER TDOT STD DRAWING D-CB-12RB **
0 lb	- TOP SLAB - DBL MAT #5 BARS.
0 lb	- RISER (As .18)
0 lb	- FLOOR (As .62) #5 BARS AT 6" C.C.E.W.
Structure Total: 19850 lb	

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: PER TDOT DRAWING D-CB-12RA OR D-RL-1 FOR WWM OPTION.

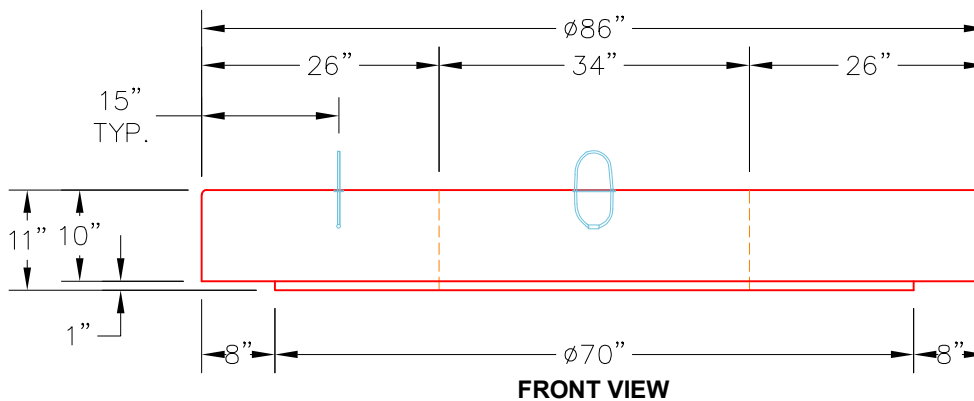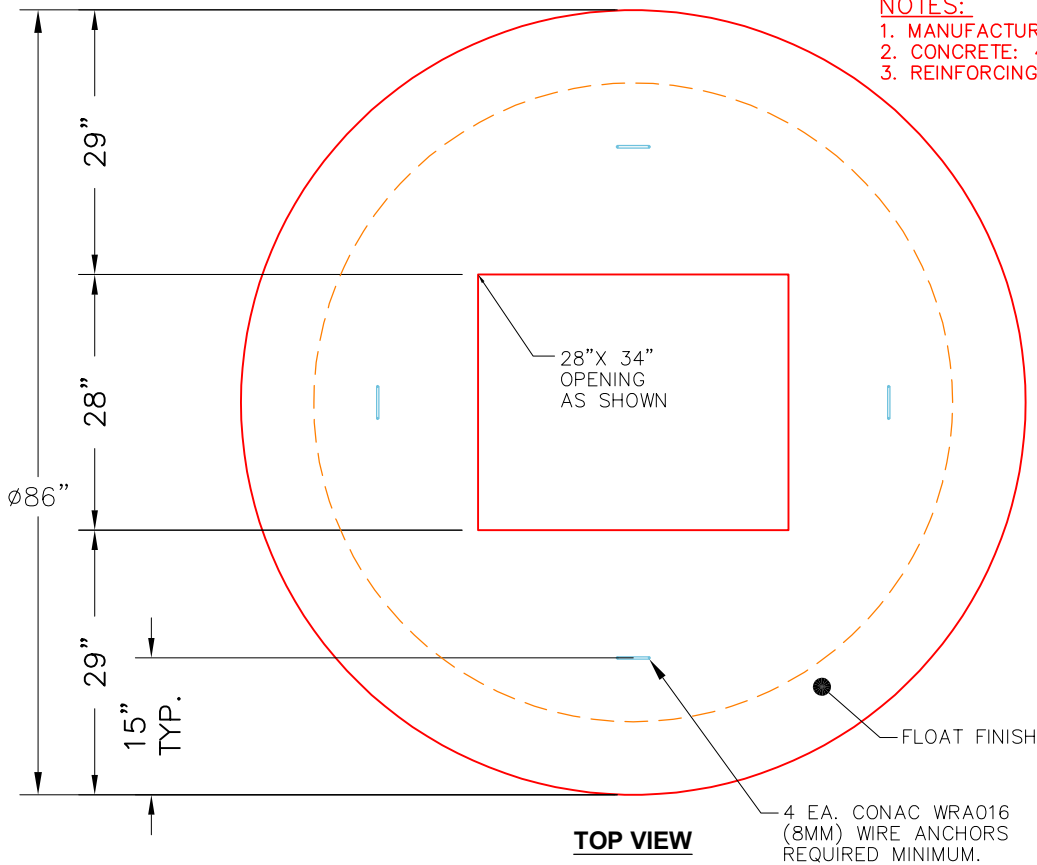

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 7"

Height (Ext): 10"

Weight (Net): 4406 lb
Volume (Net): 1.12cu.yd
