

Job Name: 25-3062 Portland Bypass
Job Location: Portland, TN
Contractor: Scotty's Contracting & Stone, LLC

Plant: Beaver Dam
6/1/2026 8:24:52 AM

Tech: J. Coppage
PC: C. Goff



Structure ID: CB-33

P2 MH060RS36S

MH RISER NO STEPS

P4) 28" x 34" - CASTING HEIGHT - 7"
P3) 60" - MH FLAT TOP - TDOT NO 12 (28"x34" Hole) - 10"
P2) 60" - MH RISER NO STEPS - 36"
P1) 60" - MH BASE Custom Ht - 70"
1) CASTING - JBS-3123 MODIFIED SET
2) 60" - Conseal CS-102 1.00"
1) 28" x 34" - Conseal CS-102 1.00"
2) Hole - 40
1) Hole - 6


Structure Notes:
1. PER TDOT D-CB-12RB / ASTM C478 SPEC'S.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. JBS 3123 MOD SINGLE SET BY ICAST
4. REINFORCING PER ASTM A615 (GRADE 60).
** PER TDOT STD DRAWING D-CB-12RB **
- TOP SLAB - DBL MAT #5 BARS.
- RISER (As .18)
- FLOOR (As .62) #5 BARS AT 6" C.C.E.W.

Structure Total: 16088 lb


Rim: 815.01' Rim to Invert: 9.99' Slack: 0.38" Sump: 3.5" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (⌋)	Offset
Invert 1										
Invert 2										
Invert 3	812.01'	90°	56.549"	4" HDPE (perf pipe)	4.8"	Hole 6	6"	6.01"	12.23"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

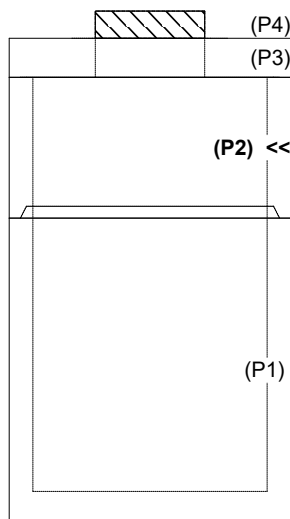

Invert: 3
Degree: 90°
Horz: 47.124"
Hole: 6"
Up(⌋): 12.23"



INSIDE WALL DIMENSIONS



Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 6"
Floor Height: 0"

Height (Int): 36"
Height (Ext): 36"

Weight (Net): 3744 lb
Volume (Net): 0.96cu.yd
