

Job Name: 25-3062 Portland Bypass
Job Location: Portland, TN
Contractor: Scotty's Contracting & Stone, LLC

Plant: Beaver Dam
6/1/2026 8:24:17 AM

Tech: J. Coppage
PC: C. Goff




Structure ID: CB-33

P3 MH060LD10SP

MH FLAT TOP - TDOT NO 12 (28"x34" Hole)

- P4) 28" x 34" - CASTING HEIGHT - 7"
P3) 60" - MH FLAT TOP - TDOT NO 12 (28"x34" Hole) - 10"
P2) 60" - MH RISER NO STEPS - 36"
P1) 60" - MH BASE Custom Ht - 70"
1) CASTING - JBS-3123 MODIFIED SET
2) 60" - Conseal CS-102 1.00"
1) 28" x 34" - Conseal CS-102 1.00"
2) Hole - 40
1) Hole - 6

0 lb	Structure Notes:
3417 lb	1. PER TDOT D-CB-12RB / ASTM C478 SPEC'S.
3744 lb	2. CONCRETE = 4,000 PSI AT 28 DAYS.
8677 lb	3. JBS 3123 MOD SINGLE SET BY ICAST
250 lb	4. REINFORCING PER ASTM A615 (GRADE 60).
0 lb	** PER TDOT STD DRAWING D-CB-12RB **
0 lb	- TOP SLAB - DBL MAT #5 BARS.
0 lb	- RISER (As .18)
0 lb	- FLOOR (As .62) #5 BARS AT 6" C.C.E.W.
Structure Total: 16088 lb	

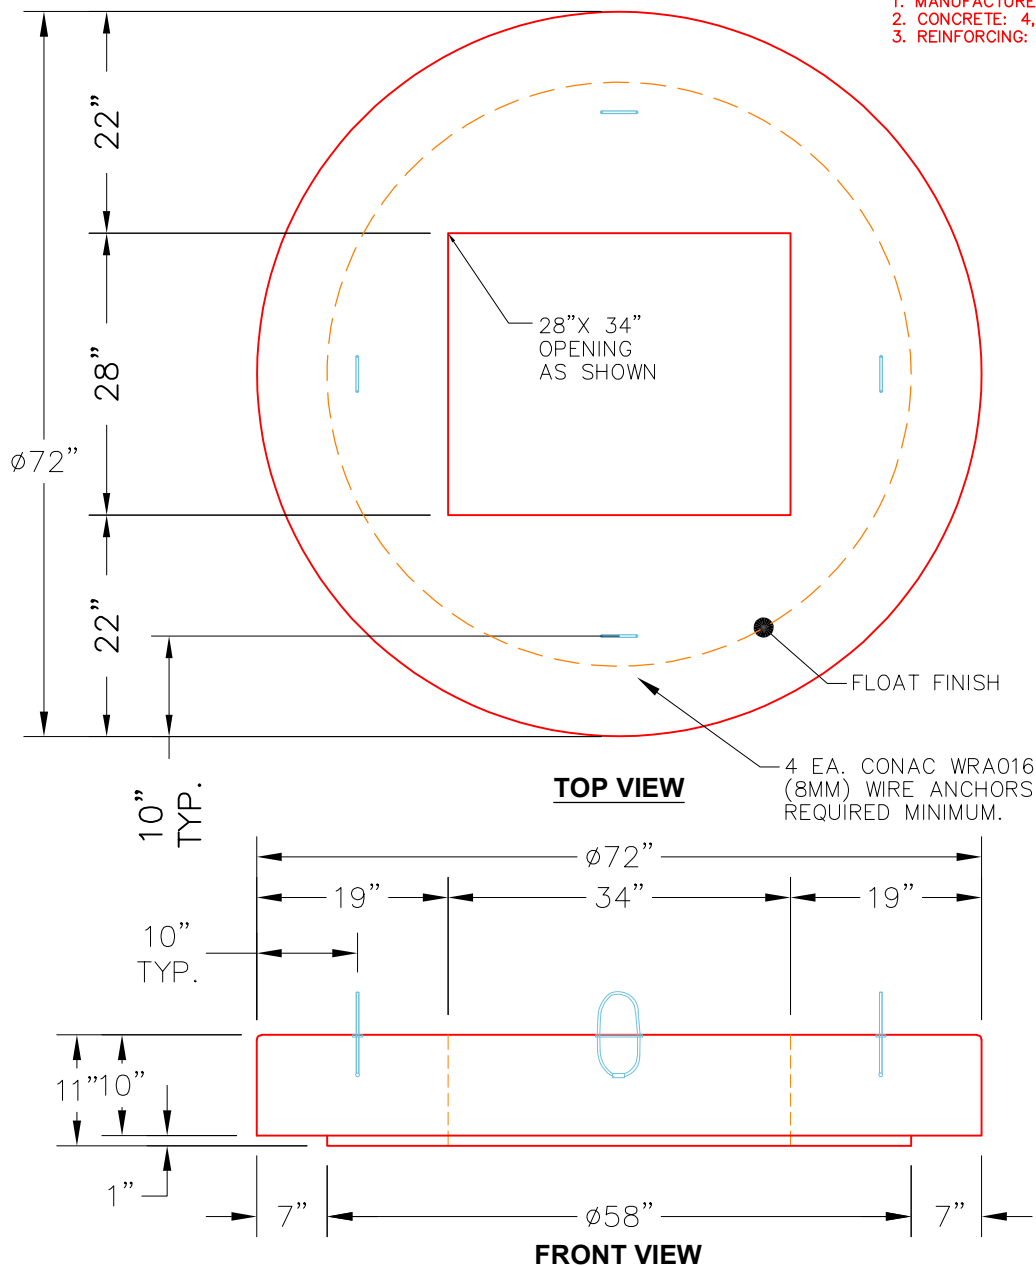

- NOTES:**
1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
 2. CONCRETE: 4,000 PSI AT 28 DAYS.
 3. REINFORCING: PER TDOT DRAWING D-CB-12RA OR D-RL-1 FOR WWM OPTION.

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 6"

Height (Ext): 10"

Weight (Net): 3417 lb
Volume (Net): 0.87cu.yd
