


Structure Notes: 1. PER TDOT D-CB-12LP / ASTM C913 SPEC'S.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. JBS 3123 MOD SINGLE SET BY ICAST
4. REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB - DBL MAT #5 BARS.
PER TDOT STD DRAWING D-CB-12LP.
- WALLS (As .62) #5 BARS AT 6" C.C.E.W.
- FLOOR (As .62) #5 BARS AT 6" C.C.E.W.

P2) 32" x 32" - CASTING HEIGHT - 7"
P1) 32" x 32" - BOX BASE 8inW, 8inF, Variable Ht - 35"
1) CASTING - JBS-3123 MODIFIED SET
1) 32" x 32" - Conseal CS-102 1.00"
1) Hole - 26
1) Hole - 6


0 lb
4935 lb
250 lb
0 lb
0 lb
0 lb

Structure Total: 5185 lb

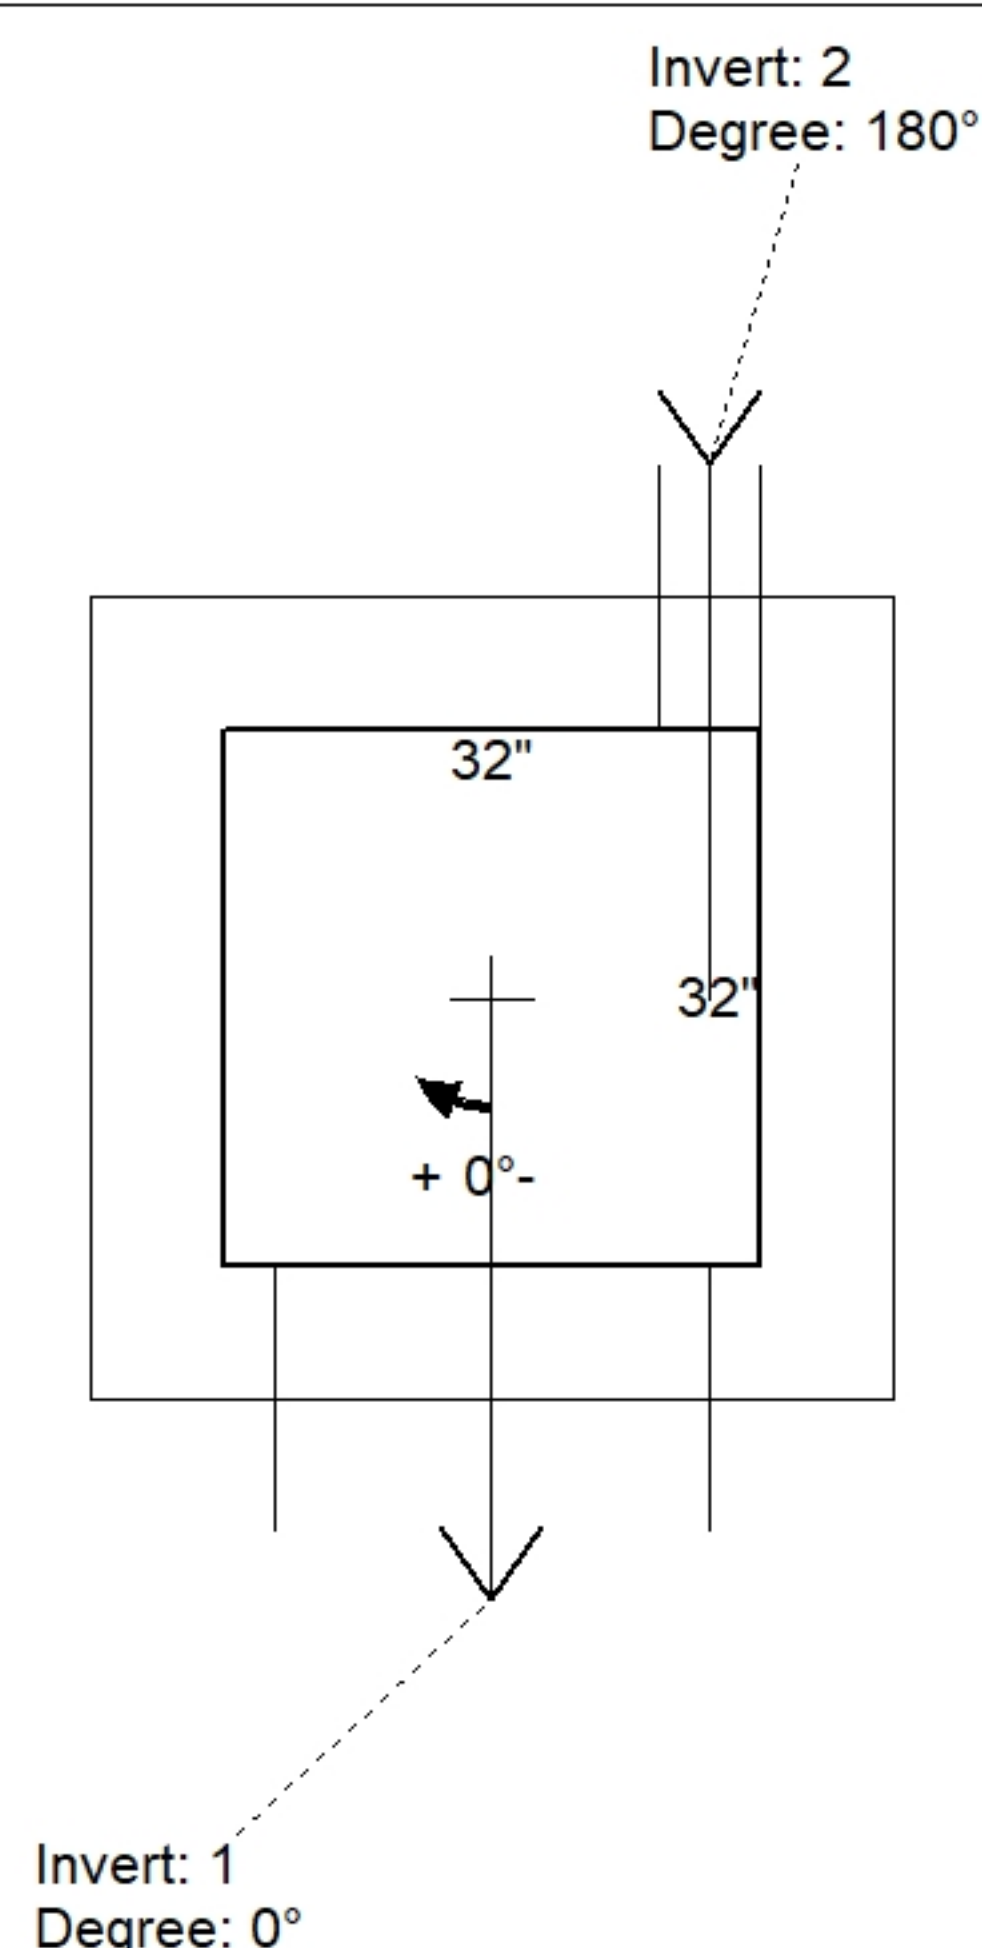

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	811.43'							
Reducer								
Invert 1	808.11'	0°	18" RCP B WALL	23"	26"	Hole 26	0"	P1
Invert 2	808.93'	180°	4" HDPE (perf pipe)	4.8"	6"	Hole 6	11.94"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

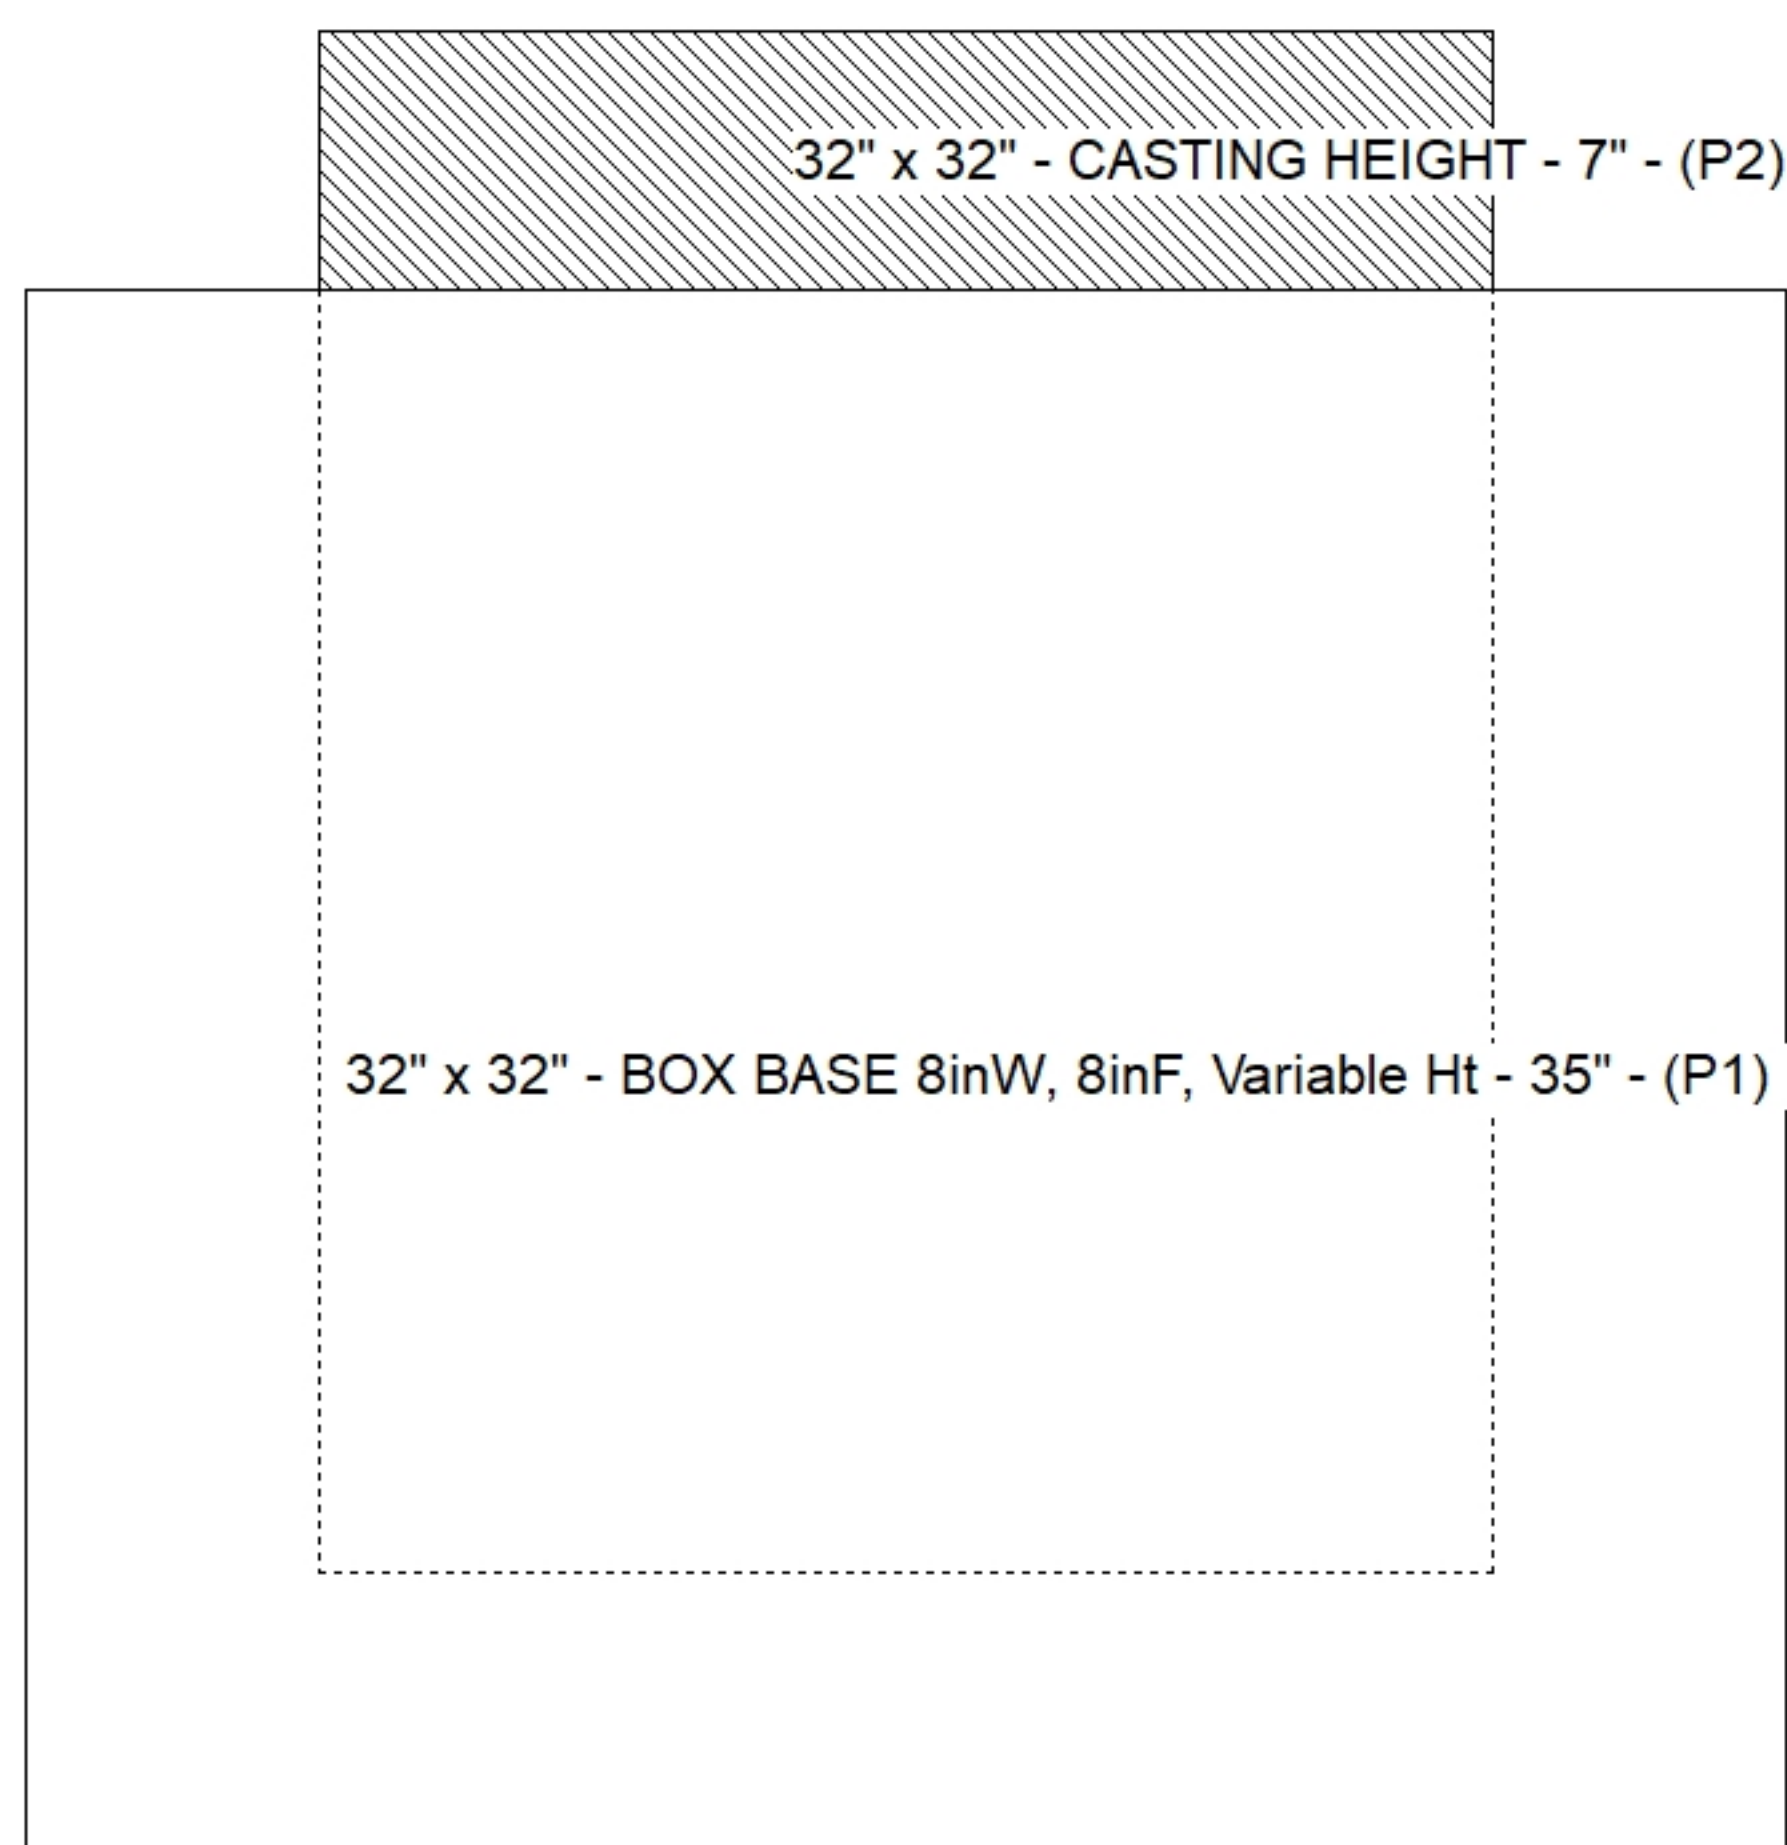

SUBMITTAL
APPROVED BY:
