
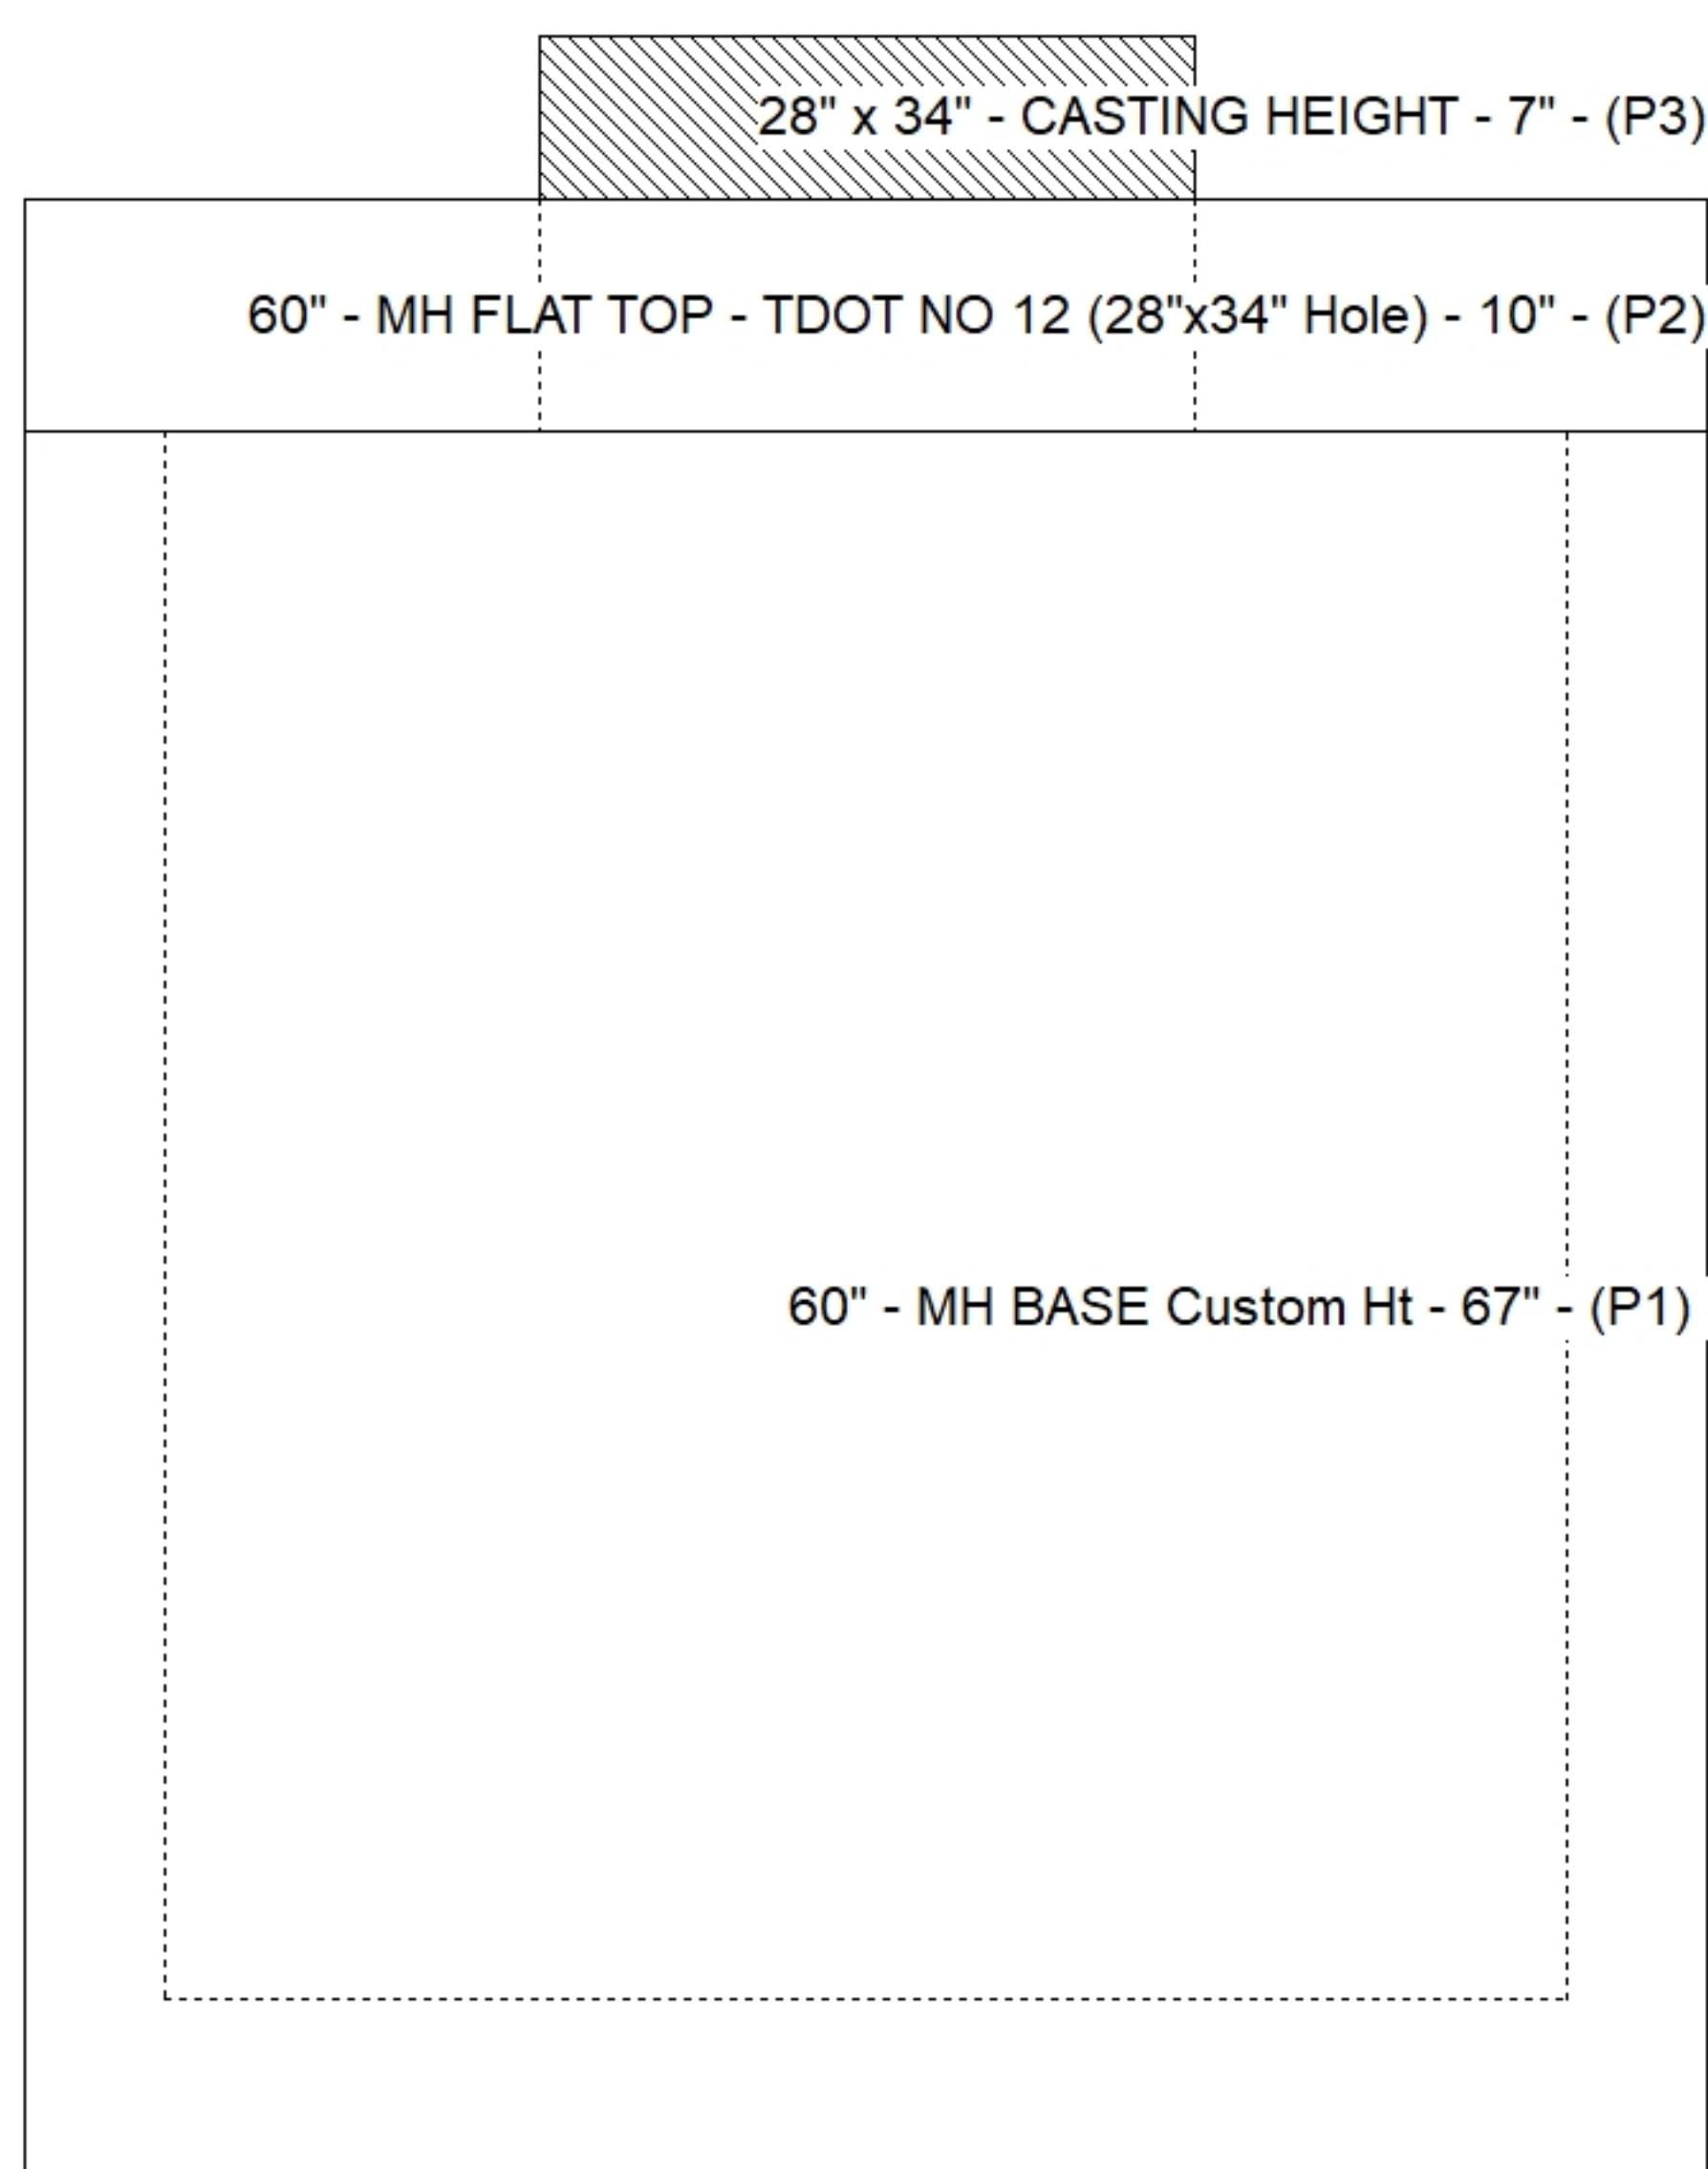


Structure Notes: 1. PER TDOT D-CB-12RB / ASTM C478 SPEC'S.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. JBS 3123 MOD SINGLE SET BY ICAST
4. REINFORCING PER ASTM A615 (GRADE 60).
** PER TDOT STD DRAWING D-CB-12RB **
- TOP SLAB - DBL MAT #5 BARS.
- RISER (As .18)
- FLOOR (As .62) #5 BARS AT 6" C.C.E.W.

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	796.4'							
Reducer								
Invert 1	789.64'	0°	30" RCP B WALL	37"	40"	Hole 40	0"	P1
Invert 2	789.64'	180°	30" RCP B WALL	37"	40"	Hole 40	0"	P1
Invert 3	793.4'	180°	4" HDPE (perf pipe)	4.8"	6"	Hole 6	48.22"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

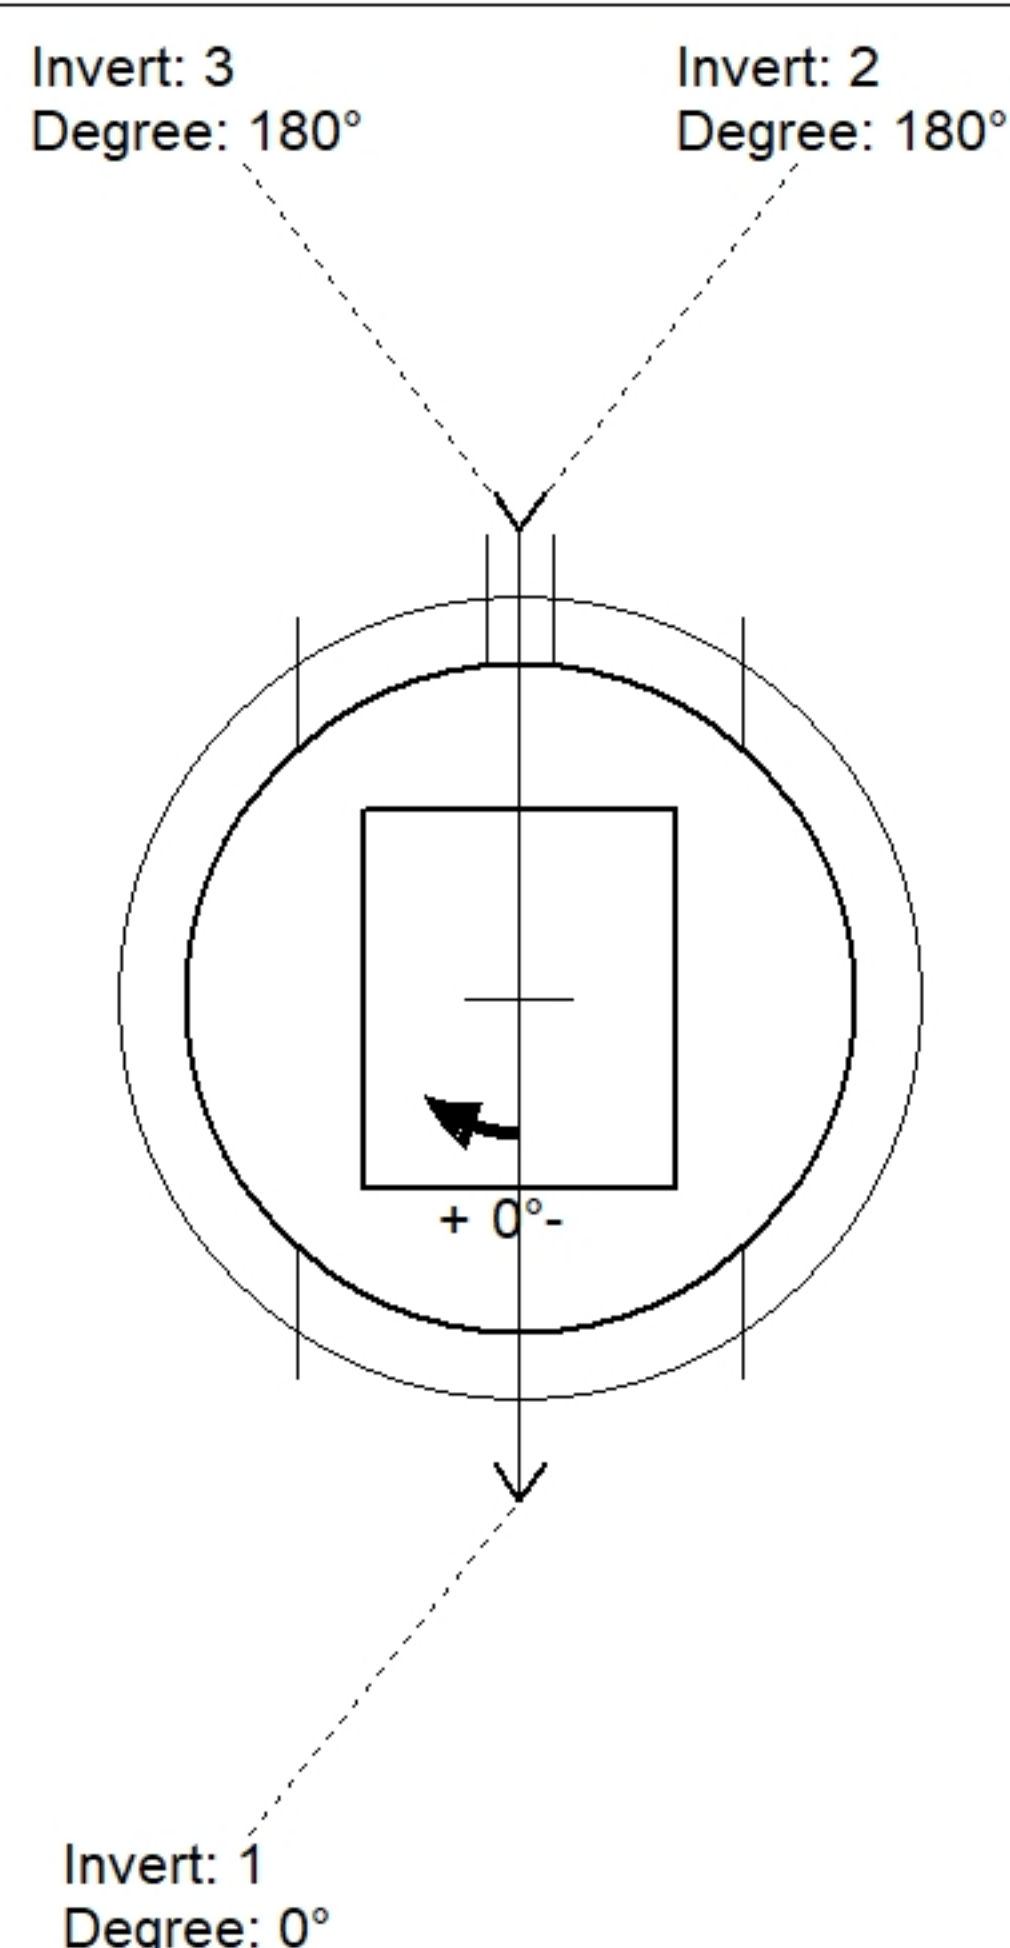

SUBMITTAL
APPROVED BY:
