

Job Name: 25-3062 Portland Bypass
Job Location: Portland, TN
Contractor: Scotty's Contracting & Stone, LLC

Plant: Beaver Dam
6/1/2026 8:24:12 AM

Tech: J. Coppage
PC: C. Goff



Structure ID: CB-9


P2 MH048LD10SP

MH FLAT TOP - TDOT NO 12 (28"x34" Hole)

- P3) 28" x 34" - CASTING HEIGHT - 7"
P2) 48" - MH FLAT TOP - TDOT NO 12 (28"x34" Hole) - 10"
P1) 48" - MH BASE Custom Ht - 40"
1) CASTING - JBS-3123 MODIFIED SET
1) 48" - Conseal CS-102 1.00"
1) 28" x 34" - Conseal CS-102 1.00"
1) Hole - 32
1) Hole - 26
1) Hole - 6


- 0 lb
1497 lb
3508 lb
250 lb
0 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 5255 lb
- Structure Notes:
1. PER TDOT D-CB-12RA / ASTM C478 SPEC'S.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. JBS 3123 MOD SINGLE SET BY ICAST
5. REINFORCING PER ASTM A615 (GRADE 60).
** PER TDOT STD DRAWING D-CB-12RA **
- TOP SLAB - DBL MAT #5 BARS.
- RISER (As .24)
- FLOOR (As .62) #5 BARS AT 6" C.C.E.W.

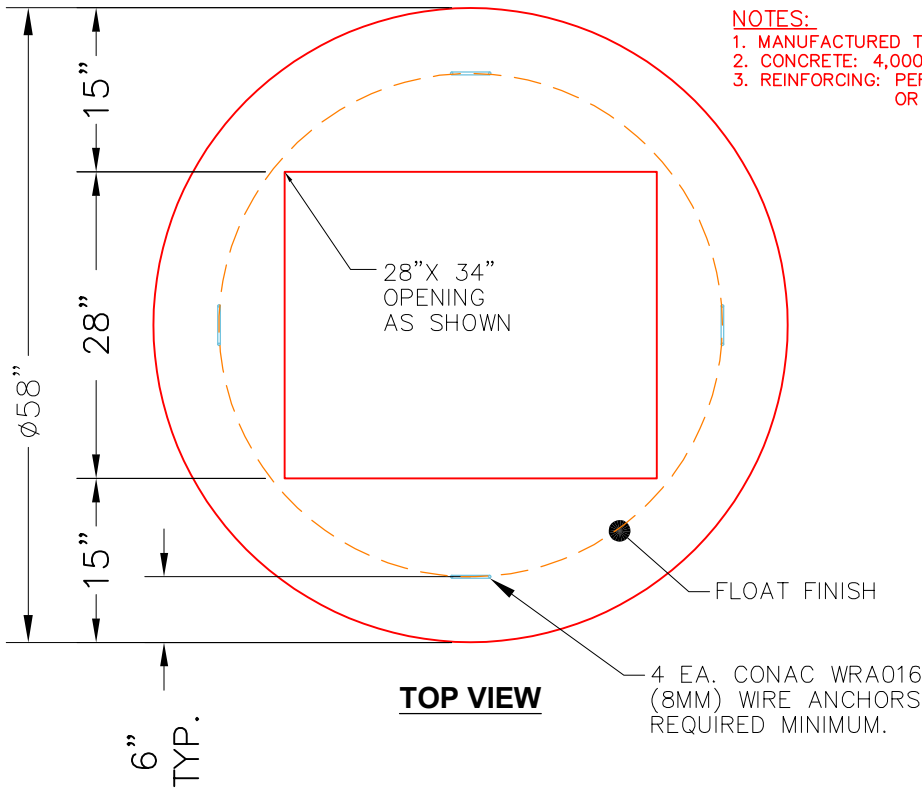

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: PER TDOT DRAWING D-CB-12RA
OR D-RL-1 FOR WWM OPTION.

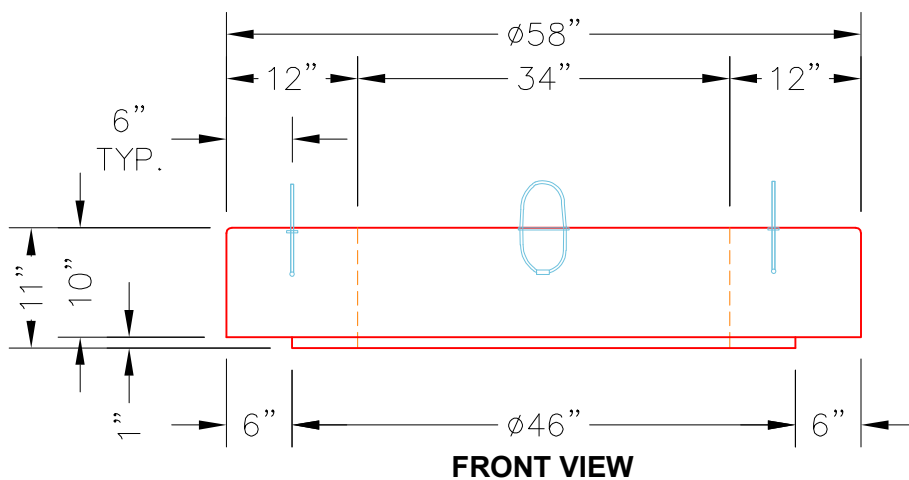

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 5"

Height (Ext): 10"

Weight (Net): 1497 lb
Volume (Net): 0.38cu.yd
