




Floor (Bot): 763.032'
Overall Height: 6.583'
Slack: 0.3"


Structure Total: 19139 lb

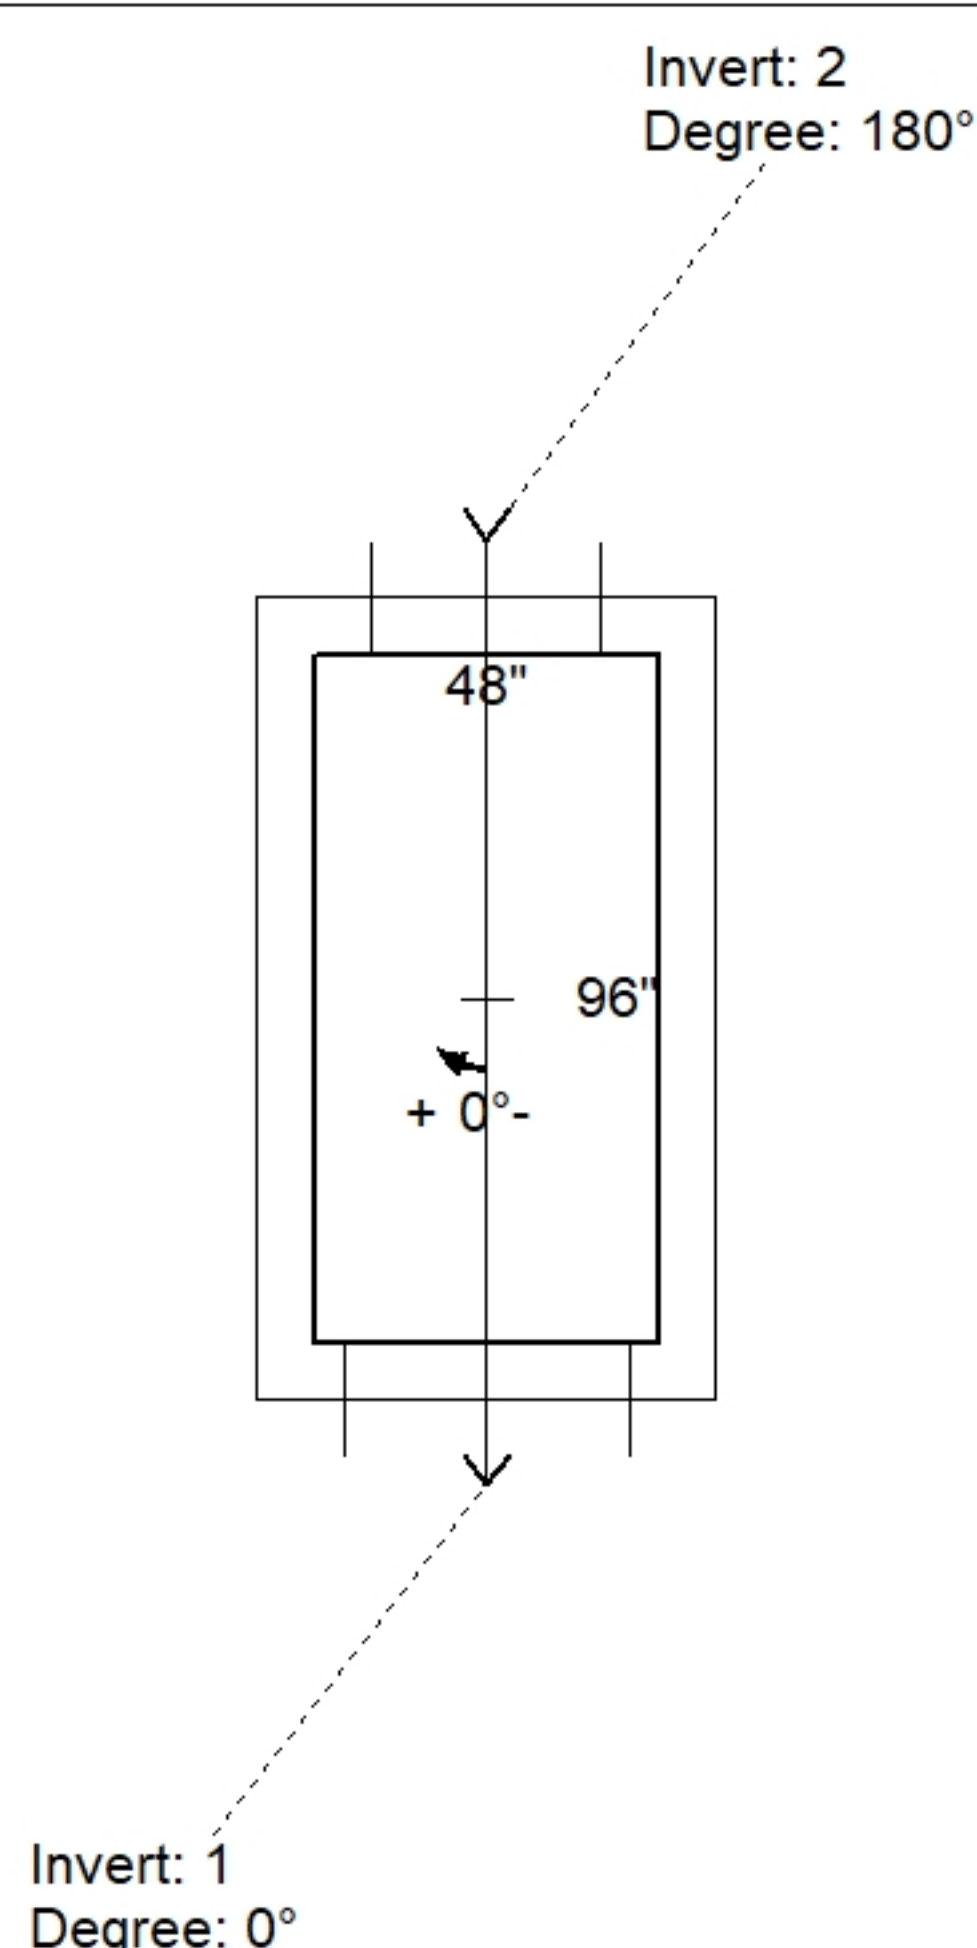

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	769.64'							
Reducer								
Invert 1	763.99'	0°	30" RCP B WALL	37"	40"	Hole 40	0"	P1
Invert 2	765.5'	180°	24" RCP B WALL	30"	32"	Hole 32	18.62"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

48" x 96" - CASTING HEIGHT - 0" - (P2)

48" x 96" - BOX BASE 8inW, 8inF, Variable Ht - 71" - (P1)

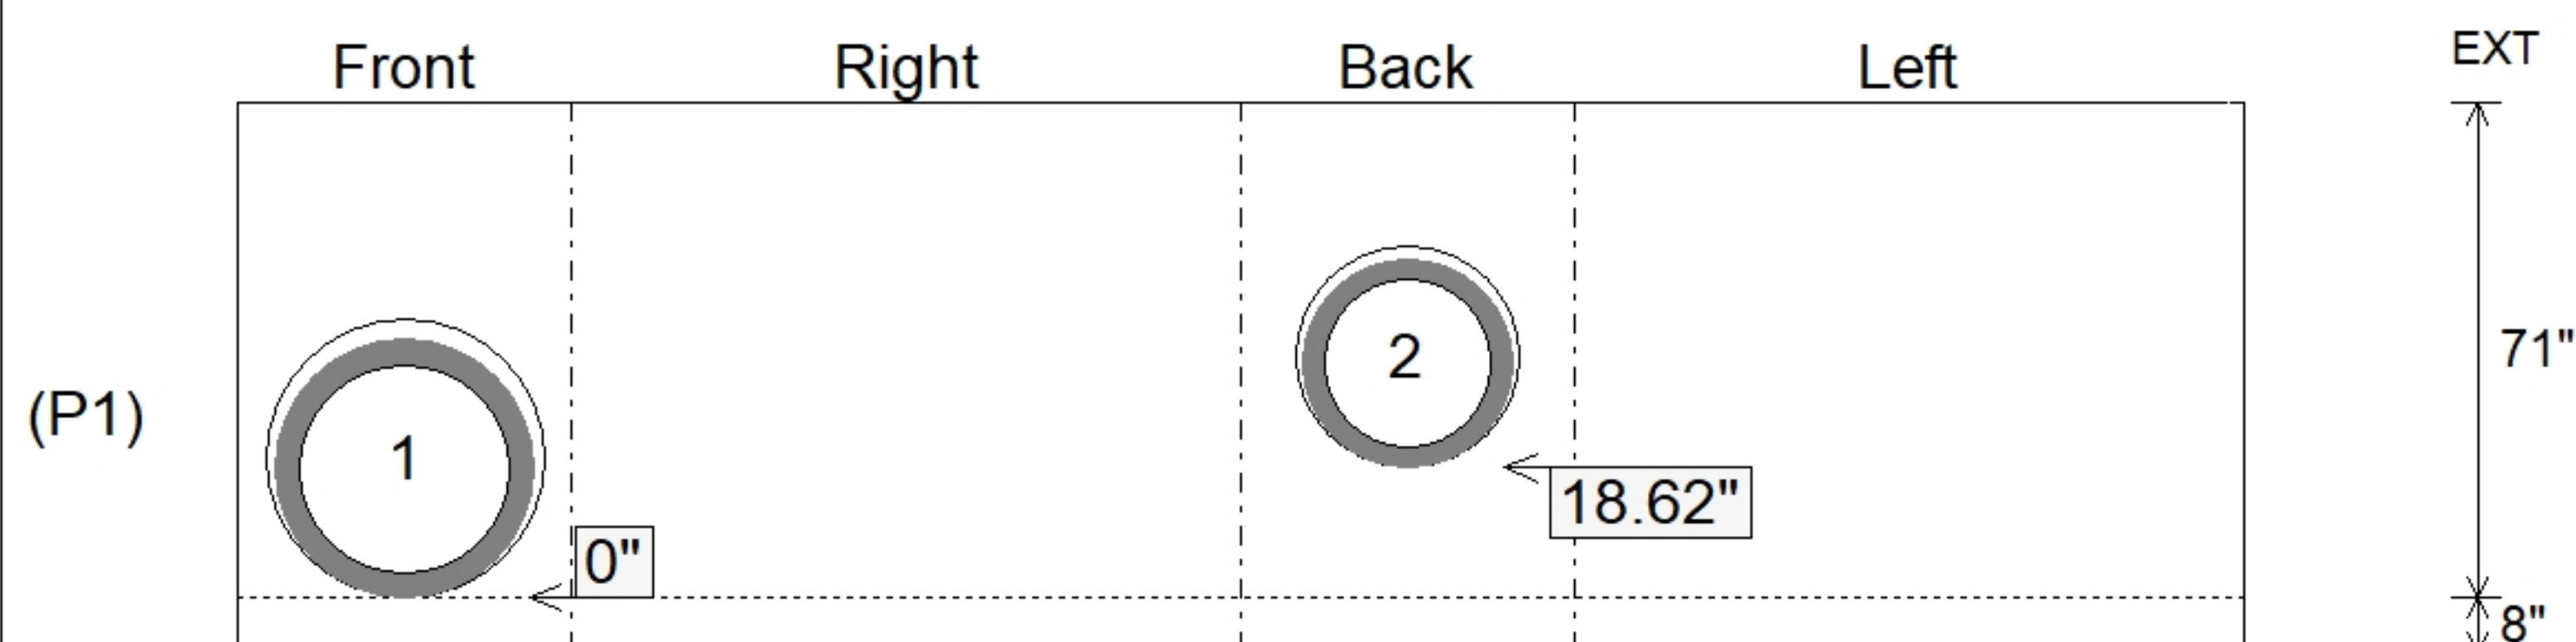

SUBMITTAL
APPROVED BY:
