

Job Name: 25-3062 Portland Bypass
Job Location: Portland, TN
Contractor: Scotty's Contracting & Stone, LLC

Plant: Beaver Dam
6/1/2026 8:23:22 AM

Tech: J. Coppage
PC: C. Goff



Structure ID: MD-8

P1 BX4848-08BAVF

BOX BASE 8inW, 8inF, Variable Ht

P2) 48" x 48" - CASTING HEIGHT - 0"
P1) 48" x 48" - BOX BASE 8inW, 8inF, Variable Ht - 38"
1) CASTING - JBS TYPE 39 TDOT GRATES (48" X 48")
1) Hole - 26

0 lb
8107 lb
459 lb
0 lb

Structure Total: 8566 lb


Structure Notes:
1. PER ASTM C913 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. JBS TDOT TYPE 39 BY ICAST
4. REINFORCING PER TDOT DRAWING D-CB-39S
ASTM A615 (GRADE 60).
5. PRODUCTION TO PLACE A 4.5" DEEP X 2" WIDE
RECESS IN THE TOP INSIDE OF THE 0 DEGREE
AND THE 180 DEGREE WALL OF THE BASE.

Rim: 816.45' Rim to Invert: 2.99' Slack: 0.38" Sump: 2.5" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	813.46'	90°	32"	18" RCP B WALL	23"	Hole 26	26"	26"	0"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)


UPSIDE-DOWN VIEW (int. dimensions)

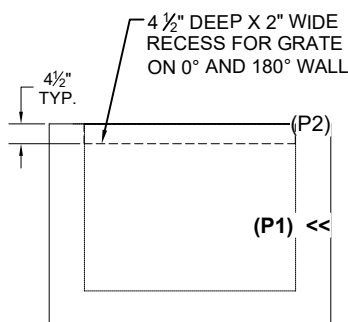

Invert: 1
Degree: 90°
Horz: 24"
Hole: 26"
Up(): 0"




4 1/2" DEEP X 2" WIDE
RECESS FOR GRATE
ON 0° AND 180° WALL



Invert: 1
Degree: 90°
Horz: 24"
Hole: 26"
Up(): 0"

INSIDE WALL DIMENSIONS

(P1)

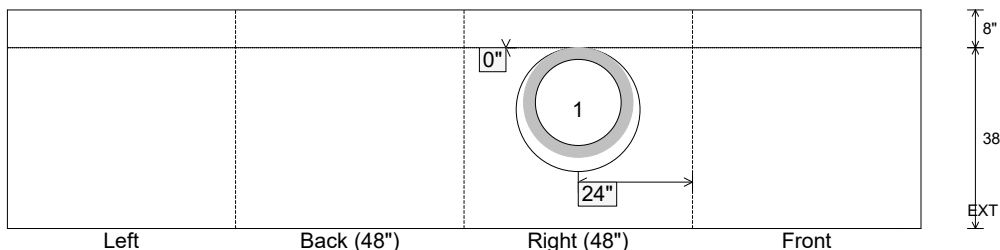

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: n/a

Wall Thickness: 8"
Floor Height: 8"

Height (Int): 38"
Height (Ext): 46"

Weight (Net): 8107 lb
Volume (Net): 2.07cu.yd
