



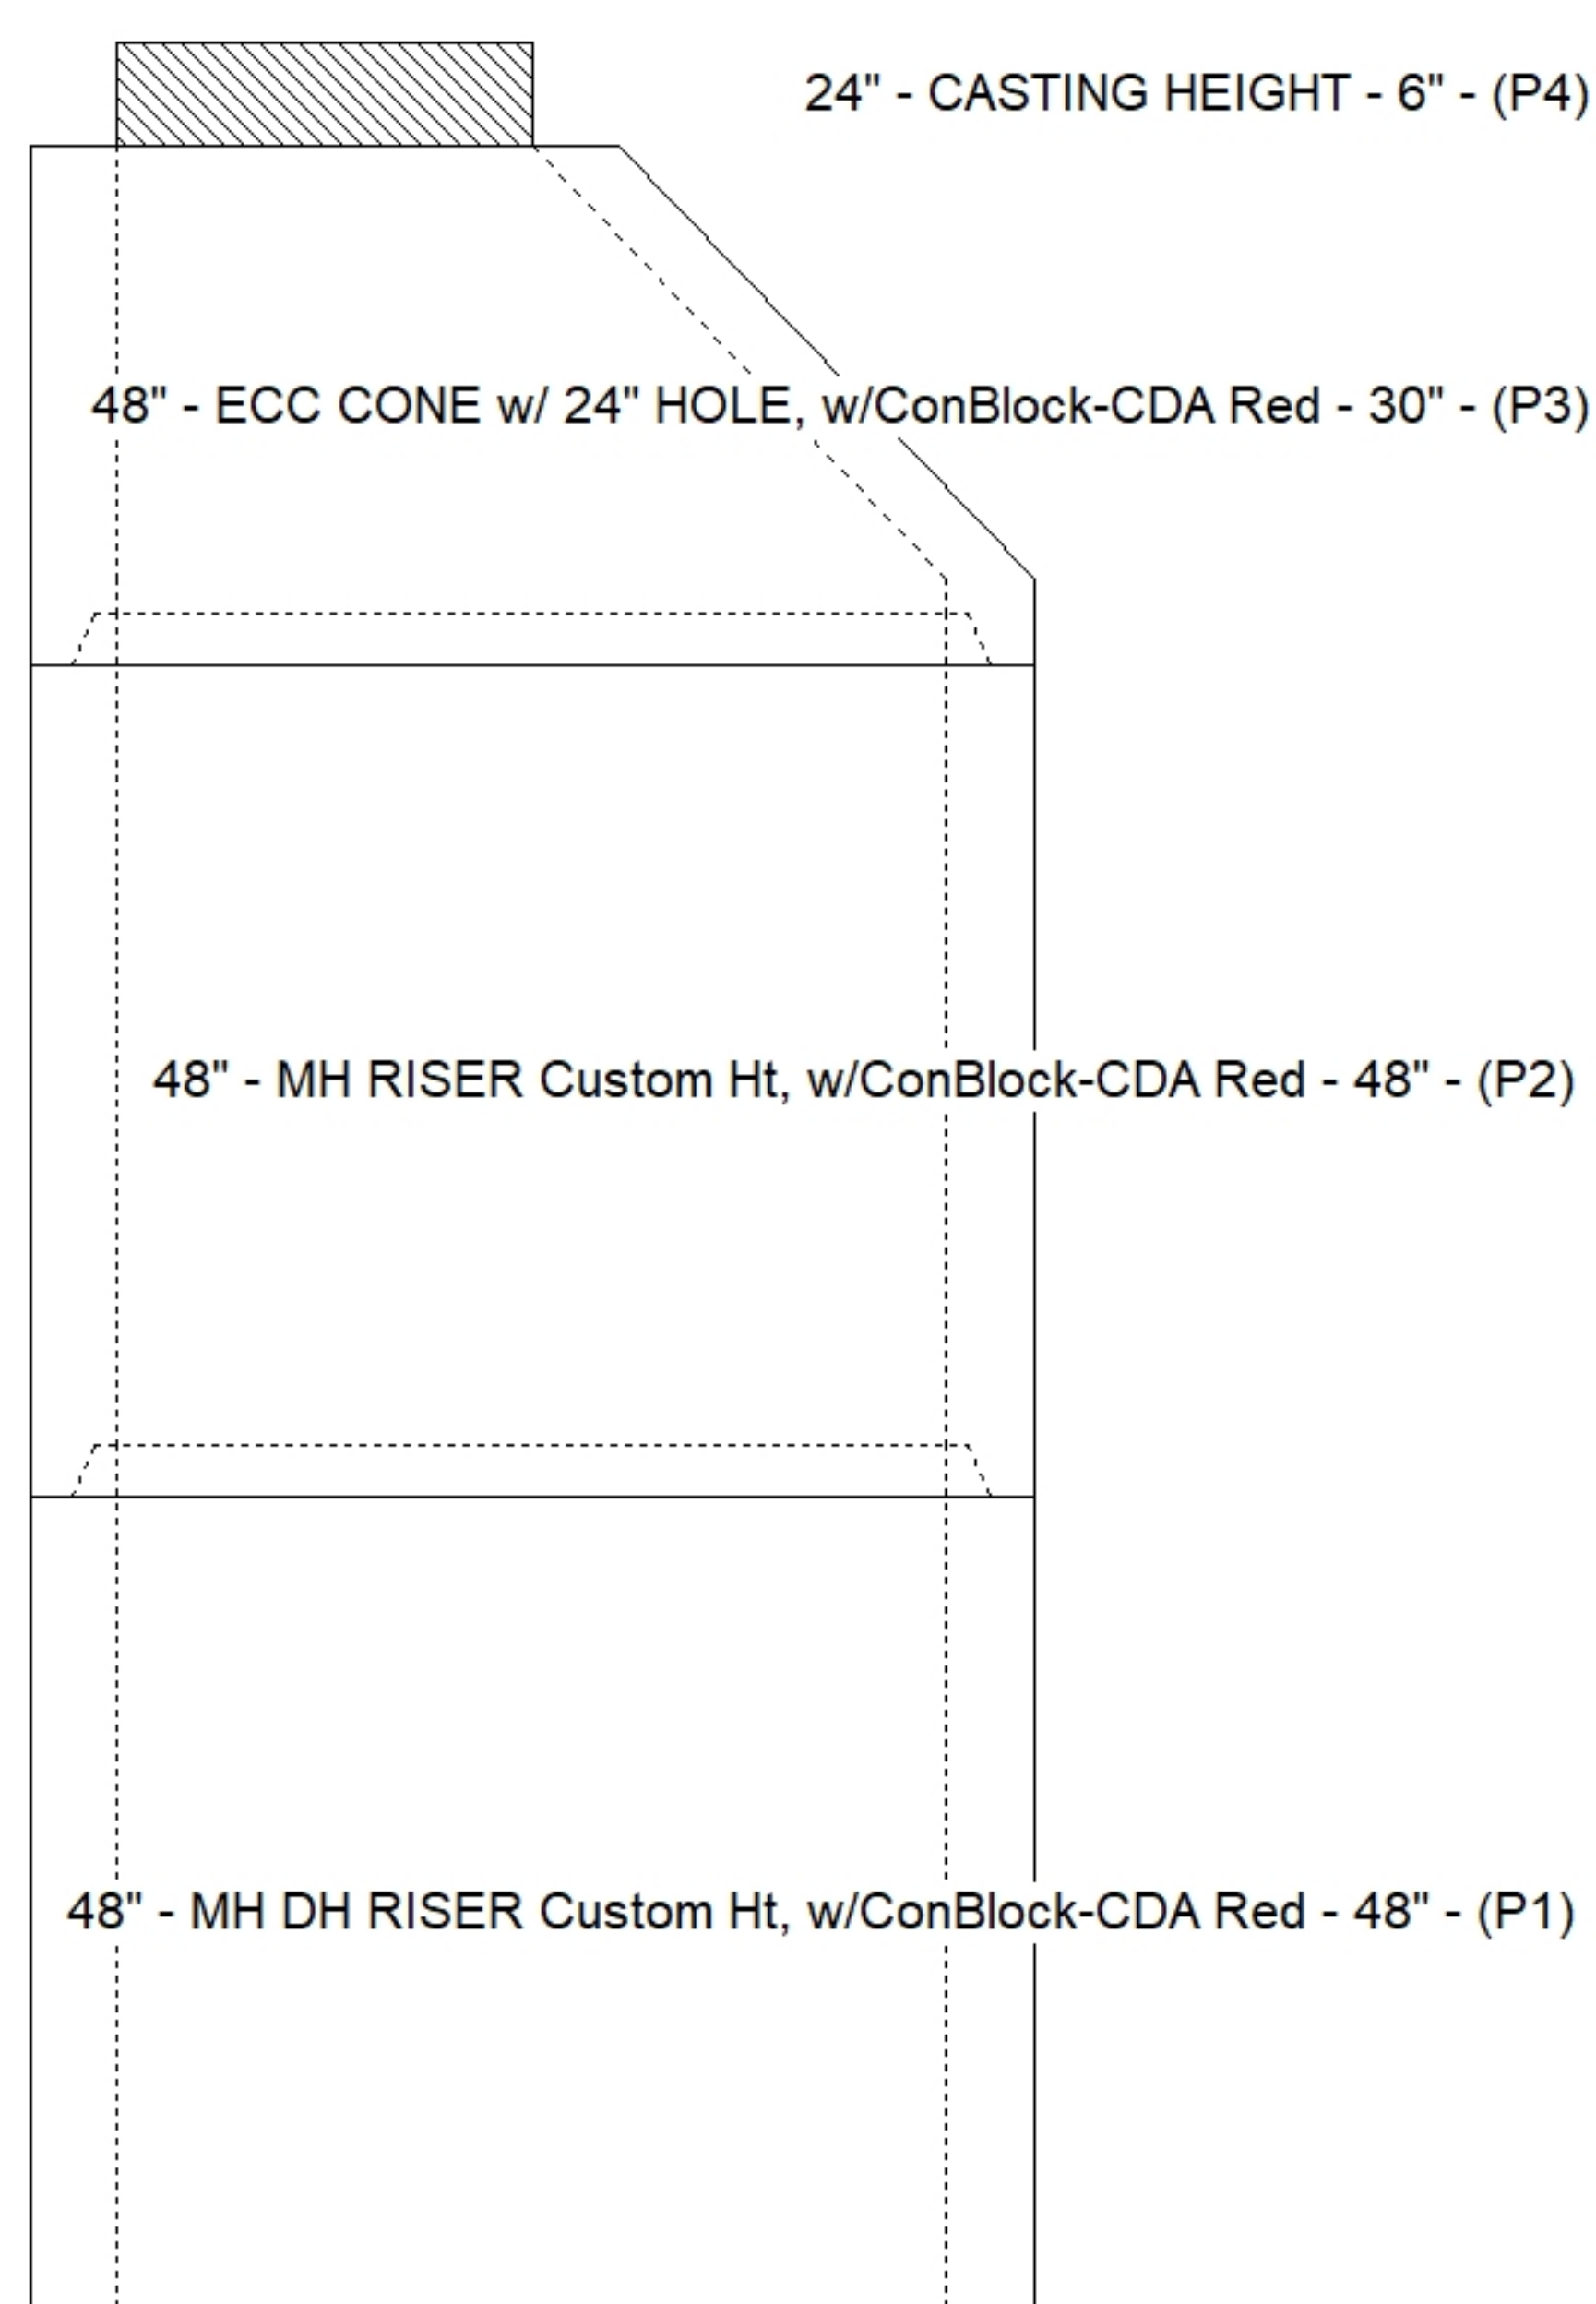

Rim: 760.87'	Sump: 5"	Floor (Bot): 749.713'
Invert: 750.13'	Floor (Top): 749.713'	Overall Height: 11'
Rim to Invert: 10.74'	Floor Height: 0"	Slack: 1.88"

P4) 24" - CASTING HEIGHT - 6"	0 lb
P3) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red - 30"	1961 lb
P2) 48" - MH RISER Custom Ht, w/ConBlock-CDA Red - 48"	3305 lb
P1) 48" - MH DH RISER Custom Ht, w/ConBlock-CDA Red - 48"	3147 lb
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)	0 lb
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212	0 lb
1) CASTING - JBS 1155 F/C SANITARY	250 lb
2) 48" - Conseal CS-102 1.00" (Double)	0 lb
1) 24" - Conseal CS-102 1.00" (Double)	0 lb
1) PSX - 12M NYLO	8 lb
2) DOGHOUSE - 12"x16"	0 lb
1) PSX - 12-06 NYLO	8 lb
11) MH Step ML-10-TDS-NCR - 10"	0 lb

Structure Total:	8680 lb

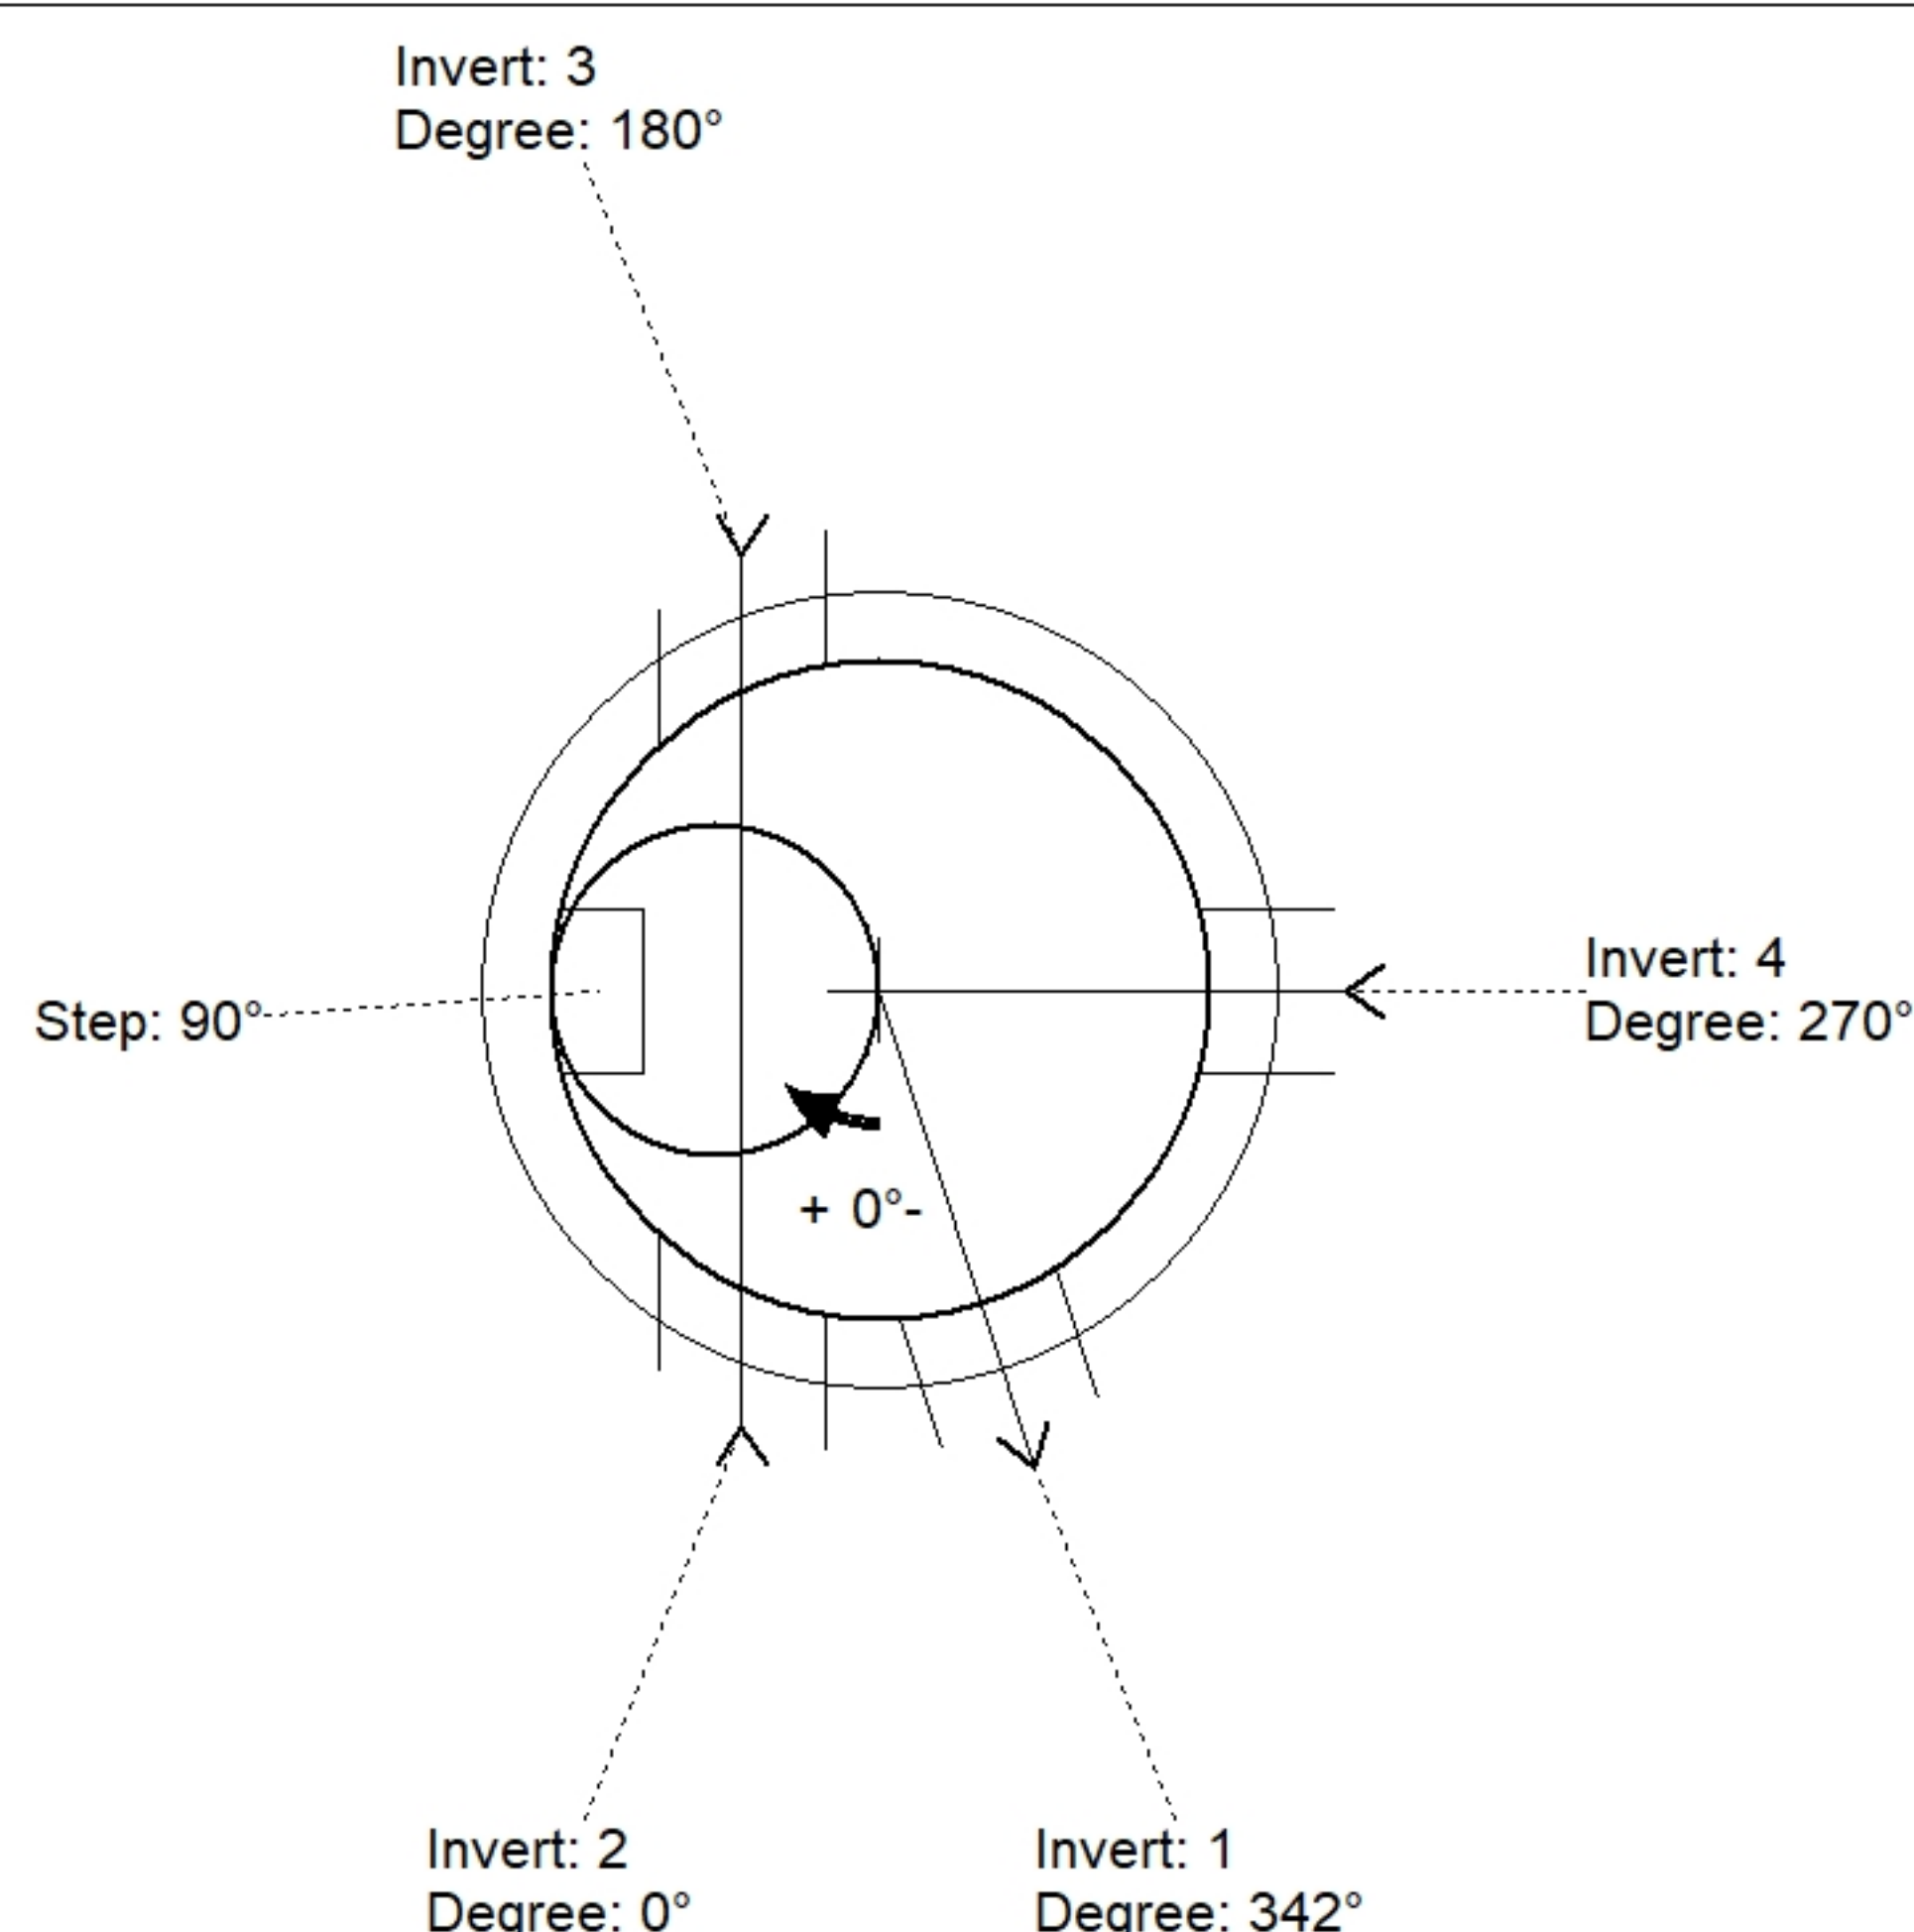

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')_	Ref
Rim	760.87'							
Reducer								
Invert 1	750.13'	342°	8" DI	9"	12"	PSX 12M NYLO	3"	P1
Invert 2	750.13'	0°	6" DI	6.875"	12" x 16"	DOGHOUSE 12"x16"	0"	P1
Invert 3	750.13'	180°	6" DI	6.875"	12" x 16"	DOGHOUSE 12"x16"	0"	P1
Invert 4	755'	270°	6" PVC SDR35	6.25"	12"	PSX 12-06 NYLO	8.19"	P2
Invert 5								
Invert 6								
Invert 7								
Invert 8								

SUBMITTAL
APPROVED BY:
