




Job Name: 25-3118 - W6 Ph 2-C Force Main Improvements Job Location: Fort Mitchell, KY 41017 Contractor: Lykins Contracting					Plant: 100 6/2/2026 8:12:43 AM		Tech: J. Horsley - A PC: Celina Goff				
Structure ID: 2280815 (Rev)											
P2 MH048RS48			MH RISER T/G								
P5) 24" - CASTING HEIGHT - 7" P4) 48" - CON CONE w/24" HOLE F/G - 36" P3) 48" - MH RISER T/G - 48" P2) 48" - MH RISER T/G - 48" P1) 48" - MH BASE (10"F) Custom Ht T/n - 48" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 3) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) Kor-N-Seal2 - S206-28 13) MH Step ML-10-TDS-NCR - 10"						0 lb 2252 lb 3353 lb 3353 lb 5025 lb 1440 lb 0 lb 0 lb 0 lb 13 lb 0 lb ----- 15437 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. STEPS AT 270 DEGREES 5. 7" CASTING SUPPLIED BY OTHERS			
Rim: 767' Rim to Invert: 15.51' Slack: 1.429" Sump: 2.309" Step Position: 270°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

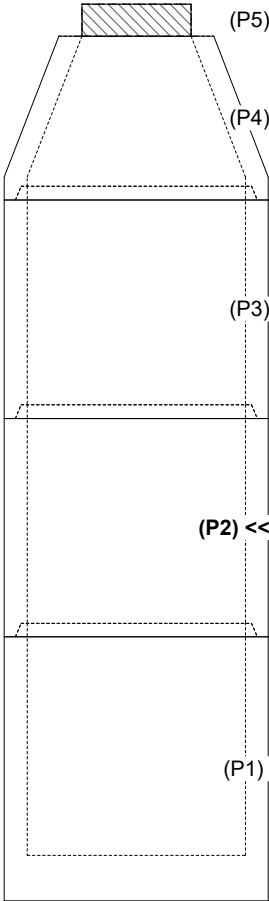

RIGHT-SIDE UP VIEW (int. dimensions)



INSIDE WALL DIMENSIONS

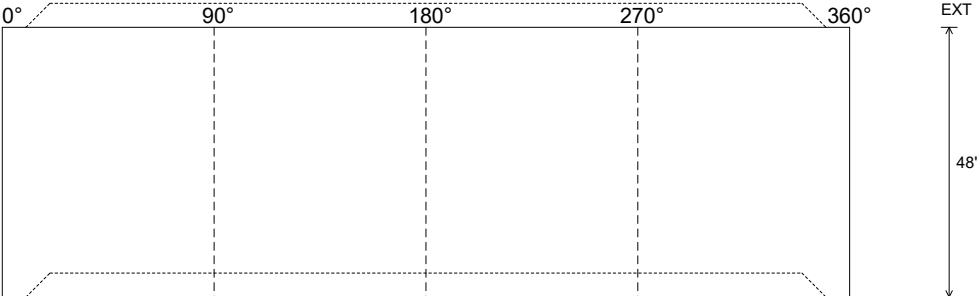

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 48" Height (Ext): 48"	Weight (Net): 3353 lb Volume (Net): 0.86cu.yd
----------------------------------	------------------------------------	--	--	--
