

Structure ID: 2301566

P3 MH048RS60

MH RISER T/G

P7) 24" - CASTING HEIGHT - 7" P6) 48" - CON CONE w/24" HOLE F/G - 24" P5) 48" - MH RISER T/G - 60" P4) 48" - MH RISER T/G - 60" P3) 48" - MH RISER T/G - 60" P2) 60" - MH Transition Slab 48" Hole T/G - 15" P1) 60" - MH BASE (12"F) Custom Ht T/n - 66" 1) 60" - MH INVERT CHANNEL - FULL HEIGHT 1) 60" - Conseal CS-102 1.00" (Double) 4) 48" - Conseal CS-102 1.00" (Double) 2) A-Lok - 1235 22) MH Step ML-10-TDS-NCR - 10"	0 lb 2252 lb 4192 lb 4192 lb 4192 lb 2204 lb 9635 lb 2692 lb 0 lb 0 lb 2 lb 0 lb ----- Structure Total: 29360 lb
---	---



Structure Notes:

1. PER ASTM C-478 SPECIFICATIONS
2. CONCRETE: 4,000 PSI AT 28 DAYS
3. REINFORCEMENT: PER ASTM A615
4. STEPS AT 270 DEGREES
5. 7" CASTING SUPPLIED BY OTHERS


Rim: 769.68' Rim to Invert: 24.27' Slack: 2.24" Sump: 3" Step Position: 270°

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

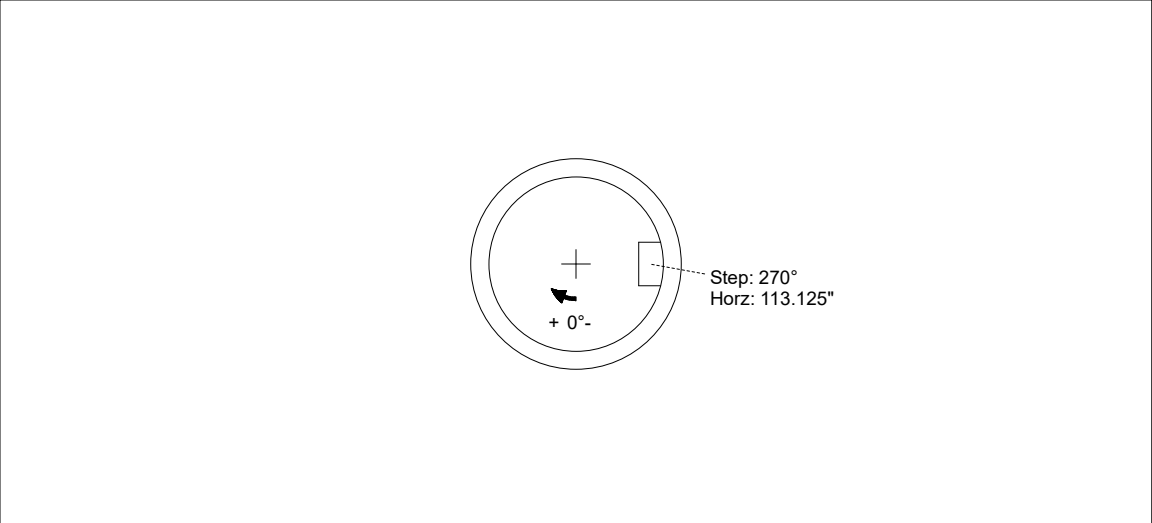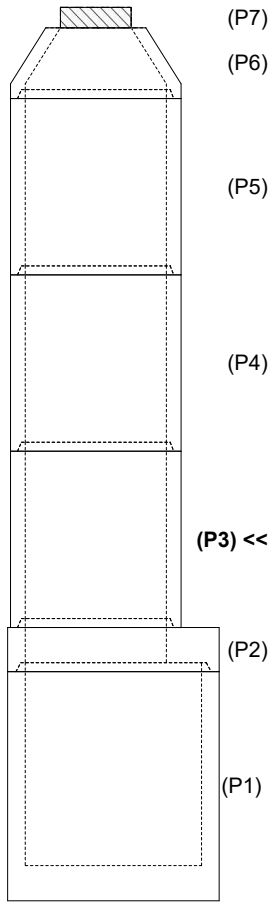

INSIDE WALL DIMENSIONS

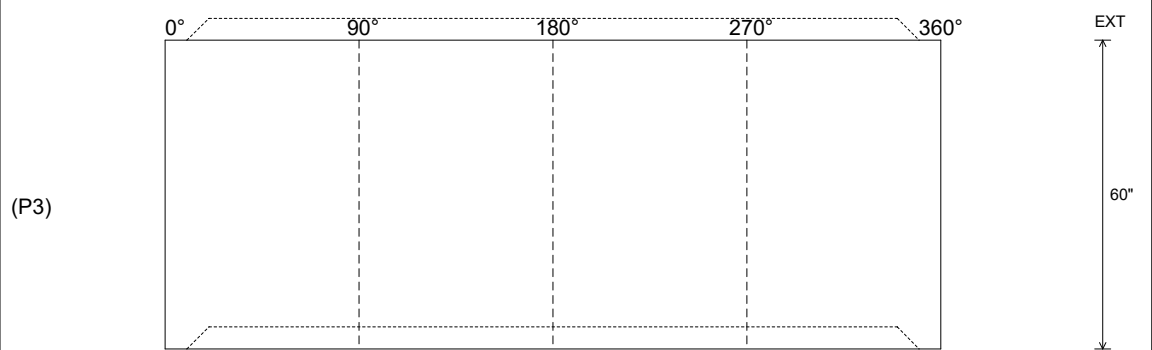

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 60" Height (Ext): 60"	Weight (Net): 4192 lb Volume (Net): 1.07cu.yd
----------------------------------	------------------------------------	--	--	--
