



Job Name: 25-3118 - W6 Ph 2-C Force Main Improvements Job Location: Fort Mitchell, KY 41017 Contractor: Lykins Contracting				Plant: 100 6/30/2026 8:11:35 AM		Tech: J. Horsley - A PC: Celina Goff				
Structure ID: 2301569										
P2		MH072RSVF		MH RISER Custom Ht T/G						
P6) 24" - CASTING HEIGHT - 7" P5) 48" - CON CONE w/24" HOLE F/G - 24" P4) 48" - MH RISER T/G - 36" P3) 72" - MH Transition Slab 48" Hole T/G - 15" P2) 72" - MH RISER Custom Ht T/G - 51" P1) 72" - MH BASE Custom Ht T/n - 51" 1) 72" - MH INVERT CHANNEL - FULL HEIGHT 2) 72" - Conseal CS-102 1.00" (Double) 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 1) A-Lok - 1235 1) Kor-N-Seal2 - S206-28 1) Kor-N-Seal2 - S206-22 10) MH Step ML-10-TDS-NCR - 10"					0 lb 2252 lb 2515 lb 3864 lb 7208 lb 10194 lb 5422 lb 0 lb 0 lb 0 lb 1 lb 6 lb 6 lb 0 lb ----- 31469 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. STEPS AT 270 DEGREES 5. 7" CASTING SUPPLIED BY OTHERS			
Rim: 761.81' Rim to Invert: 15.13' Slack: 0.56" Sump: 3" Step Position: 270°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1										
Invert 2										
Invert 3	751.83'	180°	135.125"	18" PVC SDR35	18.75"	Kor-N-Seal2 S206-22	22"	22.358"	6.75"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

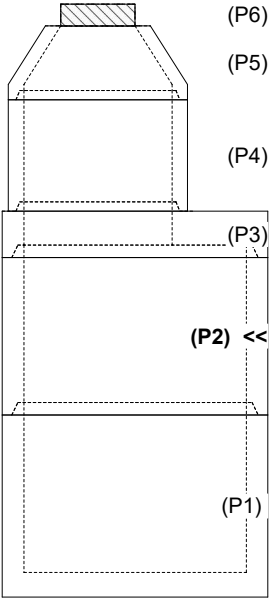

(P6)
(P5)
(P4)
(P3)
(P2) <<
(P1)

RIGHT-SIDE UP VIEW (int. dimensions)

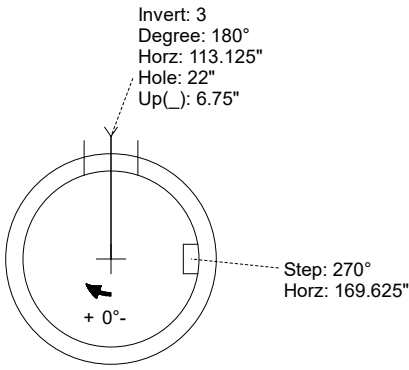


Invert: 3
Degree: 180°
Horz: 113.125"
Hole: 22"
Up(_): 6.75"

Step: 270°
Horz: 169.625"

+ 0°-

INSIDE WALL DIMENSIONS



(P2)

0° 90° 180° 270° 360°

113.125"

6.75"

51"

EXT

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 7" Floor Height: 0"	Height (Int): 51" Height (Ext): 51"	Weight (Net): 7208 lb Volume (Net): 1.84cu.yd
----------------------------------	------------------------------------	--	--	--
