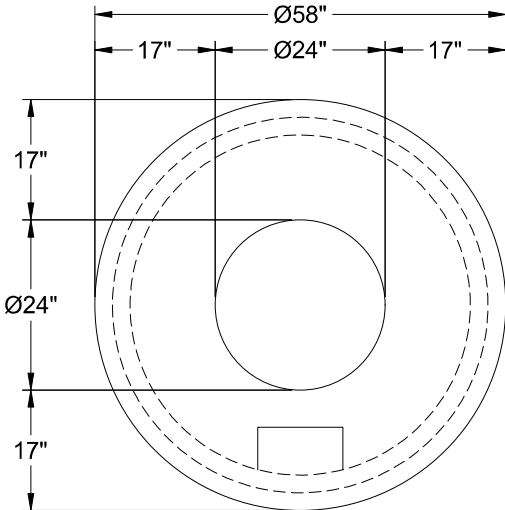



Job Name: 25-3118 - W6 Ph 2-C Force Main Improvements Job Location: Fort Mitchell, KY 41017 Contractor: Lykins Contracting		Plant: 100 6/30/2026 8:12:09 AM	Tech: J. Horsley - A PC: Celina Goff		
Structure ID: 2301569					
P5 MH048CCN24		CON CONE w/24" HOLE F/G			
P6) 24" - CASTING HEIGHT - 7" P5) 48" - CON CONE w/24" HOLE F/G - 24" P4) 48" - MH RISER T/G - 36" P3) 72" - MH Transition Slab 48" Hole T/G - 15" P2) 72" - MH RISER Custom Ht T/G - 51" P1) 72" - MH BASE Custom Ht T/n - 51" 1) 72" - MH INVERT CHANNEL - FULL HEIGHT 2) 72" - Conseal CS-102 1.00" (Double) 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 1) A-Lok - 1235 1) Kor-N-Seal2 - S206-28 1) Kor-N-Seal2 - S206-22 10) MH Step ML-10-TDS-NCR - 10"		0 lb 2252 lb 2515 lb 3864 lb 7208 lb 10194 lb 5422 lb 0 lb 0 lb 0 lb 1 lb 6 lb 6 lb 0 lb	<u>Structure Notes:</u> 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. STEPS REQUIRED 5. 7" CASTING SUPPLIED BY OTHERS		
Structure Total:		31469 lb			
					
 48" - CON CONE w/24" HOLE F/G - 24" - (P5)					
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 24"	Weight (Net): 2252 lb Volume (Net): 0.57cu.yd	
