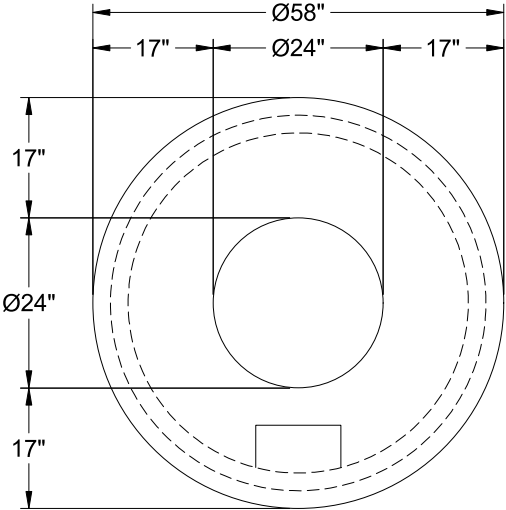



Job Name: 25-3118 - W6 Ph 2-C Force Main Improvements Job Location: Fort Mitchell, KY 41017 Contractor: Lykins Contracting		Plant: 100 6/2/2026 8:13:13 AM	Tech: J. Horsley - A PC: Celina Goff	
Structure ID: 717				
P3 MH048CCN36		CON CONE w/24" HOLE F/G		
P4) 24" - CASTING HEIGHT - 7" P3) 48" - CON CONE w/24" HOLE F/G - 36" P2) 48" - MH RISER T/G - 60" P1) 48" - MH BASE T/n - 42" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) Kor-N-Seal2 - S206-28 9) MH Step ML-10-TDS-NCR - 10"		0 lb 2252 lb 4192 lb 3719 lb 1440 lb 0 lb 0 lb 13 lb 0 lb ----- 11616 lb Structure Total:	Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. STEPS REQUIRED 5. 7" CASTING SUPPLIED BY OTHERS	
				
				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 36"	Weight (Net): 2252 lb Volume (Net): 0.57cu.yd
