

Job Name: 25-3170 - Publix BG
Job Location: Bowling Green, KY
Contractor: Scotty's Contracting & Stone, LLC

PC: C. Goff
 TECH: K. Cardwell
 Plant: Beaver Dam, KY



Structure ID: **DBI6A**
 Spec: Storm
 Type: BX 8inW, 8inF
 Size: 24" x 30"

Rim: 574.7'
 Invert: 572.12'
 Rim to Invert: 2.58'

Sump: 0"
 Floor (Top): 572.12'
 Floor Height: 8"


Floor (Bot): 571.453'
 Overall Height: 3.25'
 Slack: -0.04"

Structure Notes:
 PLAN LABEL: DBI 6A
 1. PER ASTM C-913 SPECS
 2. CONCRETE: 4,000 PSI AT 28 DAYS
 3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60)
 4. KY 460 FRAME & GRATE SUPPLIED BY ICAST


STRUCTURE SUMMARY:

P2) 24" x 30" - CASTING HEIGHT - 4"	0 lb
P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht F/n - 27"	3378 lb
1) CASTING - HOE KY-460-11 F/G (DBI 11)	421 lb
1) 24" x 30" - Conseal CS-102 1.00"	0 lb
1) DOGHOUSE INVRTD - 30"x27"	0 lb


Structure Total:	3799 lb

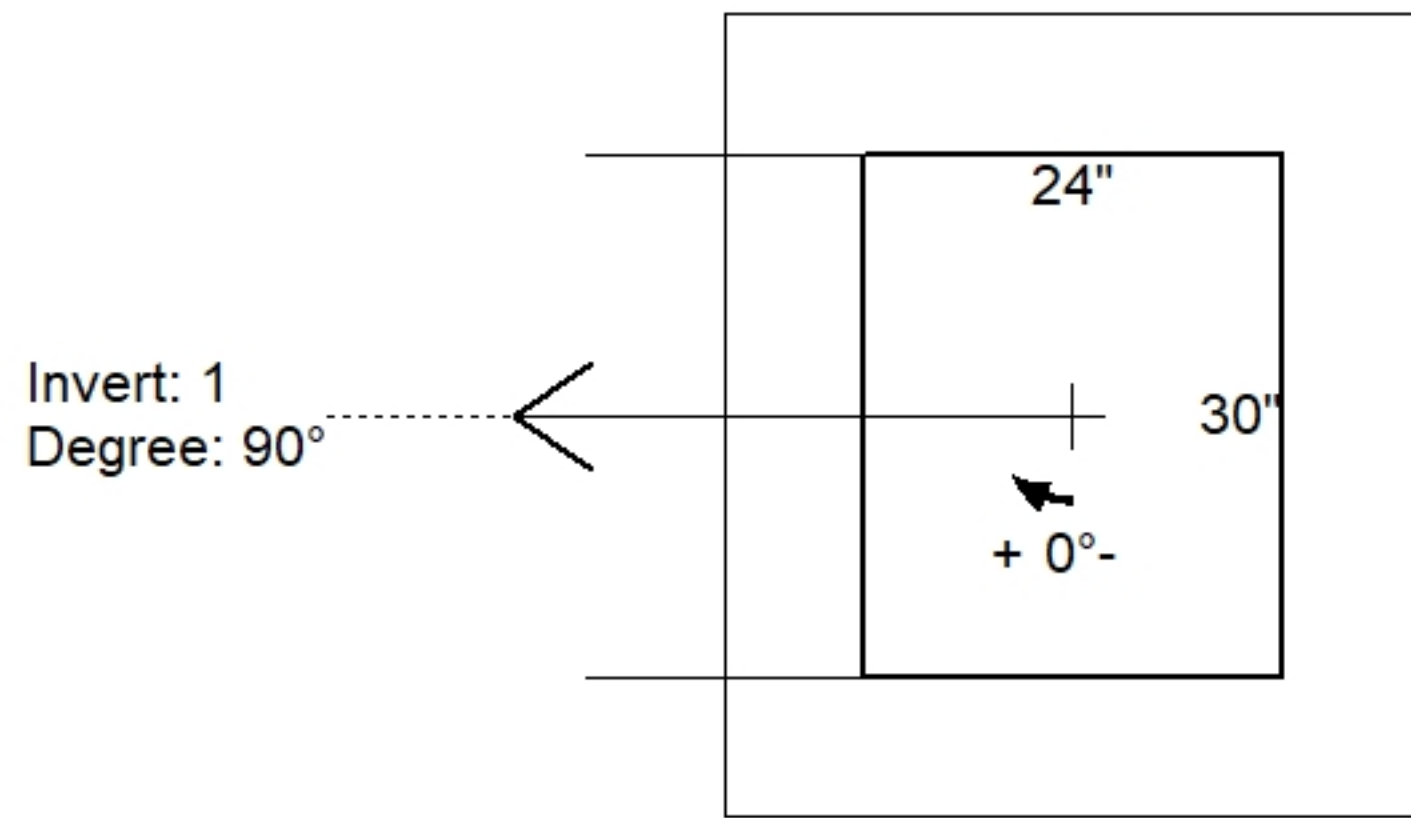

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	574.7'							
Reducer								
Invert 1	572.12'	90°	24" ADS N-12	28"	30" x 27"	DOGHOUSE INVRTD 30"x27"	-2"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

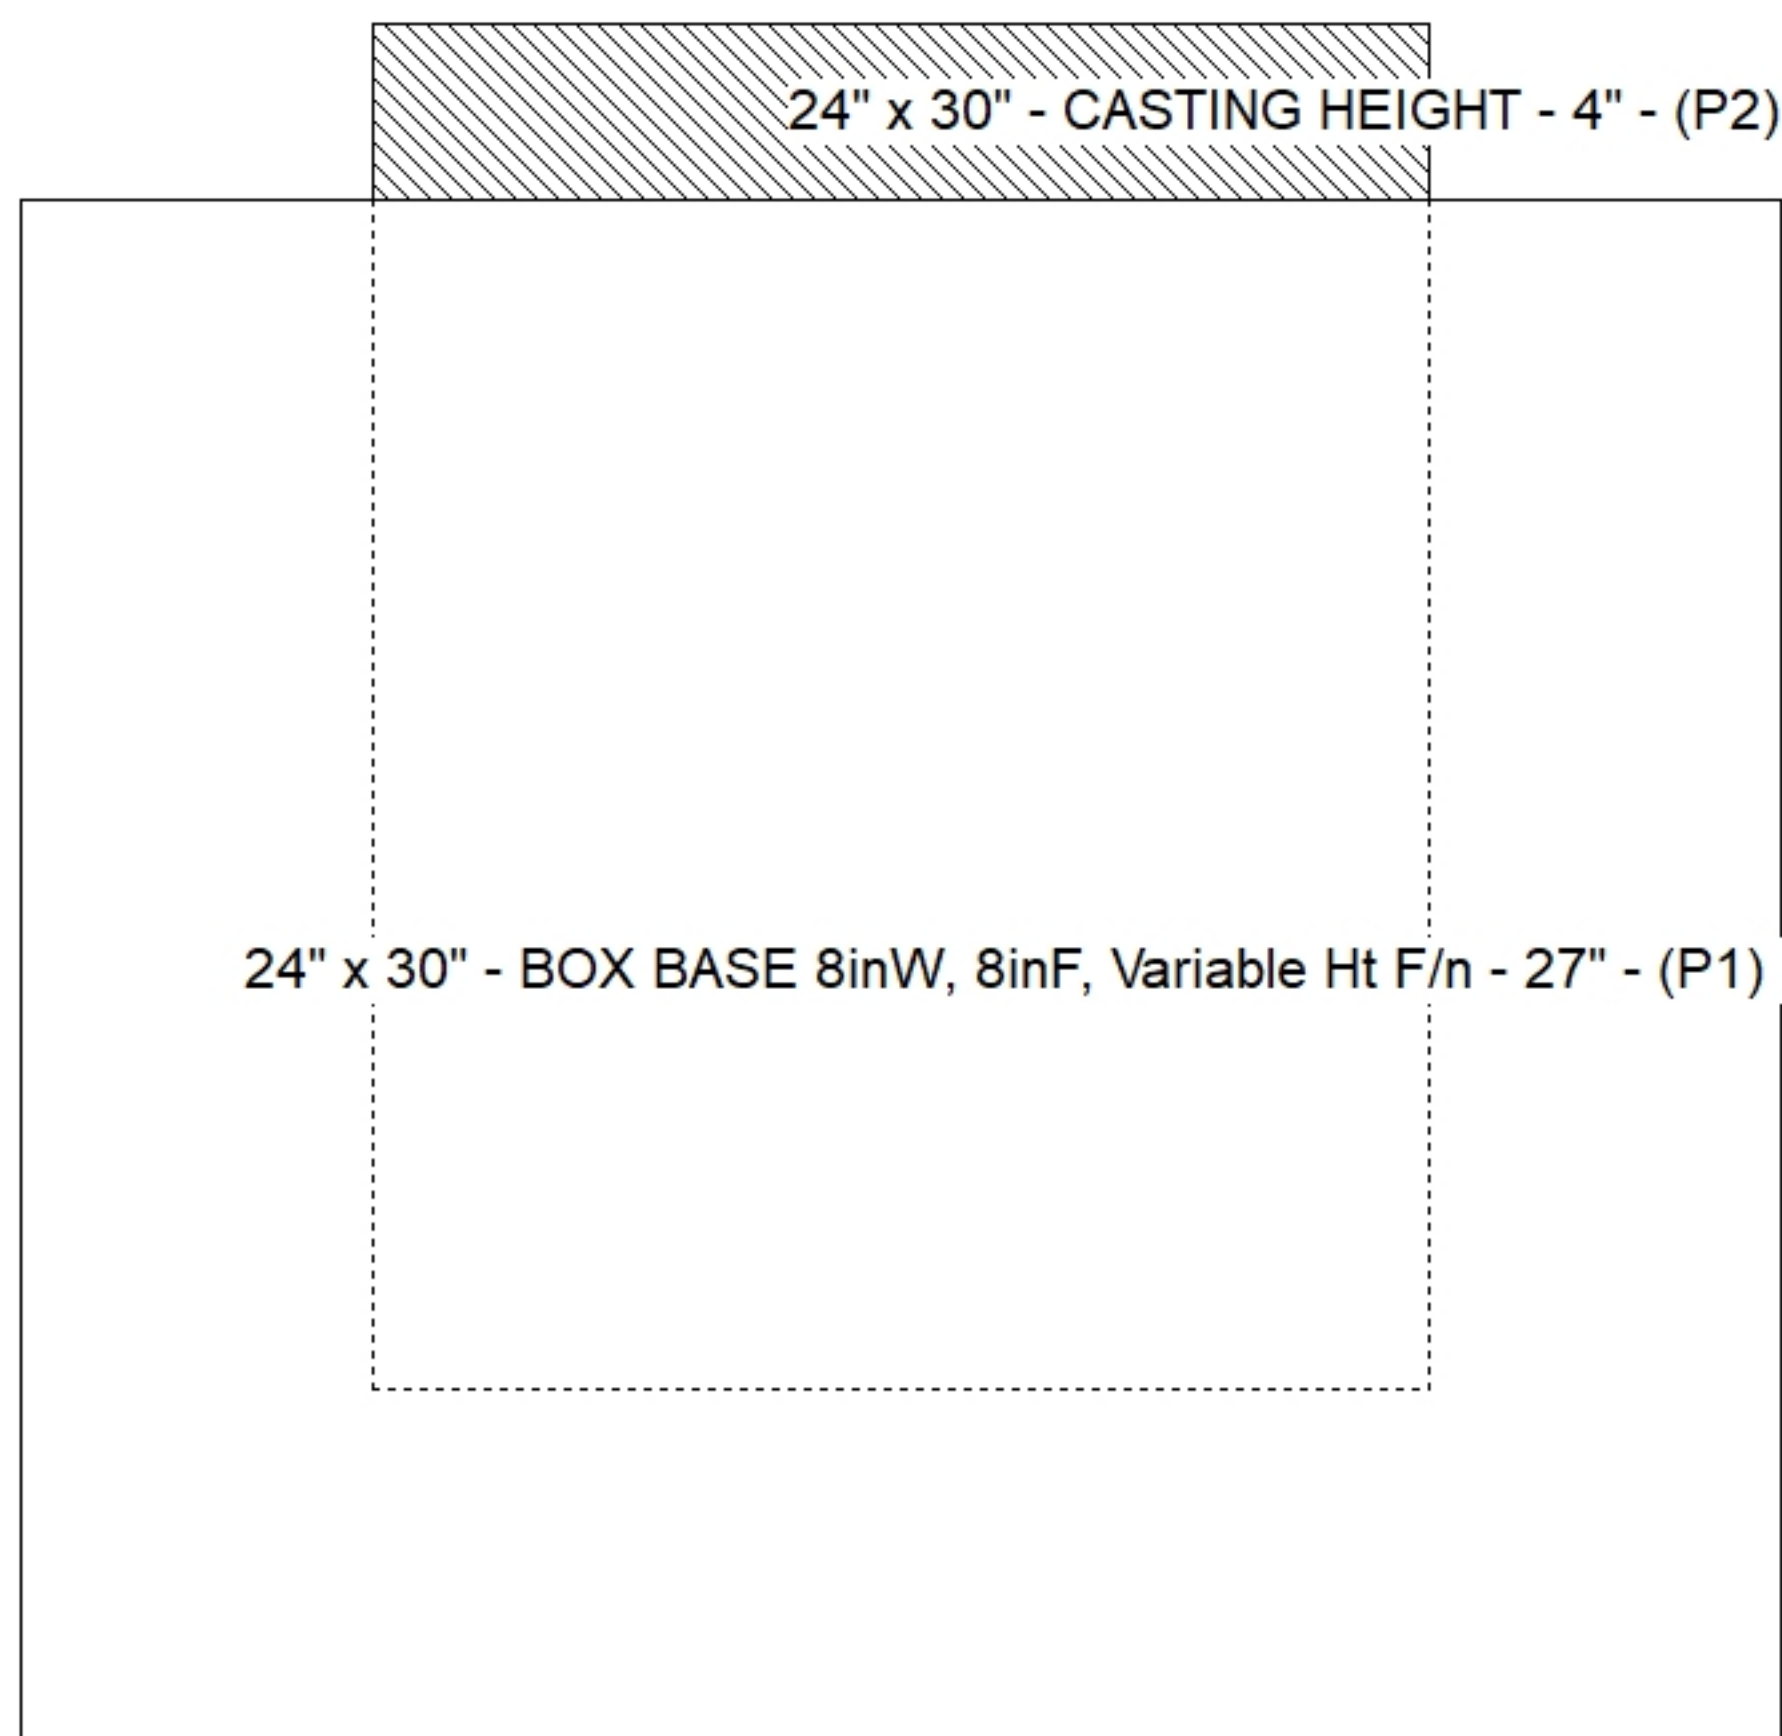

Cast (Int. Dim.) - Interior Dimensions

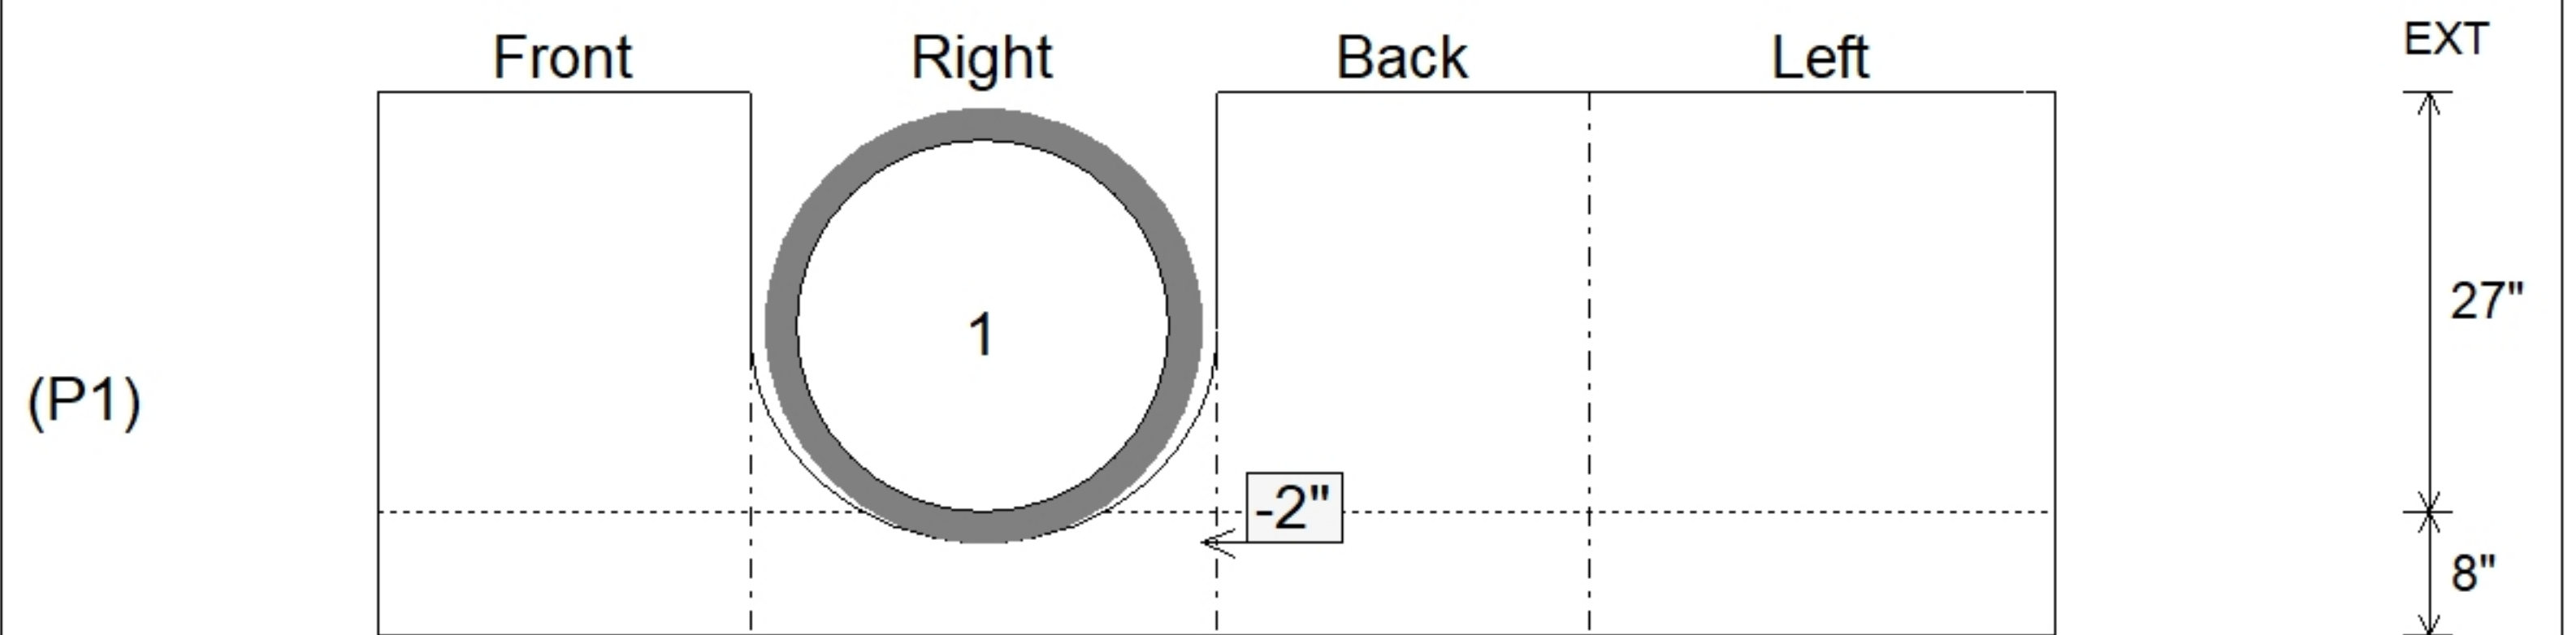

Submittal Drawing
 10/23/2025 7:20:19 AM

SUBMITTAL
 APPROVED BY:
