

Contractor: Walker Principles

TECH: J. Horsley

Plant: 100



Size: 60" x 60"

Rim to Invert: 7.59'

Floor Height: 8"


Slack: 0.04"

REINFORCING PER ASTM A615 (GRADE 60).
 - TOP SLAB (As .62) T#5 BARS AT 6" C.C.E.W.
 - WALLS (As .47) #5 BARS AT 8" C.C.E.W.
 - FLOOR (As .47) #5 BARS AT 8" C.C.E.W.


1) A-Lok - 0150

1 lb


Structure Total: 23681 lb

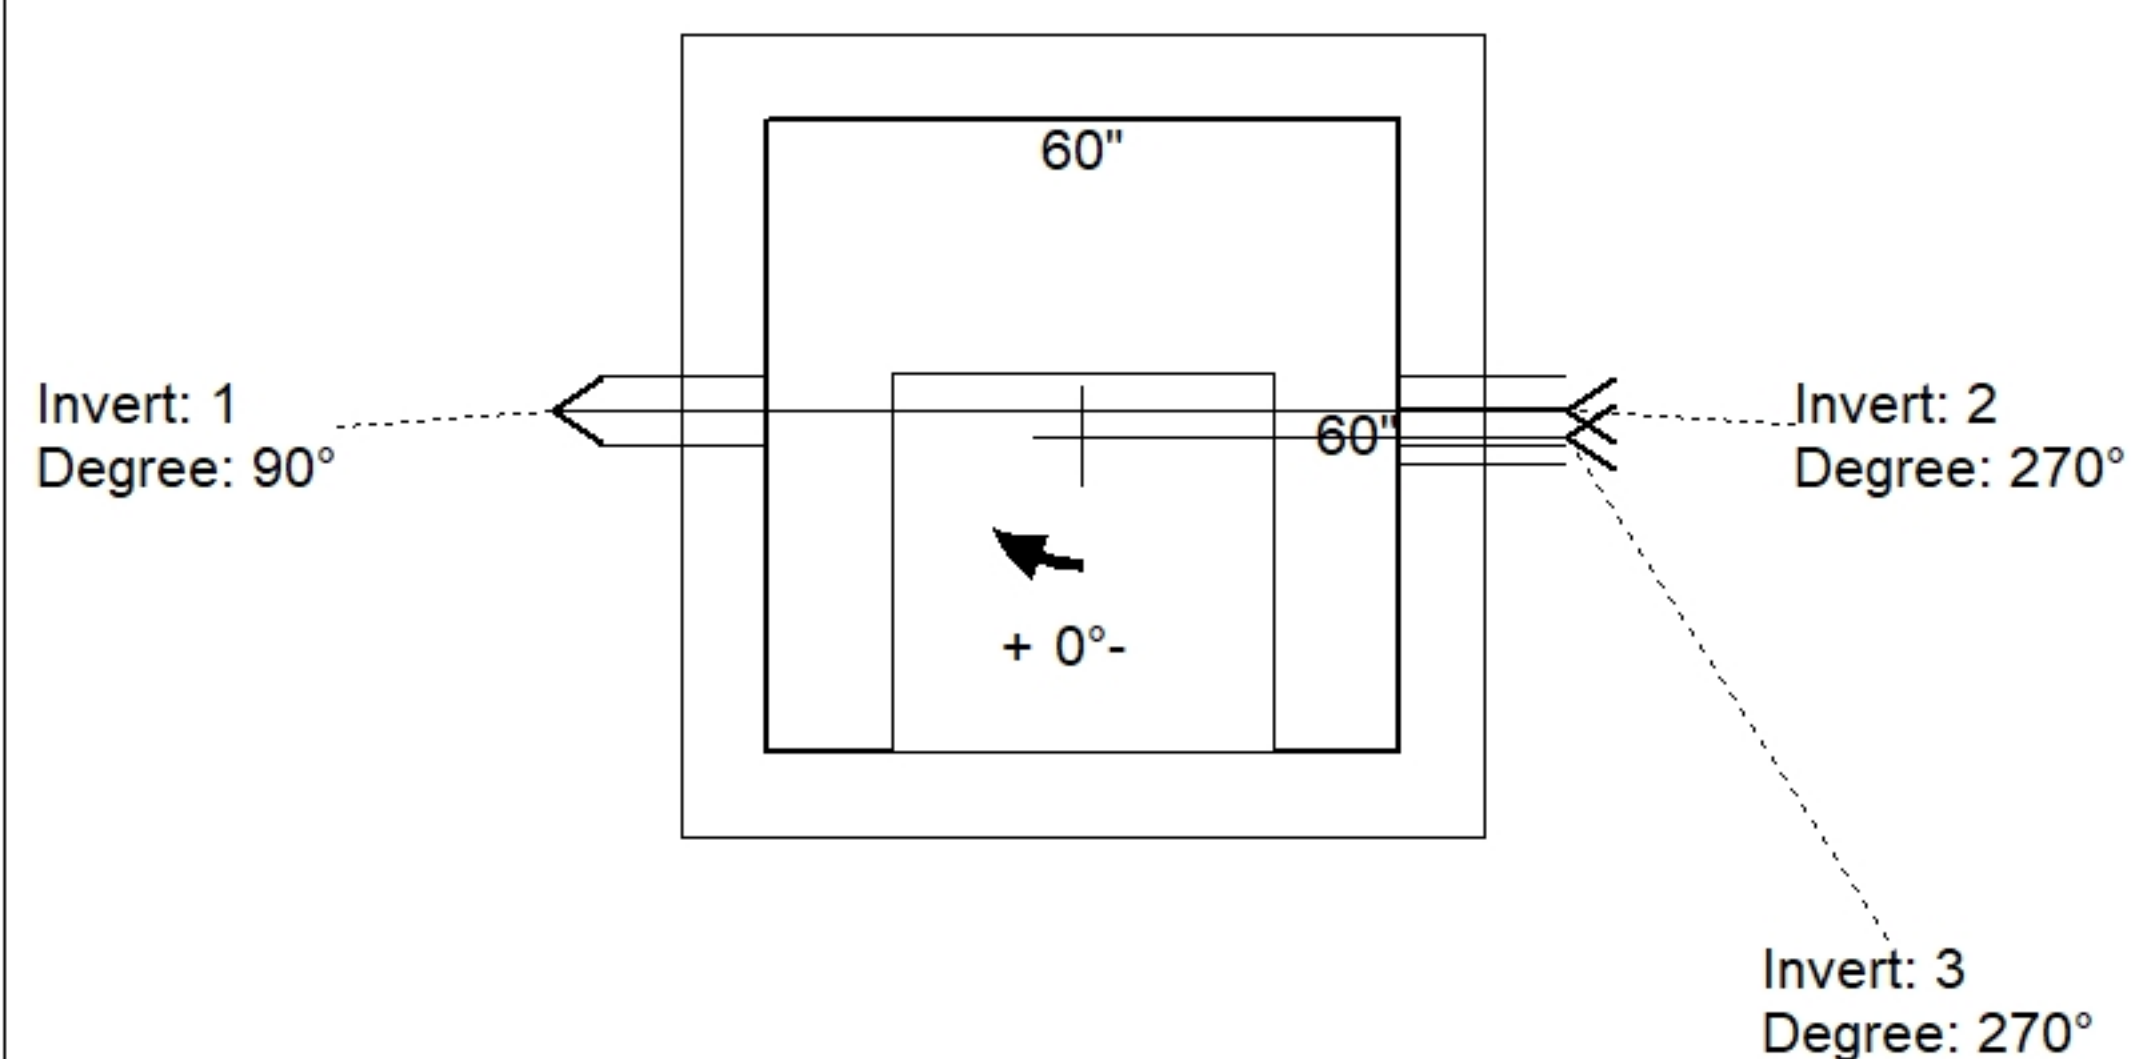

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (")	Ref
Rim	890.5'							
Reducer								
Invert 1	885.83'	90°	3" DI	3.5"	6.5"	Z-Lok C107-3	34.25"	P1
Invert 2	885.5'	270°	3" DI	3.5"	6.5"	Z-Lok C107-3	30.29"	P1
Invert 3	882.91'	270°	4" DI	4.75"	5.25"	A-Lok 0150	0.335"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

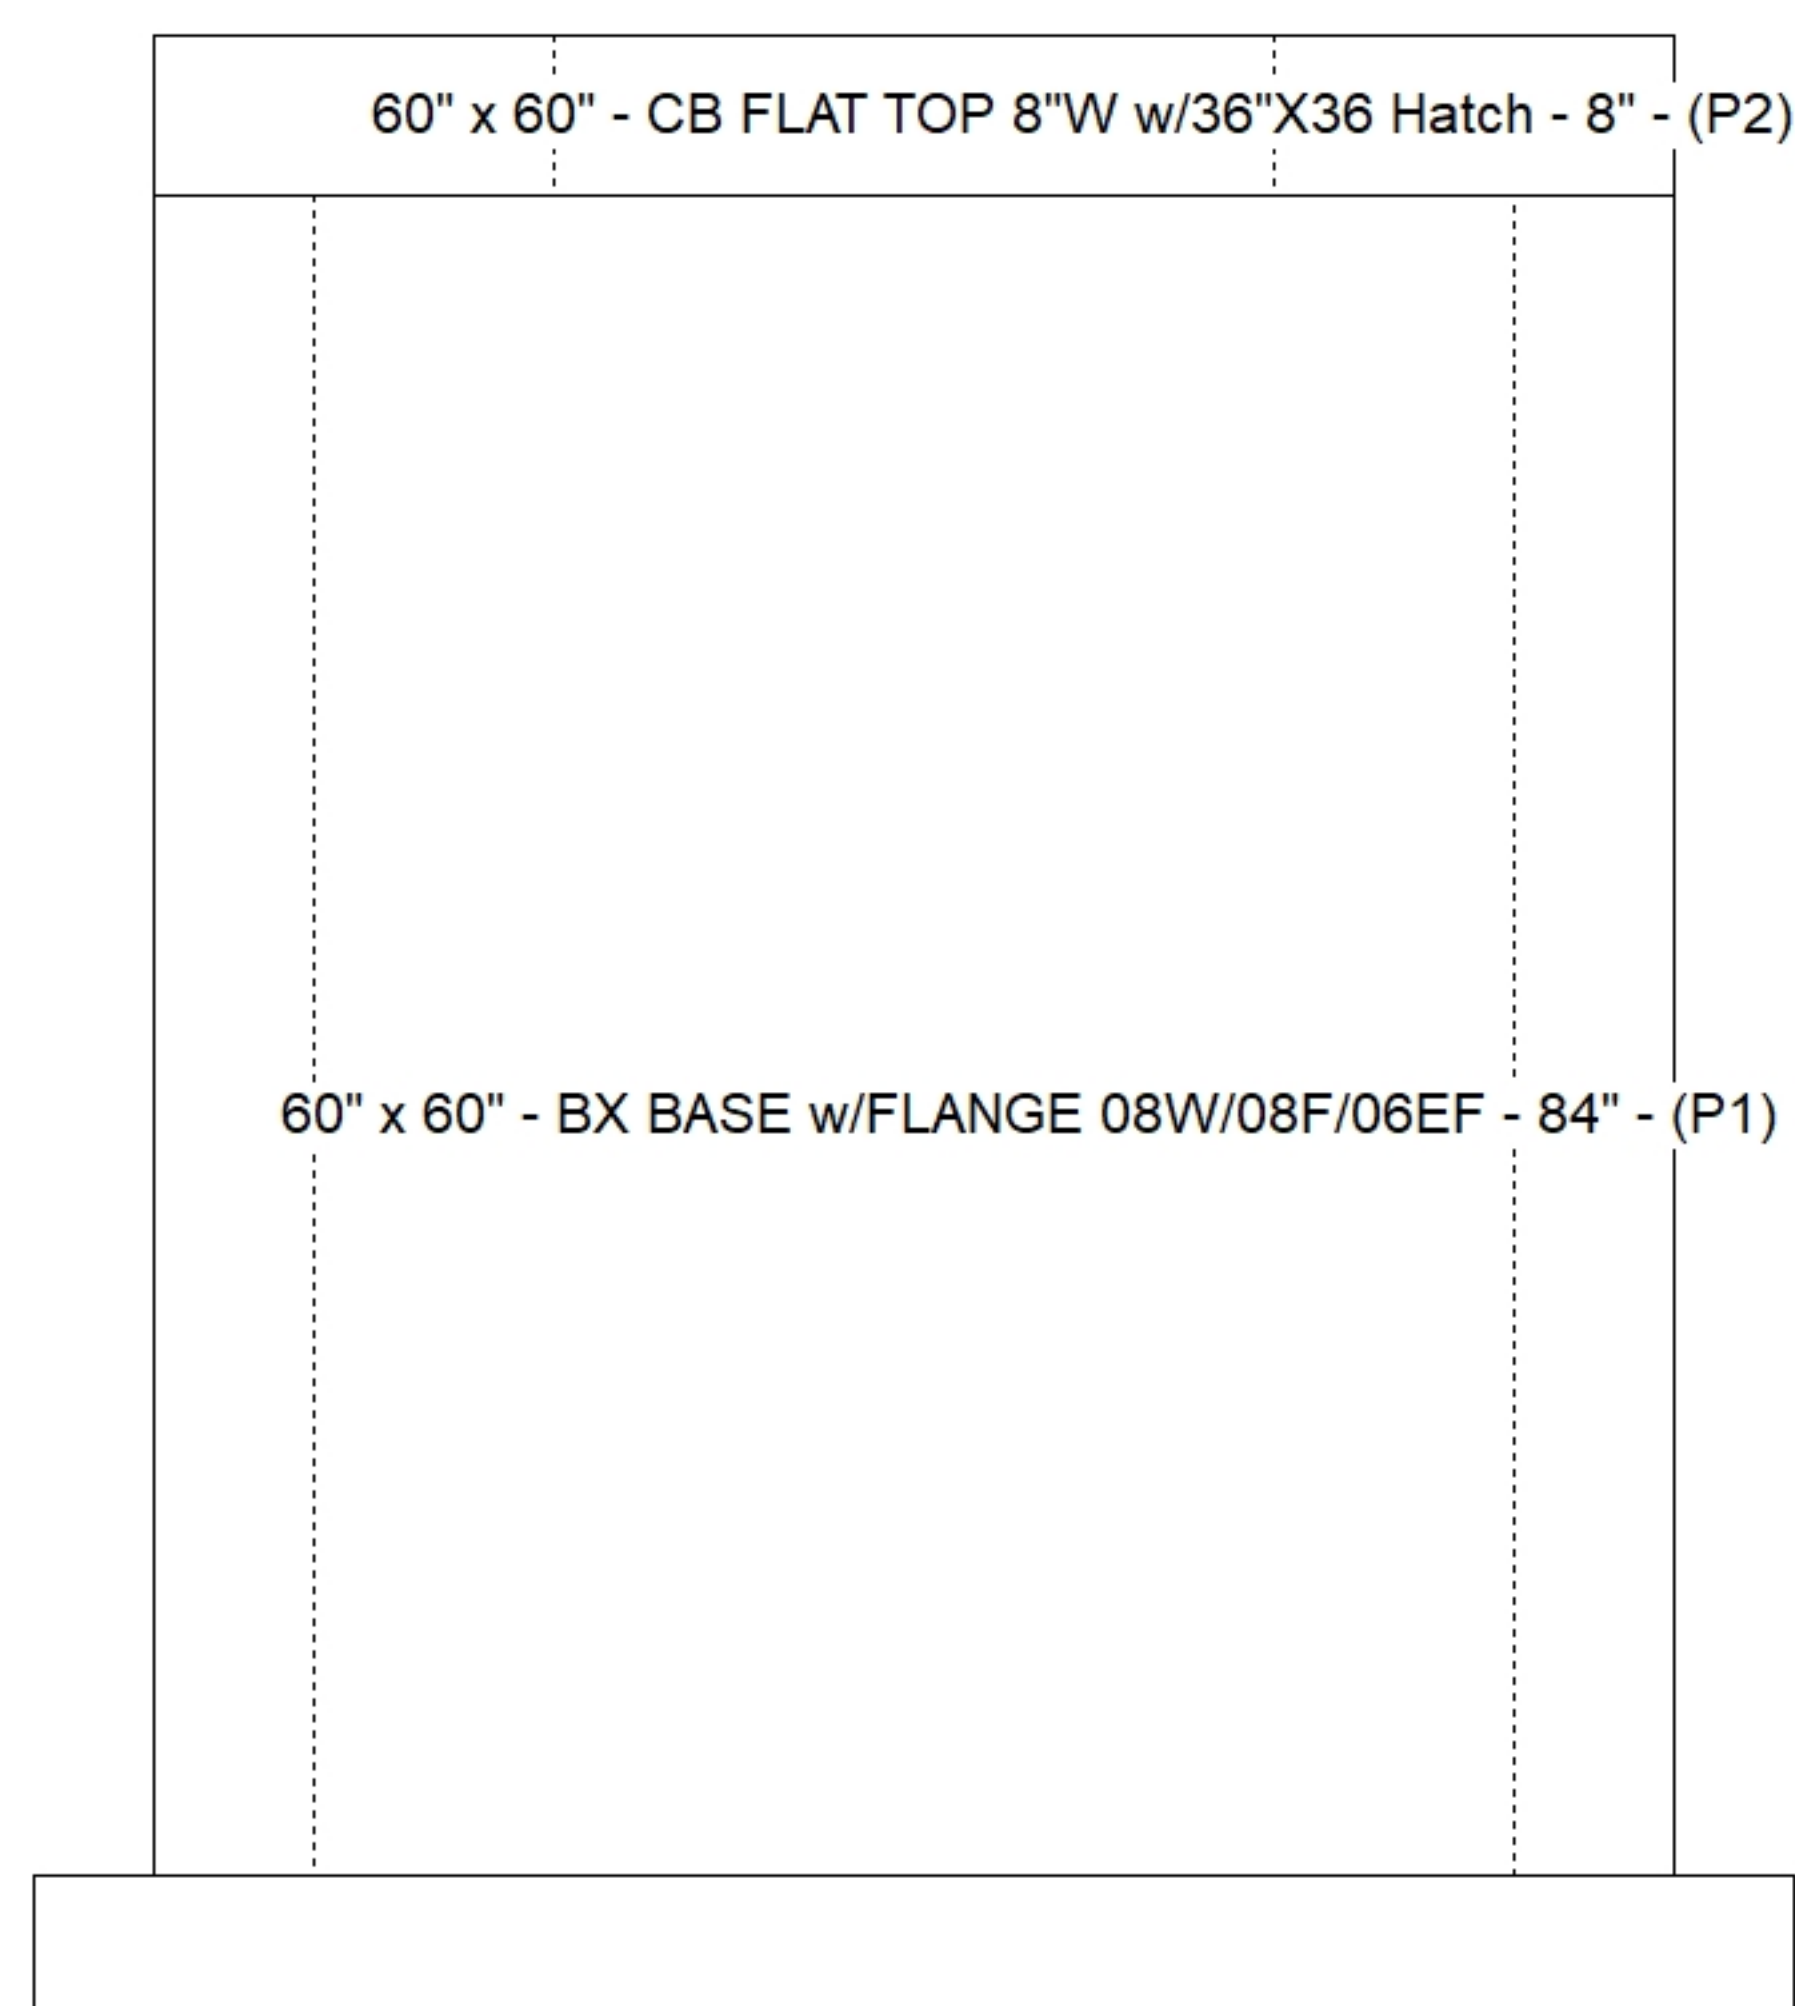

Default - Interior Dimensions

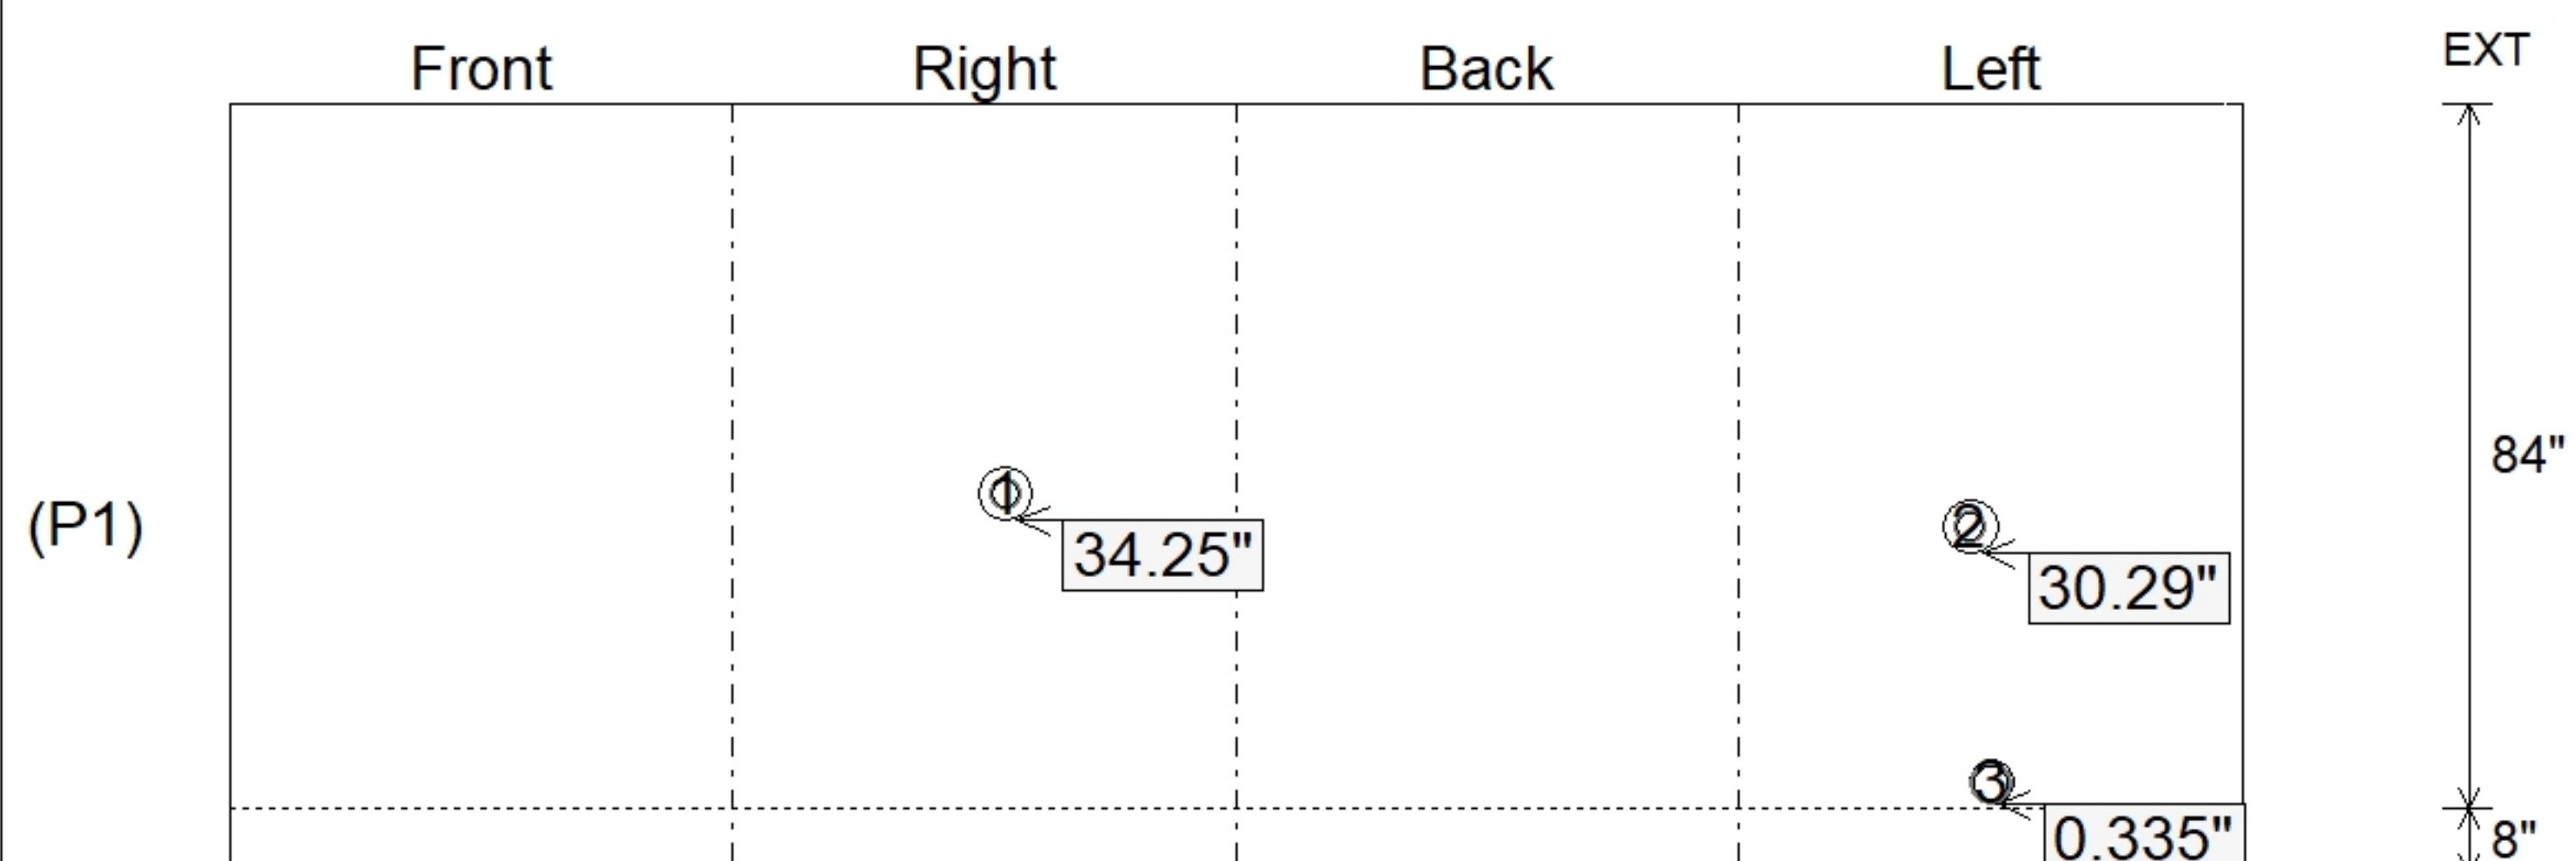

Submittal Drawing
7/9/2026 7:51:05 AM

SUBMITTAL
APPROVED BY:
