

Contractor: Walker Principles

TECH: J. Horsley

Plant: 100



Slack: 0.04"


REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- RISER/WALLS (As .18)
- FLOOR (As .47) #5 BARS AT 8" C.C.E.W.


- P4) 60" - MH FLAT TOP w/30"x30" Hatch - 13"
- P3) 60" - MH RISER SPECIAL - 18"
- P2) 60" - MH RISER SPECIAL - 72"
- P1) 60" - MH BASE w/FLANGE (08F/07EF) - 43"
- 3) JOINT WRAP - 12" WD x 096" MAC WRAP
- 1) HATCH (Alum.) - HALLIDAY W1S 30"x30"
- 1) SECONDARY POUR - EXT. FLANGE
- 3) 60" - Conseal CS-231 1.00" (Double)
- 1) Z-Lok - C107-3
- 2) A-Lok - 0225
- 1) A-Lok - 0150

2455 lb
1879 lb
7442 lb
8388 lb
0 lb
62 lb
0 lb
0 lb
1 lb
2 lb
1 lb


Structure Total: 20230 lb

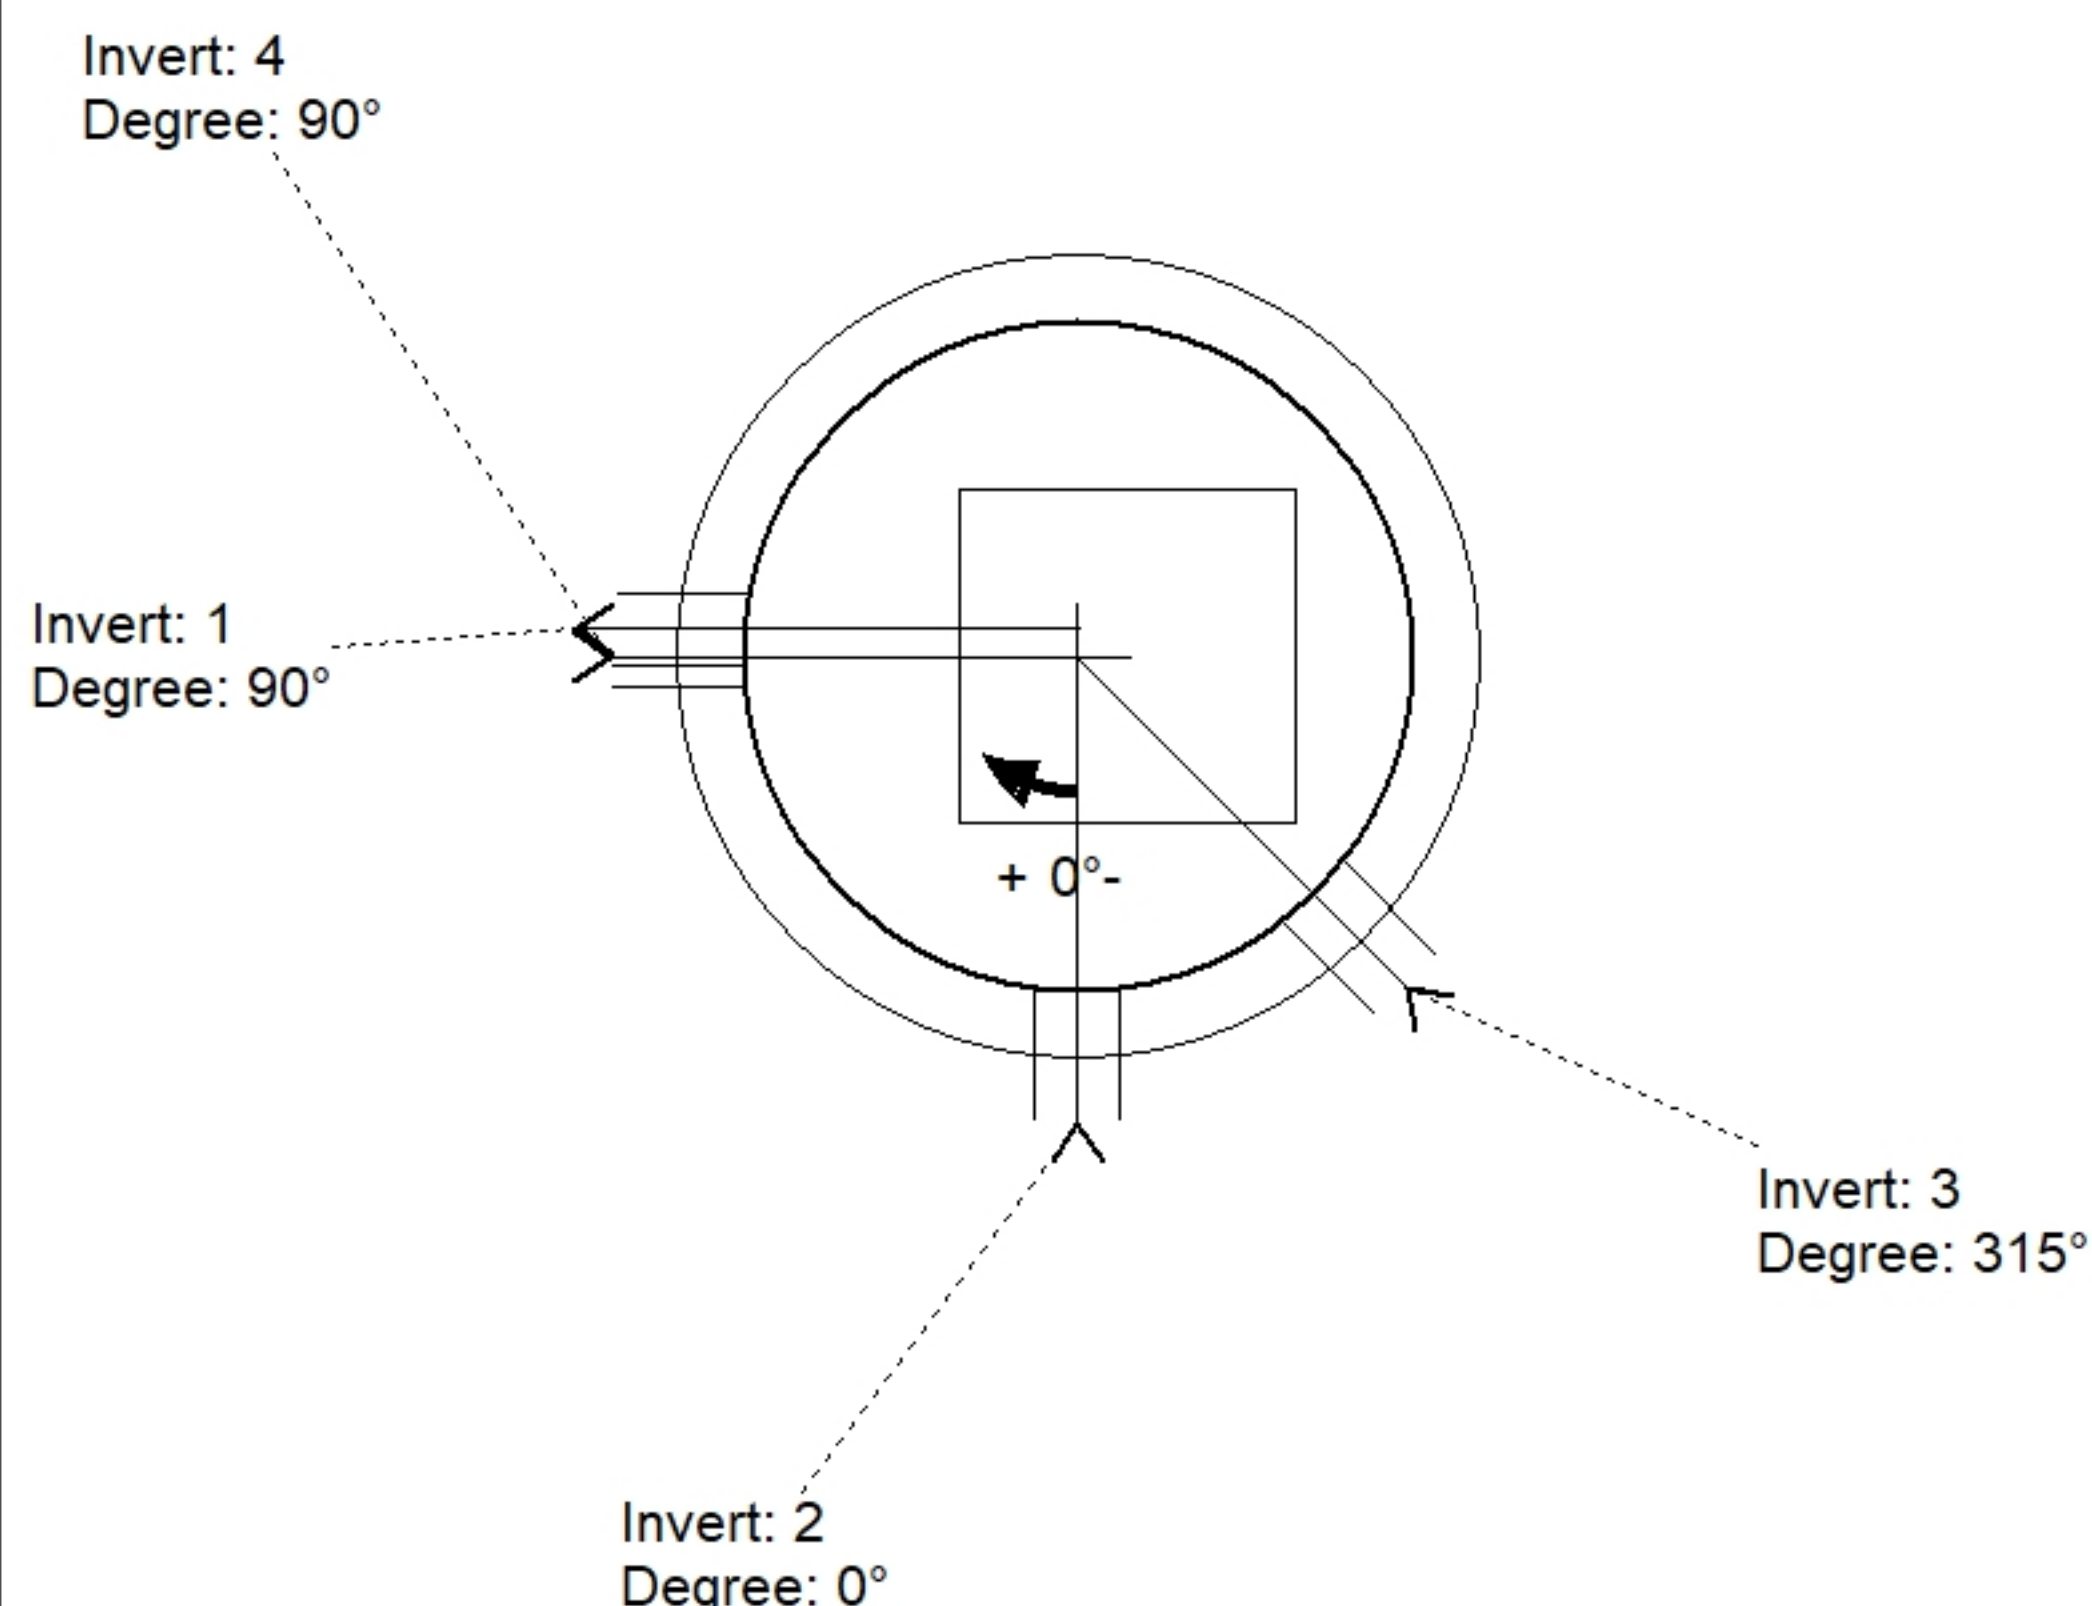

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	890.5'							
Reducer								
Invert 1	885.83'	90°	3" DI	3.5"	6.5"	Z-Lok C107-3	40.5"	P2
Invert 2	885.5'	0°	6" DI	6.875"	7.63"	A-Lok 0225	37.475"	P2
Invert 3	883.5'	315°	6" DI	6.875"	7.63"	A-Lok 0225	13.475"	P2
Invert 4	882.91'	90°	4" DI	4.75"	5.25"	A-Lok 0150	6.585"	P2
Invert 5								
Invert 6								
Invert 7								
Invert 8								

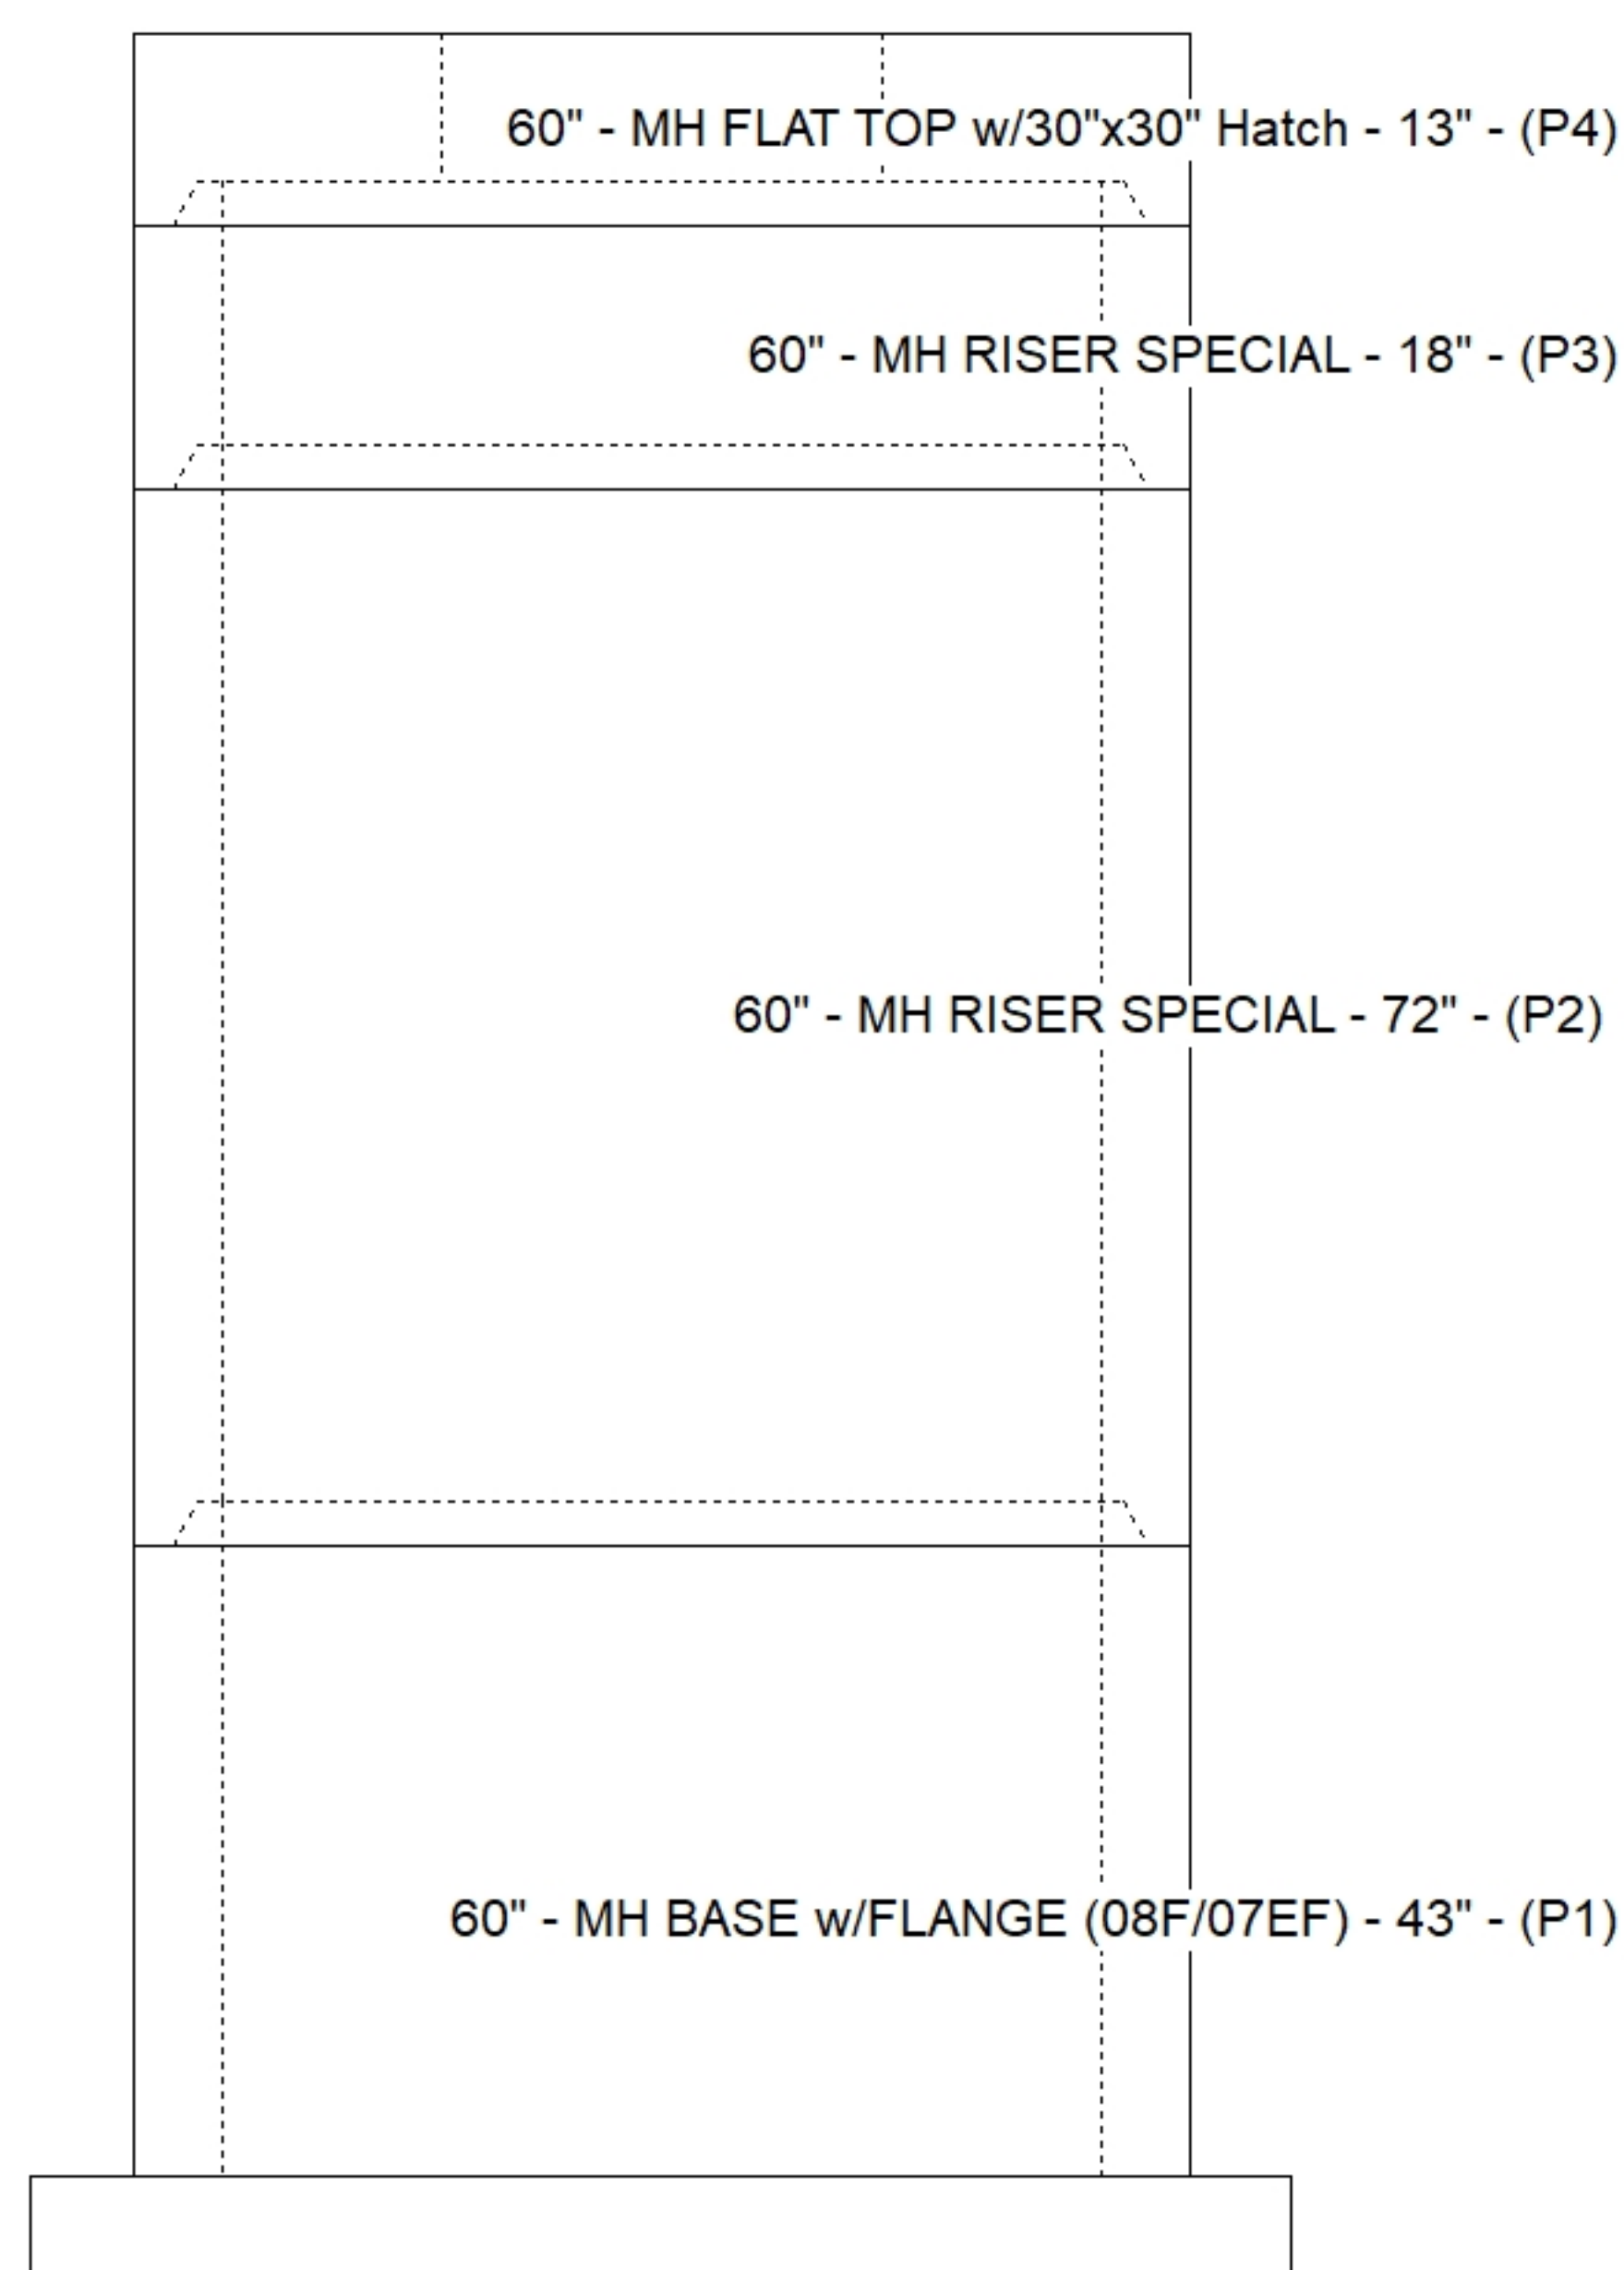

Default - Interior Dimensions

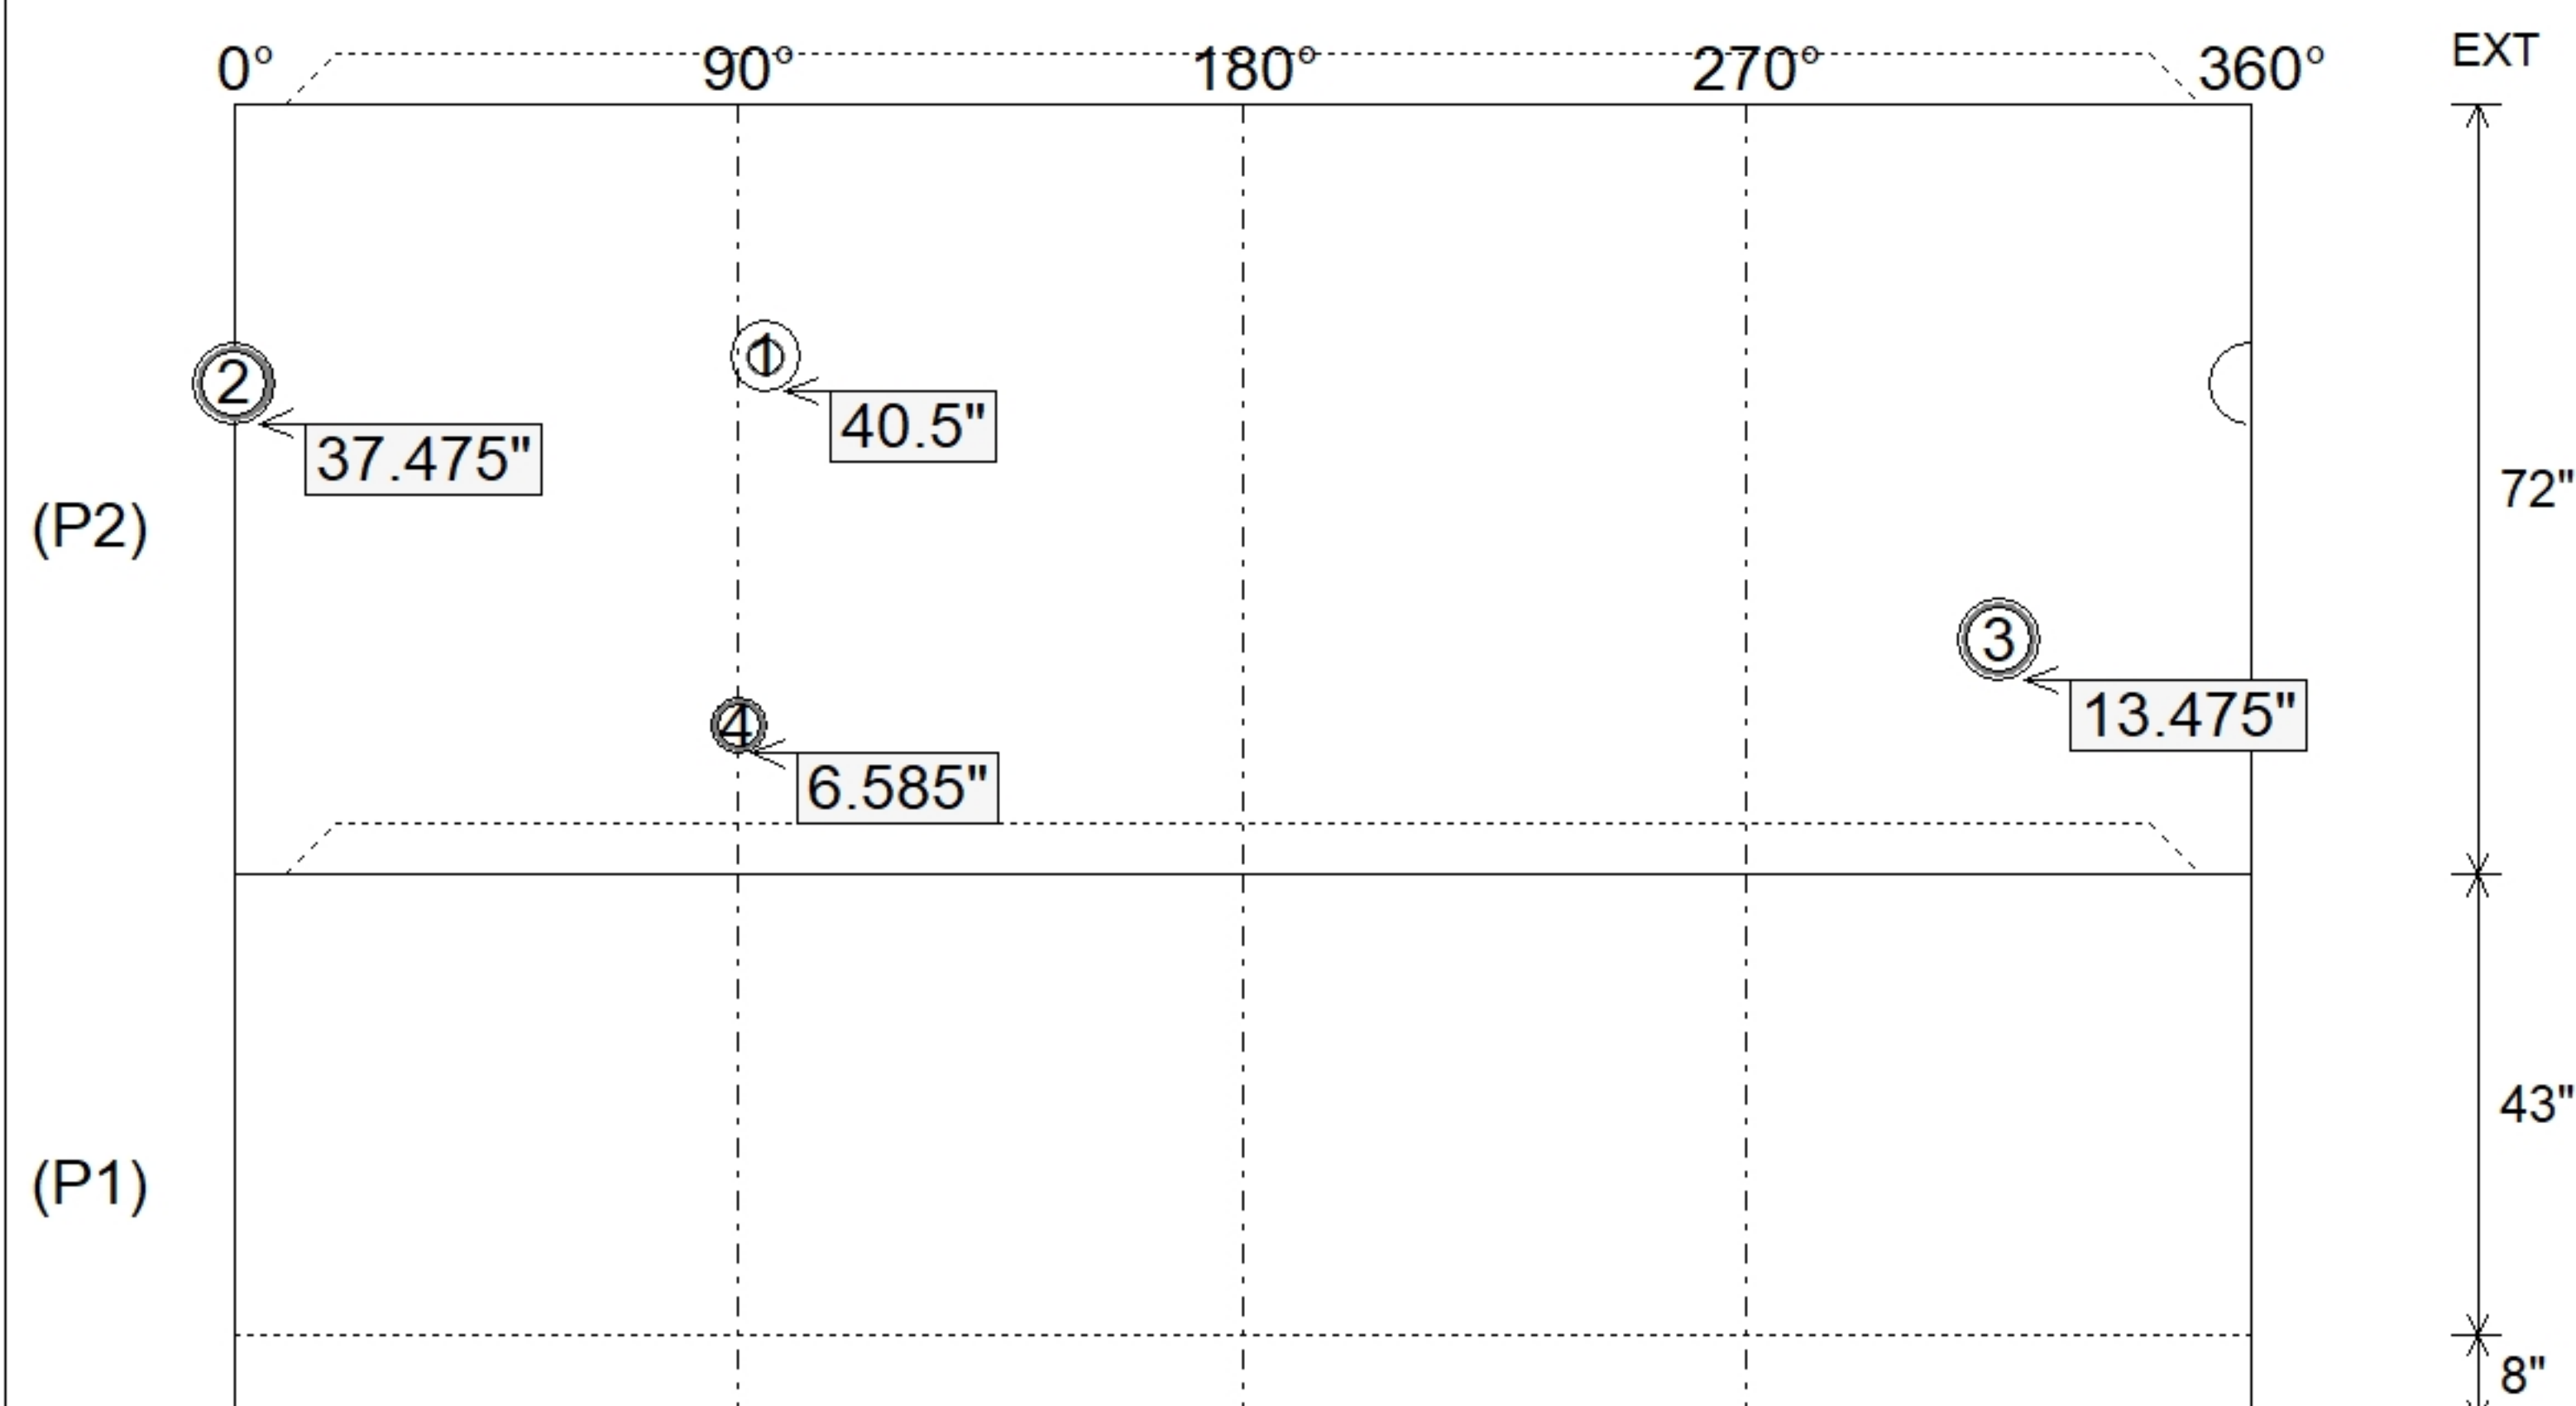

Submittal Drawing
7/9/2026 7:51:03 AM

SUBMITTAL
APPROVED BY:
