


Job Name: 25-3193 - KYTC Kenton Co Call 328 (251320) Job Location: Independence, KY Contractor: Eaton Asphalt					Plant: 100 7/1/2026 12:30:28 PM		Tech: Jared - A PC: J. Jarvis				
Structure ID: 452											
P1 BX2436-08BVF		BOX BASE 8inW, 8inF, Variable Ht									
P3) 24" x 120" - CB INLET KY A 10' TOP RIGHT - 10" P2) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT - 18" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 33" 1) CASTING - HOE KY-206 F/C (KY TY1) 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 24 1) Hole - 20 2) Hole - 8					3398 lb 5270 lb 4030 lb 206 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 12903 lb		Structure Notes: ** KYTC STATE PROJECT ** 1. HOE KY 206 F/C (KY TY1) PROVIDED BY ICAST. 2. CONCRETE = 4,000 PI AT 28 DAYS. 3. REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W. 4. KY-206 FRAME & COVER "STORM" SUPPLIED BY ICAST FRAME TO BE CAST INTO TOP PHASE TOP FLANGE SIDE UP				
Rim: 874.63' Rim to Invert: 5.09' Slack: 0.08" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	869.54'	180°	20"	18" ADS N-12	22"	Hole 24	24"	24"	-3"	0"	
Invert 2	869.54'	270°	26"	15" ADS N-12	18"	Hole 20	20"	20"	-2.5"	0"	
Invert 3	869.54'	0°	20"	18" ADS N-12	22"	Hole 24	24"	24"	-3"	0"	
Invert 4	871.46'	90°	26"	4" HDPE (perf pipe)	4.8"	Hole 8	8"	8"	21.04"	0"	
Invert 5	871.46'	270°	26"	4" HDPE (perf pipe)	4.8"	Hole 8	8"	8"	21.04"	0"	
Invert 6											
Invert 7											
Invert 8											

RIGHT-SIDE UP VIEW (int. dimensions)

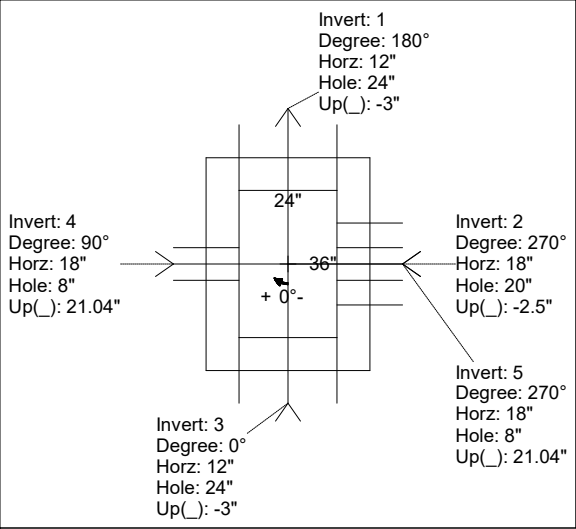

Invert: 1
Degree: 180°
Horz: 12"
Hole: 24"
Up(): -3"


Invert: 2
Degree: 270°
Horz: 18"
Hole: 20"
Up(): -2.5"

Invert: 3
Degree: 0°
Horz: 12"
Hole: 24"
Up(): -3"

Invert: 4
Degree: 90°
Horz: 18"
Hole: 8"
Up(): 21.04"

Invert: 5
Degree: 270°
Horz: 18"
Hole: 8"
Up(): 21.04"

UPSIDE-DOWN VIEW (int. dimensions)

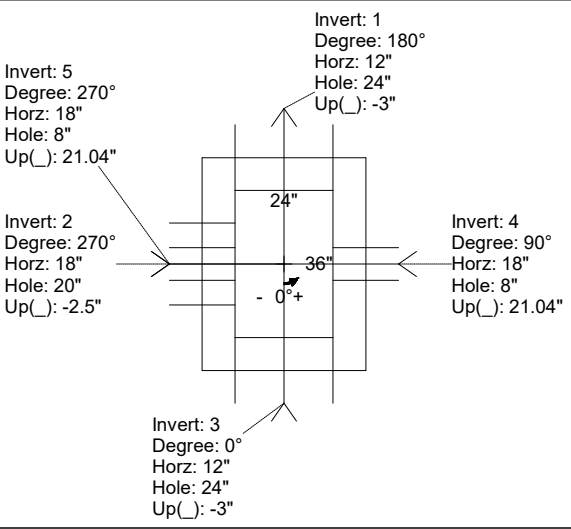

Invert: 1
Degree: 180°
Horz: 12"
Hole: 24"
Up(): -3"


Invert: 2
Degree: 270°
Horz: 18"
Hole: 20"
Up(): -2.5"

Invert: 3
Degree: 0°
Horz: 12"
Hole: 24"
Up(): -3"

Invert: 4
Degree: 90°
Horz: 18"
Hole: 8"
Up(): 21.04"

Invert: 5
Degree: 270°
Horz: 18"
Hole: 8"
Up(): 21.04"

INSIDE WALL DIMENSIONS

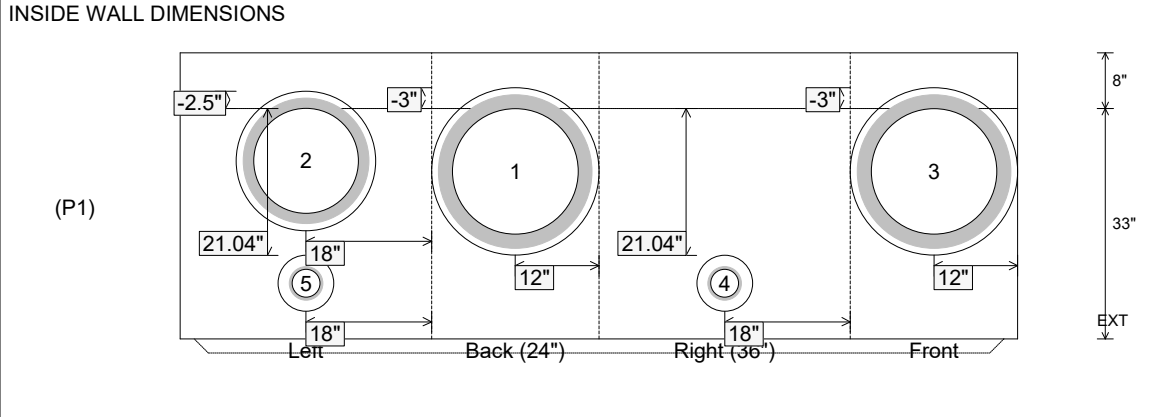

(P1)

Left Back (24") Right (36") Front

EXT

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 33" Height (Ext): 41"	Weight (Net): 4030 lb Volume (Net): 1.03cu.yd
----------------------------------	---------------------------------	--	--	--
