

Contractor: Eaton Asphalt

TECH: Jared - A


Plant: 100



Slack: 0.08"

FRAME TO BE CAST INTO TOP PHASE TOP FLANGE SIDE UP


Structure Total: 13131 lb

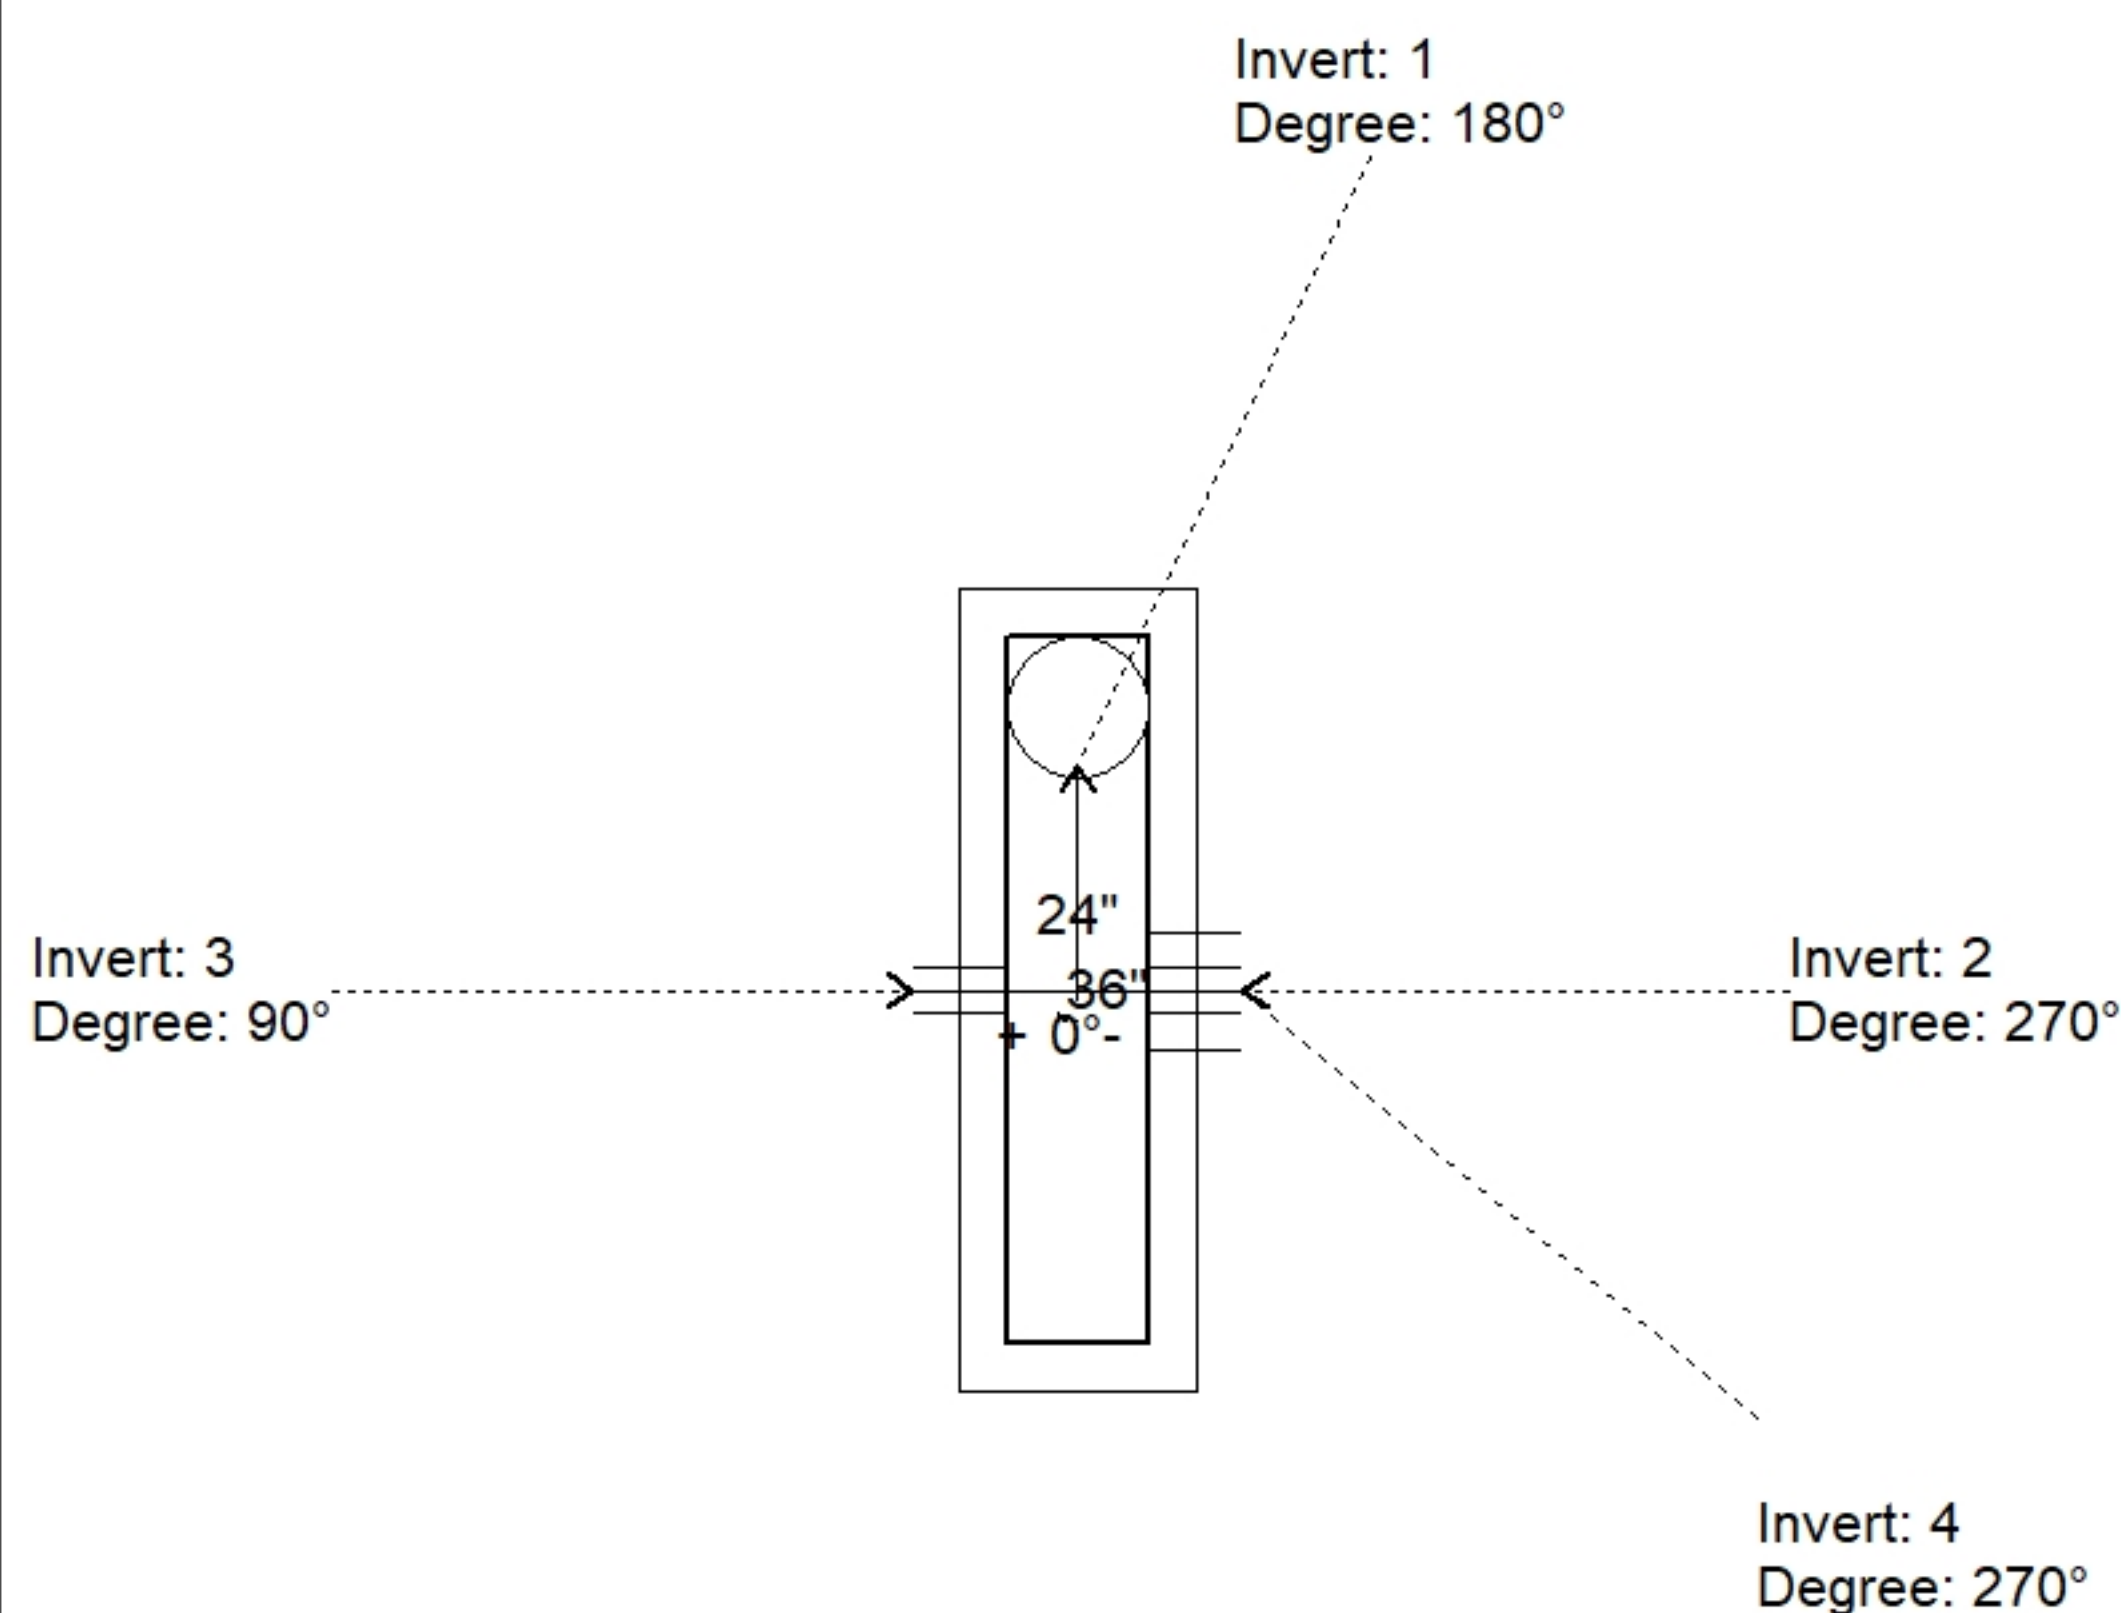

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	883'							
Reducer								
Invert 1	877.91'	180°	18" ADS N-12	22"	24"	Hole 24	-3"	P1
Invert 2	877.91'	270°	15" ADS N-12	18"	20"	Hole 20	-2.5"	P1
Invert 3	879.83'	90°	4" HDPE (perf pipe)	4.8"	8"	Hole 8	21.04"	P1
Invert 4	879.83'	270°	4" HDPE (perf pipe)	4.8"	8"	Hole 8	21.04"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 36" - BOX BASE 8inW. 8inE. Variable Ht - 33" - (P1)

Default - Interior Dimensions

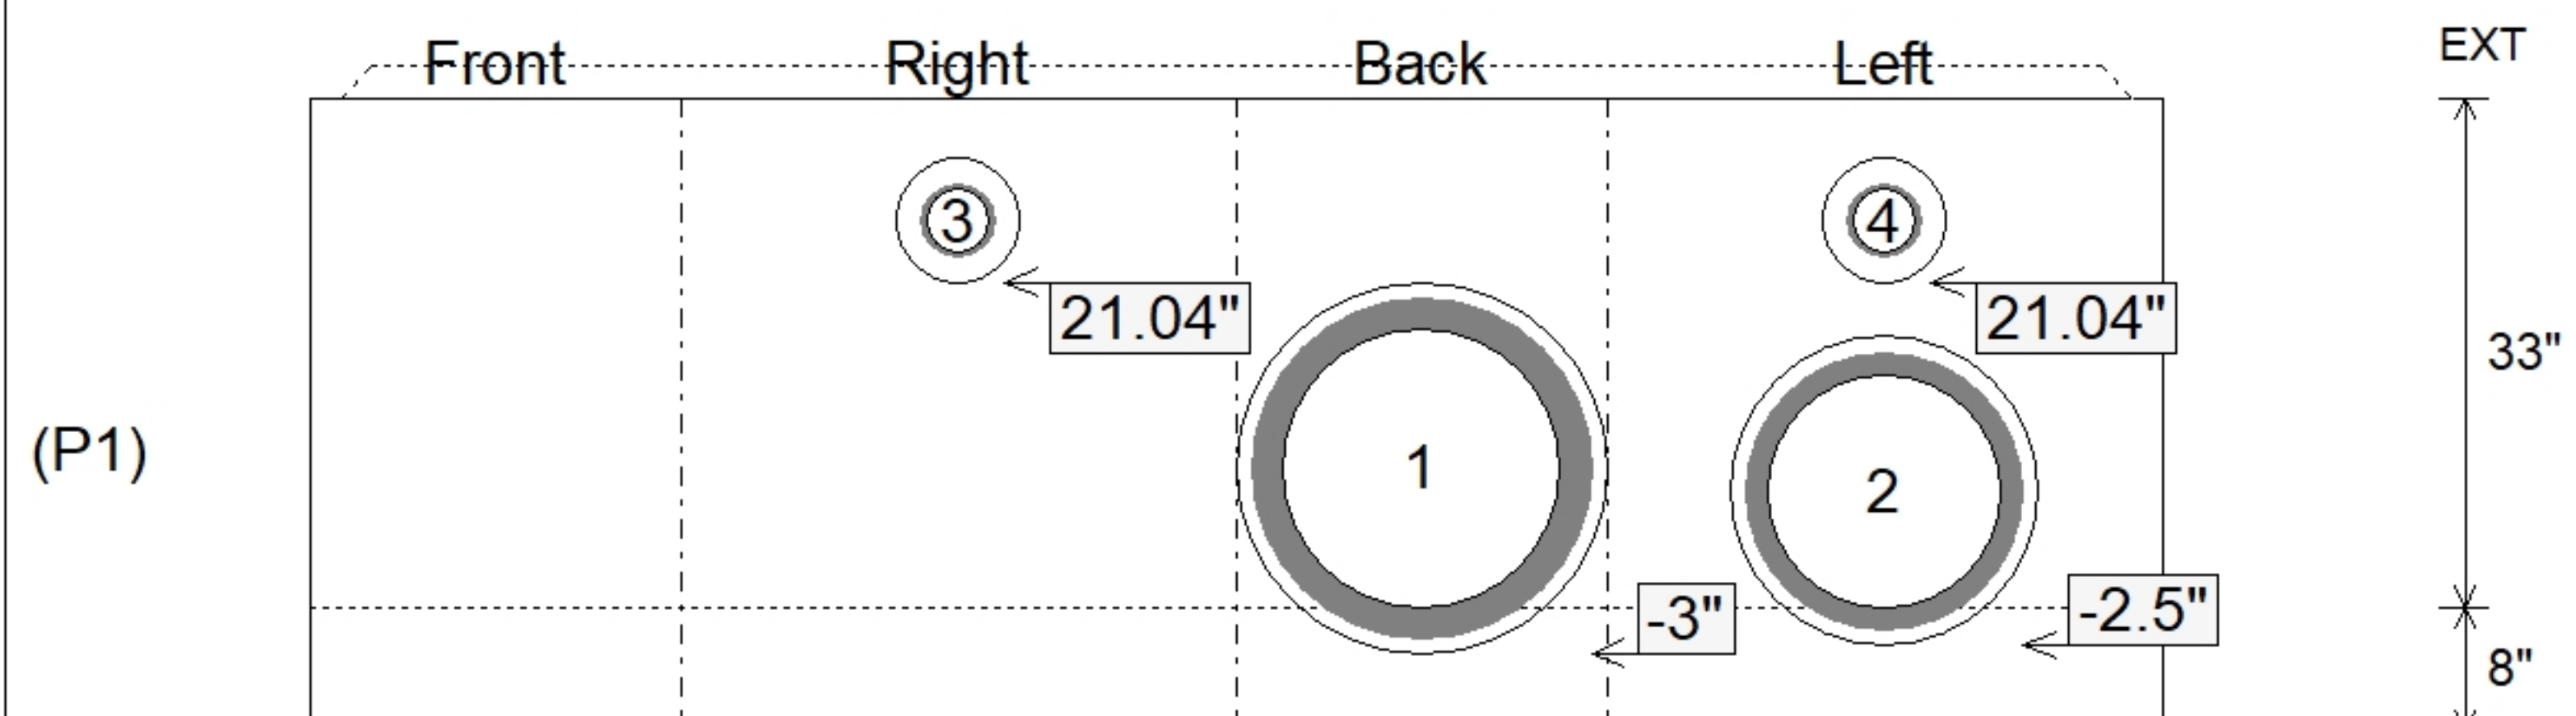

SUBMITTAL
APPROVED BY:
