

Job Name: 25-3193 - KYTC Kenton Co Call 328 (251320)  
Job Location: Independence, KY  
Contractor: Eaton Asphalt

Plant: 100

Tech: Jared - A

7/1/2026 12:29:46 PM

PC: J. Jarvis



## Structure ID: 462

**P1 BX24300808VF**

**BOX BASE 8inW, 8inF, Variable Ht**

P3) 15" x 27" - P.I.P. - BY OTHERS - 8"  
P2) 24" x 30" - CB FLAT TOP 8"W w/15"x27" HOLE - 8"  
P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht - 40"  
1) CASTING - HOE KY-230-G F/G (GRADE)  
1) 24" x 30" - Conseal CS-102 1.00"  
1) 15" x 27" - Conseal CS-102 1.00"  
1) Hole - 20  
2) Hole - 4

0 lb  
963 lb  
4767 lb  
237 lb  
0 lb  
0 lb  
0 lb  
0 lb  
0 lb  
Structure Total: 5967 lb

### Structure Notes:

**\*\*KYTC STATE PROJECT\*\***



1. HOE KY-230-G F/G (GRADE) PROVIDED BY ICAST.
2. KYTC DBI TYPE 13G / ASTM C-913 SPEC'S.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60).
  - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
  - WALLS (As .31) #5 BARS AT 12" C.C.E.W..
  - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.
5. STUB #5 BARS 12" OUT OF THE TOP OF THE SLAB  
(SPACED AT 12" CC) AROUND THE 15" X 27" HOLE

Rim: 891.27' Rim to Invert: 4.67' Slack: 0.04" Sump: 0" Step Position:


| Position | Elev    | Angle | Ext. (cw) | Pipe         | Pipe OD | Connector | Hole | Horz Size | Up ( ) | Offset |
|----------|---------|-------|-----------|--------------|---------|-----------|------|-----------|--------|--------|
| Invert 1 | 886.6'  | 0°    | 20"       | 15" ADS N-12 | 18"     | Hole 20   | 20"  | 20"       | -2.5"  | 0"     |
| Invert 2 | 889.27' | 90°   | 23"       | 4" WEEP HOLE | 4"      | Hole 4    | 4"   | 4"        | 32.04" | 0"     |
| Invert 3 | 889.27' | 270°  | 23"       | 4" WEEP HOLE | 4"      | Hole 4    | 4"   | 4"        | 32.04" | 0"     |
| Invert 4 |         |       |           |              |         |           |      |           |        |        |
| Invert 5 |         |       |           |              |         |           |      |           |        |        |
| Invert 6 |         |       |           |              |         |           |      |           |        |        |
| Invert 7 |         |       |           |              |         |           |      |           |        |        |
| Invert 8 |         |       |           |              |         |           |      |           |        |        |

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

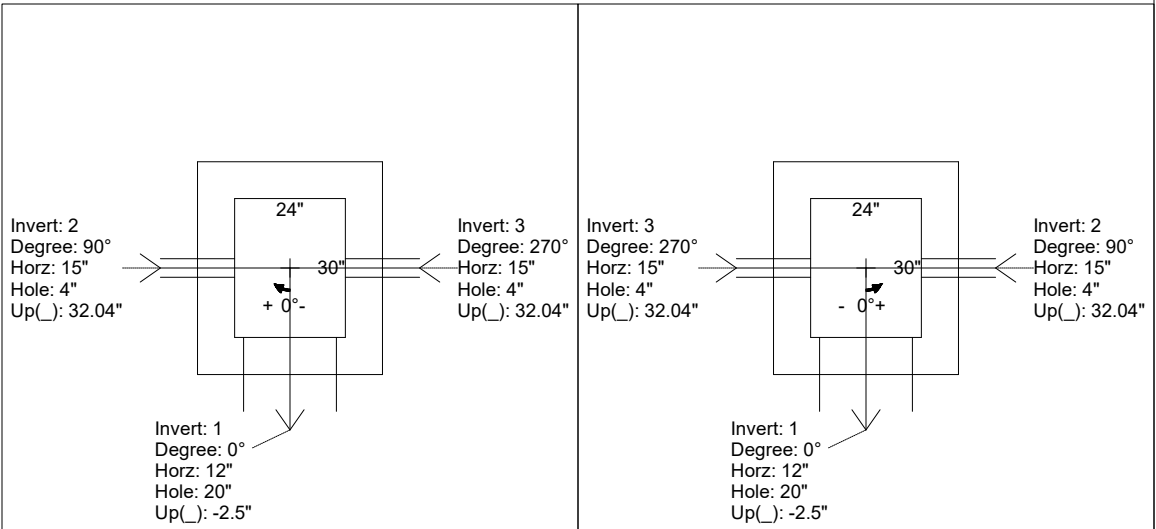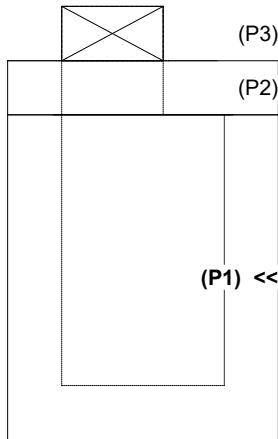

INSIDE WALL DIMENSIONS

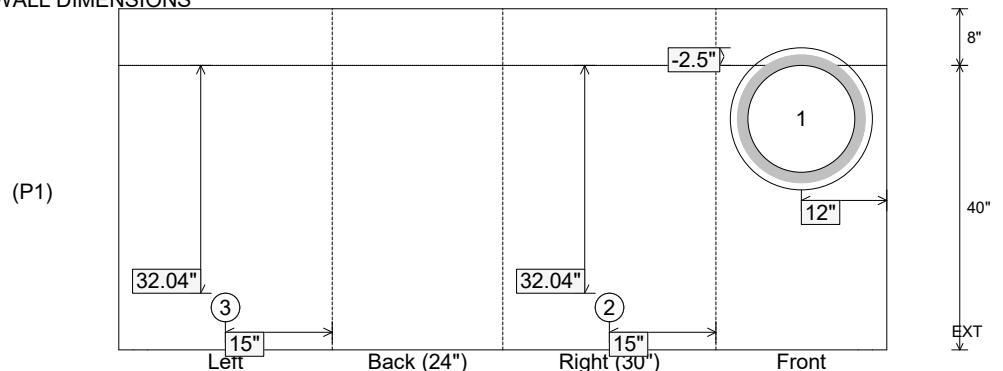

Coating (Int):  
Coating (Ext):

Seam Up: Flat  
Seam Dn: n/a

Wall Thickness: 8"  
Floor Height: 8"

Height (Int): 40"  
Height (Ext): 48"

Weight (Net): 4767 lb  
Volume (Net): 1.22cu.yd
