

Job Name: 25-3193 - KYTC Kenton Co Call 328 (251320)
Job Location: Independence, KY
Contractor: Eaton Asphalt

PC: J. Jarvis
TECH: Jared - A
Plant: 100



Structure ID: 464

Spec: KYTC
Type: CBI TYPE A (10')
Size: 24" x 36"

Rim: 899.58'
Invert: 894.49'
Rim to Invert: 5.09'

Sump: 0"
Floor (Top): 894.49'
Floor Height: 8"


Floor (Bot): 893.823'
Overall Height: 5.75'
Slack: 0.08"

Structure Notes:

- ** KYTC STATE PROJECT ****
1. PER KYTC CBI TY A / ASTM C-913 SPECS
2. CONCRETE: 4,000 PSI AT 28 DAYS
3. REINFORCEMENT:
- TOP PHASE TOP: #5 BAR @ 6" C.C. E.W. (GRADE 60)
- TOP PHASE BOTTOM: #5 BAR @ 12" C.C. E.W. (GRADE 60)
- PIPE CHAMBER: #5 BAR @ 12" C.C. E.W. (GRADE 60)
4. NO STORM INVERT
5. NO STEPS
6. KY-206 FRAME & COVER "STORM" SUPPLIED BY ICAST - FRAME TO BE CAST INTO TOP PHASE TOP FLANGE SIDE UP
7. INVERT 3 OFFSET 14" FROM CENTER


STRUCTURE SUMMARY:

P3) 24" x 120" - CB INLET KY A 10' TOP RIGHT F/G - 10" 3398 lb
P2) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT T/G - 18" 5270 lb
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht T/n - 33" 4536 lb
1) CASTING - HOE KY-206 F/C (KY TY1) 206 lb
1) This Structure Includes a Cast-in Item - KY-206 Frame (Supplied by iCast) 0 lb
1) 24" x 36" - Con seal CS-102 1.00" 0 lb
1) Hole - 24 0 lb
2) Hole - 8 0 lb
Structure Total: 13410 lb

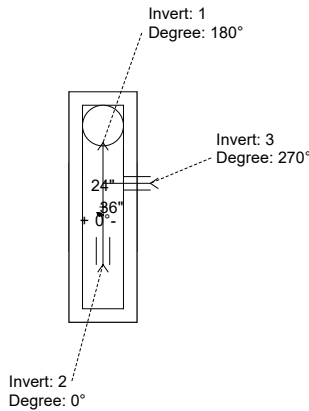

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (L)	Ref
Rim	899.58'							
Reducer								
Invert 1	894.49'	180°	18" ADS N-12	22"	24"	Hole 24	-3"	P1
Invert 2	896.41'	0°	4" HDPE (perf pipe)	4.8"	8"	Hole 8	21"	P1
Invert 3	896.41'	270°	4" HDPE (perf pipe)	4.8"	8"	Hole 8	21"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Cast (Int. Dim.) - Interior Dimensions

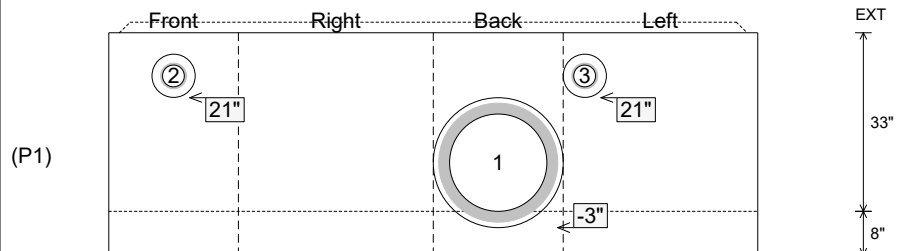

Submittal Drawing
6/4/2026 4:48:06 PM

SUBMITTAL
APPROVED BY:
