

Contractor: Eaton Asphalt

TECH: Jared - A

Plant: 100



Size: 36" x 36"

Rim to Invert: 3.27'

Floor Height: 8"


Slack: 0.24"

1. HOE KY-316 SET (DB 1) PROVIDED BY ICAST.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. REINFORCING PER ASTM A615 (GRADE 60).
 - WALLS (As .31) #5 BARS AT 12" C.C.E.W.
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.
4. STUB #5 BARS 20" OUT TOP OF WALLS (SPA@12"C/C)

2) Hole - 4



0 lb
4583 lb
317 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 4900 lb

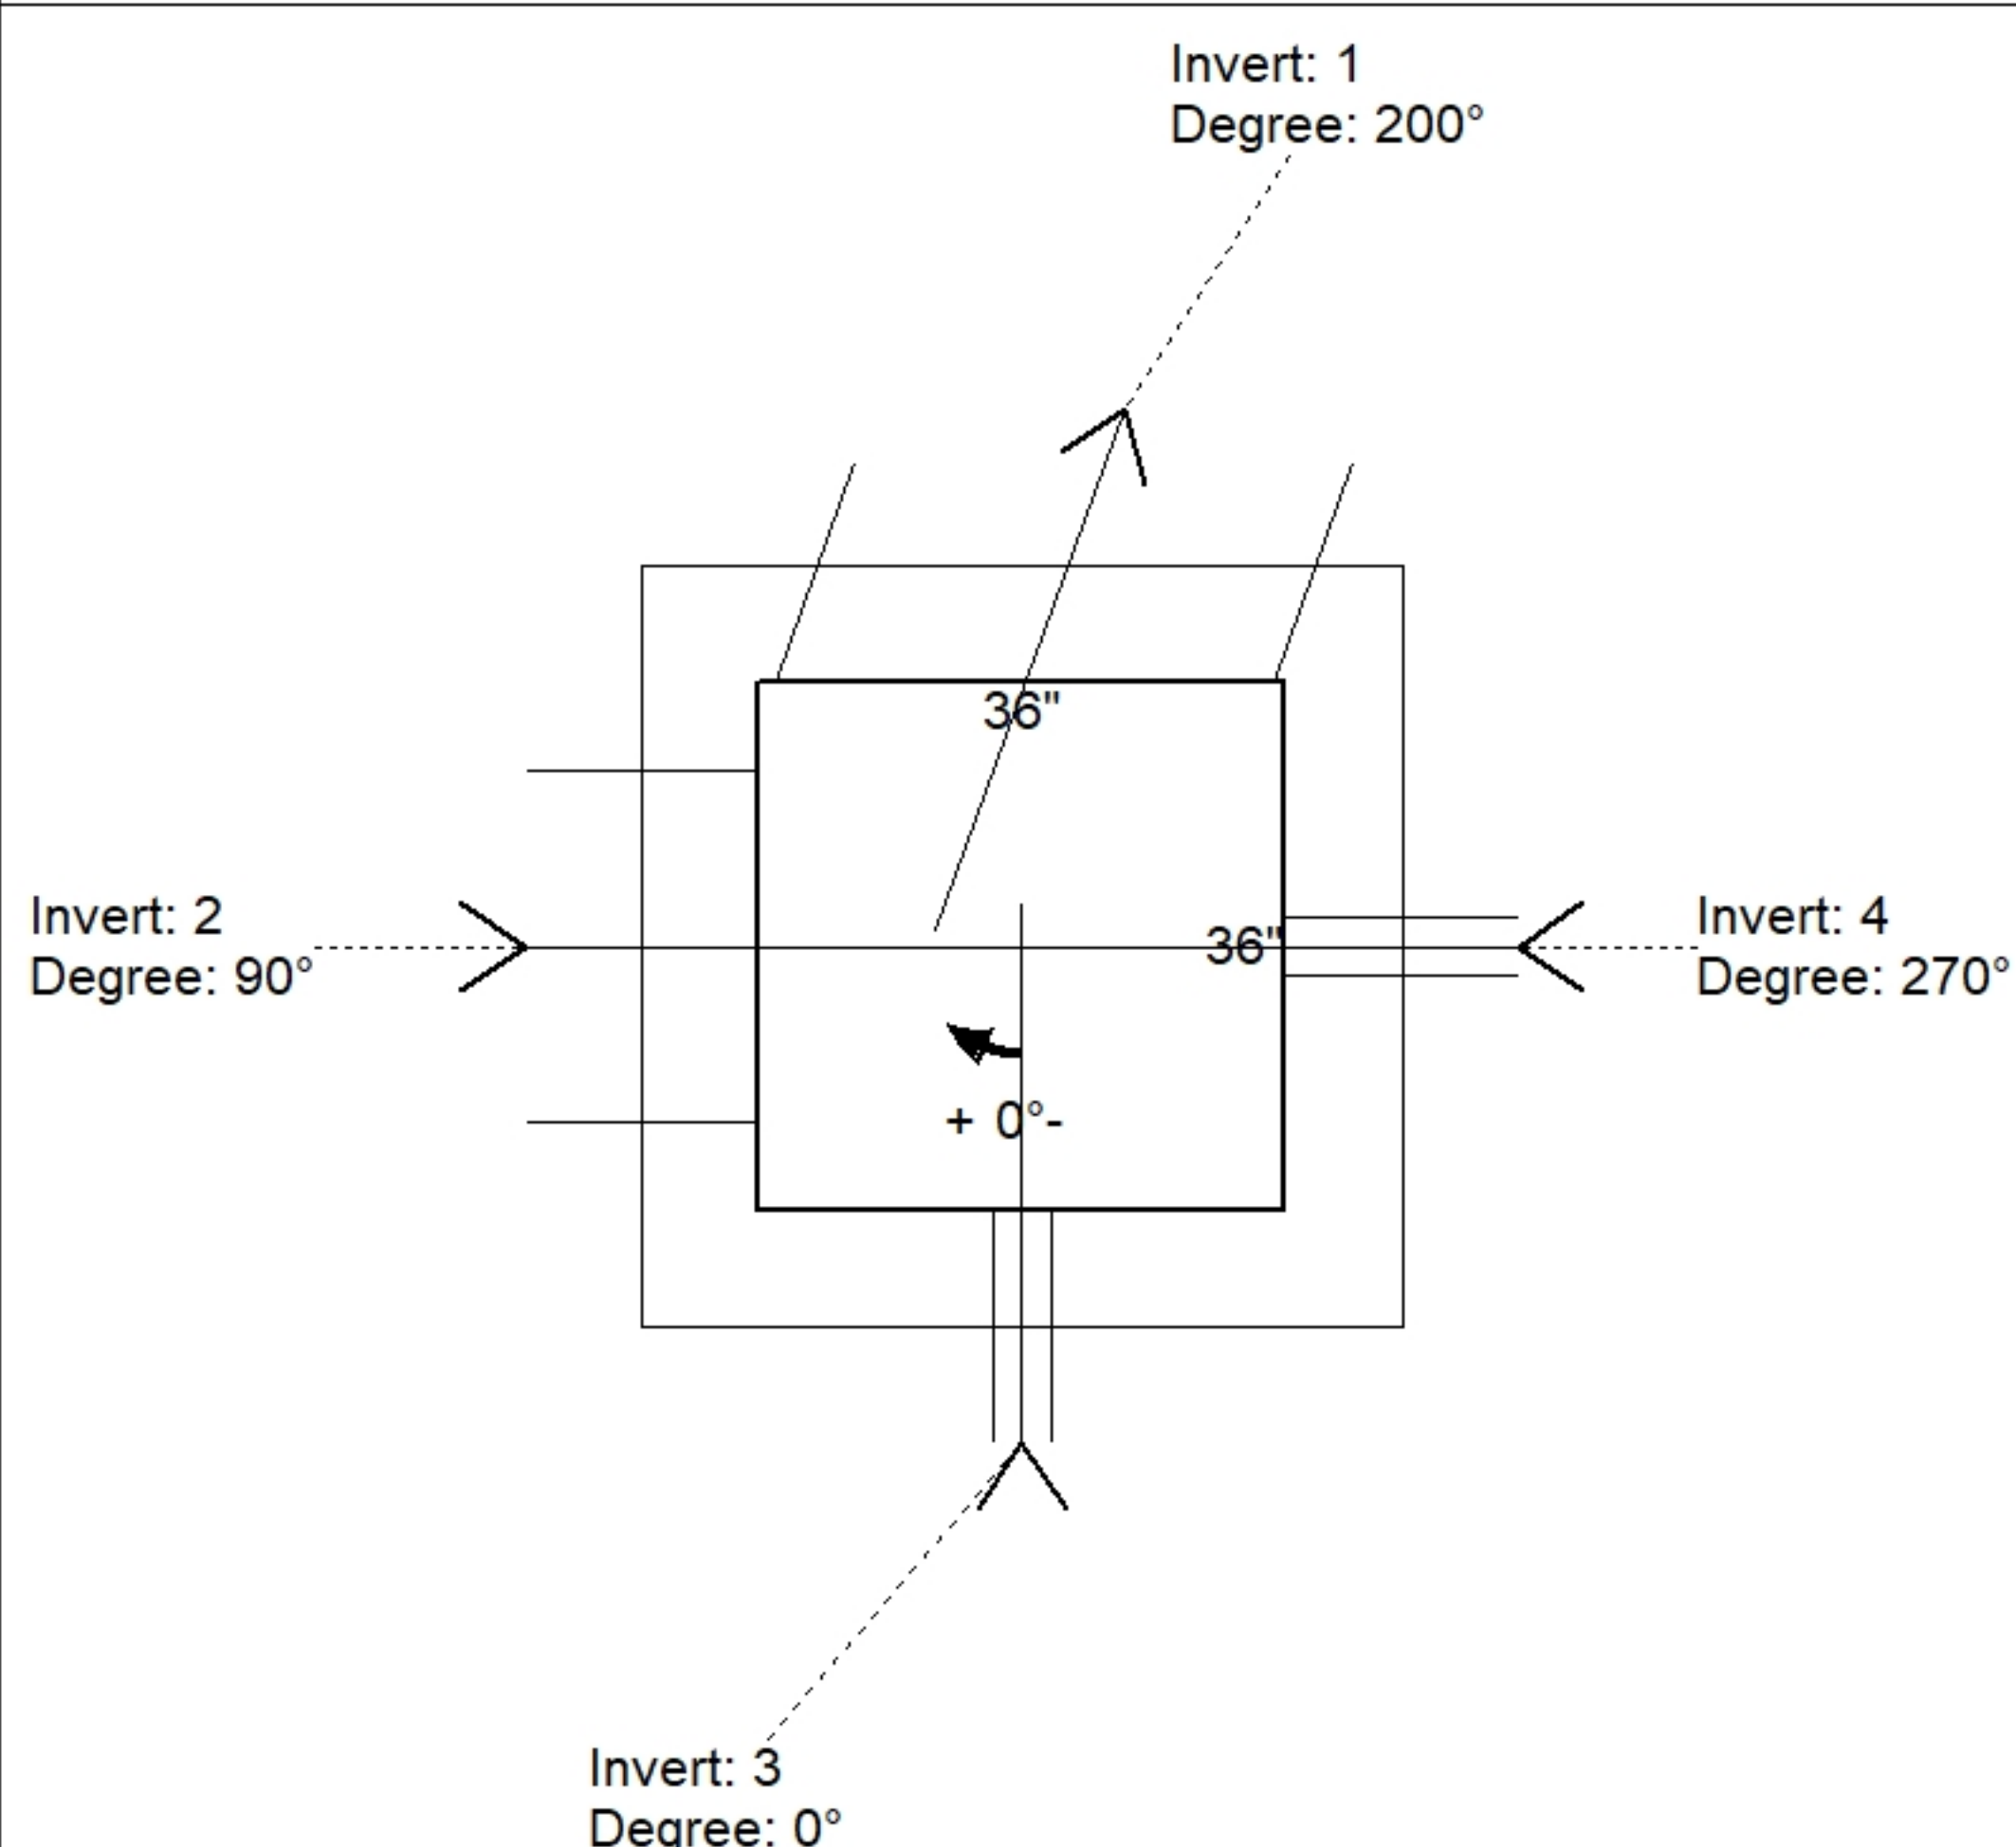

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	891.29'							
Reducer								
Invert 1	888.02'	200°	24" ADS N-12	28"	32"	Hole 32	-4"	P1
Invert 2	888.02'	90°	18" ADS N-12	22"	24"	Hole 24	-3"	P1
Invert 3	889.89'	0°	4" WEEP HOLE	4"	4"	Hole 4	22.44"	P1
Invert 4	889.89'	270°	4" WEEP HOLE	4"	4"	Hole 4	22.44"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

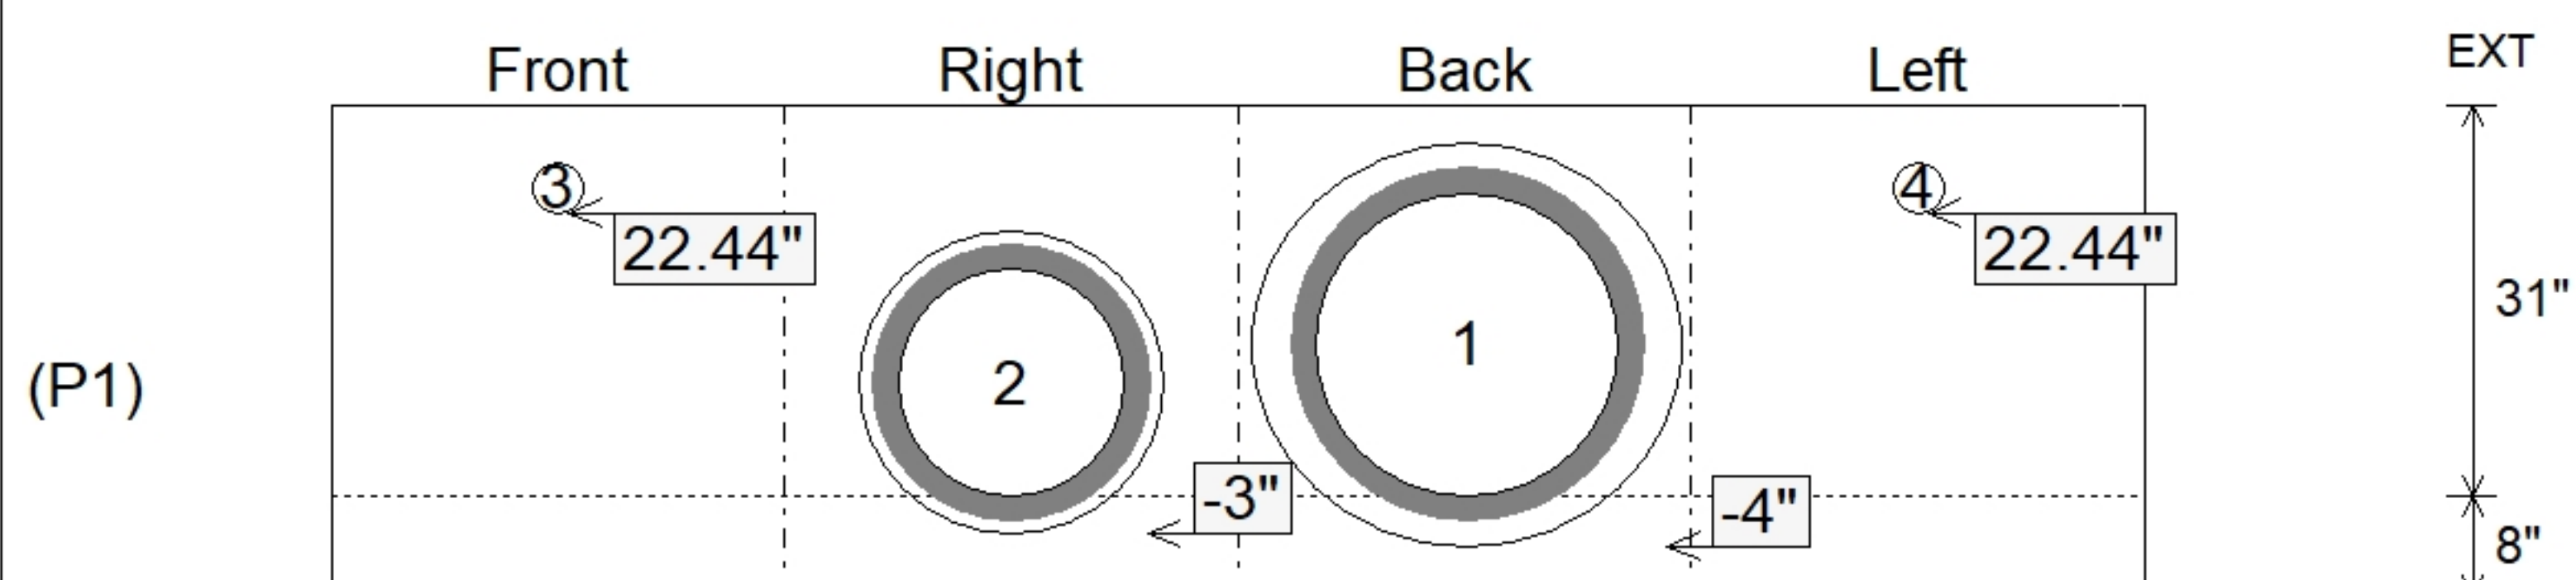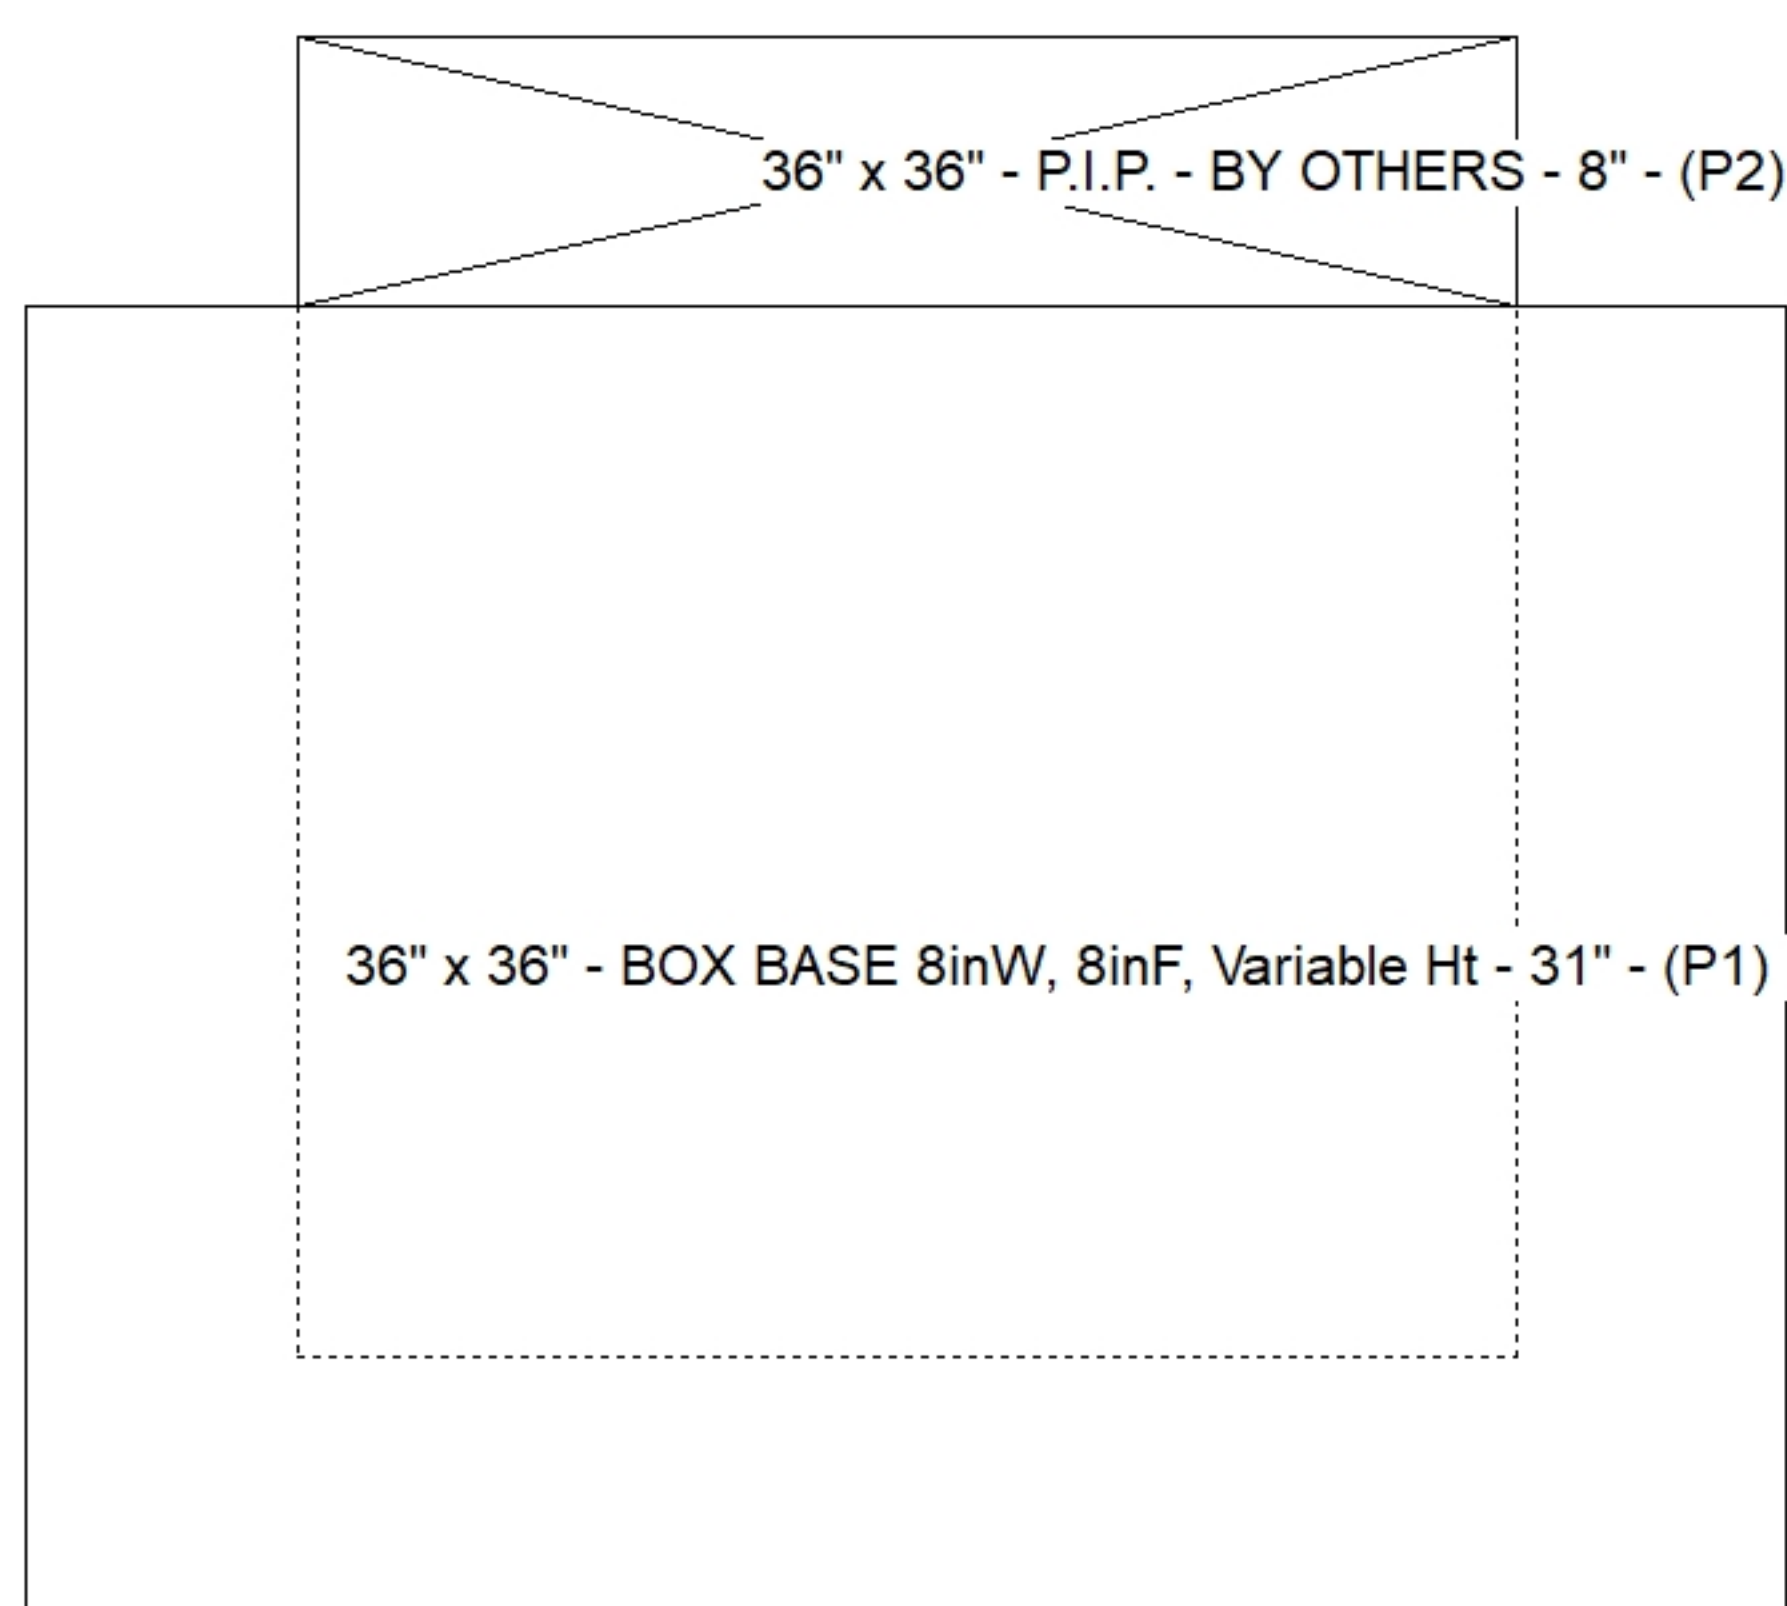

Submittal Drawing
7/10/2026 11:53:58 AM

SUBMITTAL
APPROVED BY:
