

Job Name: 25-3193 - KYTC Kenton Co Call 328 (251320)
Job Location: Independence, KY
Contractor: Eaton Asphalt

PC: J. Jarvis
 TECH: Jared - A
 Plant: 100



Structure ID: **531**

Spec: KYTC
 Type: CBI TYPE A (10')
 Size: 24" x 36"

Rim: 831.78'
 Invert: 826.19'
 Rim to Invert: 5.59'

Sump: 0"
 Floor (Top): 826.19'
 Floor Height: 8"


Floor (Bot): 825.523'
 Overall Height: 6.25'
 Slack: 0.08"

Structure Notes:

- ** KYTC STATE PROJECT ****
 1. PER KYTC CBI TY A / ASTM C-913 SPECS
 2. CONCRETE: 4,000 PSI AT 28 DAYS
 3. REINFORCEMENT:
 - TOP PHASE TOP: #5 BAR @ 6" C.C. E.W. (GRADE 60)
 - TOP PHASE BOTTOM: #5 BAR @ 12" C.C. E.W. (GRADE 60)
 - PIPE CHAMBER: #5 BAR @ 12" C.C. E.W. (GRADE 60)
 4. NO STORM INVERT
 5. NO STEPS
 6. KY-206 FRAME & COVER "STORM" SUPPLIED BY ICAST - FRAME TO BE CAST INTO TOP PHASE TOP FLANGE SIDE UP



STRUCTURE SUMMARY:

P3) 24" x 120" - CB INLET KY A 10' TOP RIGHT F/G - 10" 3398 lb
 P2) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT T/G - 18" 5270 lb
 P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht T/n - 39" 4701 lb
 1) CASTING - HOE KY-206 F/C (KY TY1) 206 lb
 1) This Structure Includes a Cast-in Item - KY-206 Frame (Supplied by iCast) 0 lb
 1) 24" x 36" - Conseal CS-102 1.00" 0 lb
 2) Hole - 24 0 lb
 2) Hole - 8 0 lb
Structure Total: 13575 lb

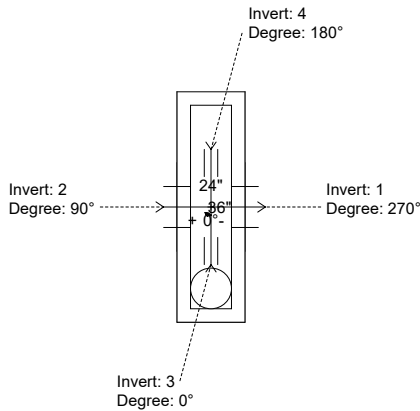

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (L)	Ref
Rim	831.78'							
Reducer								
Invert 1	826.19'	270°	18" ADS N-12	22"	24"	Hole 24	-3"	P1
Invert 2	826.19'	90°	18" ADS N-12	22"	24"	Hole 24	-3"	P1
Invert 3	828.61'	0°	4" HDPE (perf pipe)	4.8"	8"	Hole 8	27"	P1
Invert 4	828.61'	180°	4" HDPE (perf pipe)	4.8"	8"	Hole 8	27"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Cast (Int. Dim.) - Interior Dimensions

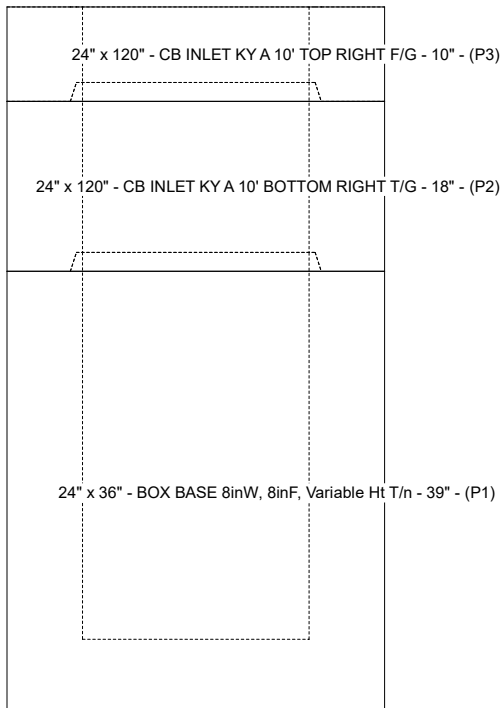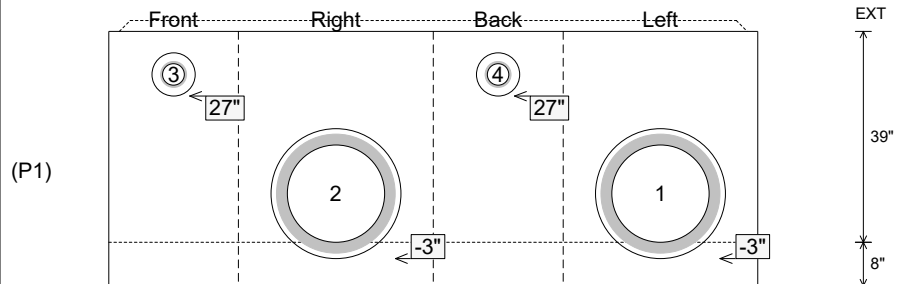

Submittal Drawing
 6/4/2026 4:49:15 PM

SUBMITTAL
 APPROVED BY:
