




Job Name: 25-3193 - KYTC Kenton Co Call 328 (251320) Job Location: Independence, KY Contractor: Eaton Asphalt					Plant: 100 6/4/2026 4:51:09 PM		Tech: Jared - A PC: J. Jarvis				
Structure ID: 572											
P1		BX2436-08BVF		BOX BASE 8inW, 8inF, Variable Ht T/n							
P3) 24" x 120" - CB INLET KY A 10' TOP LEFT F/G - 10" P2) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT T/G - 18" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht T/n - 33" 1) CASTING - HOE KY-206 F/C (KY TY1) 1) This Structure Includes a Cast-in Item - KY-206 Frame (Supplied by iCast) 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 24 1) Hole - 20 2) Hole - 8					3400 lb 5270 lb 4165 lb 206 lb 0 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 13040 lb		Structure Notes: ** KYTC STATE PROJECT ** 1. PER KYTC CBI TY A / ASTM C-913 SPECS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. NO STORM INVERT 5. NO STEPS 6. KY-206 FRAME & COVER "STORM" SUPPLIED BY ICAST - FRAME TO BE CAST INTO TOP PHASE TOP FLANGE SIDE UP 7. INVERTS 4 & 5 OFFSET 14" FROM CENTER OF WALL				
Rim: 860.65' Rim to Invert: 5.09' Slack: 0.08" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	855.56'	0°	20"	18" ADS N-12	22"	Hole 24	24"	24"	-3"	0"	
Invert 2	855.56'	180°	20"	18" ADS N-12	22"	Hole 24	24"	24"	-3"	0"	
Invert 3	855.56'	270°	26"	15" ADS N-12	18"	Hole 20	20"	20"	-2.5"	0"	
Invert 4	857.48'	90°	12"	4" HDPE (perf pipe)	4.8"	Hole 8	8"	8"	21"	-14"	
Invert 5	857.48'	270°	12"	4" HDPE (perf pipe)	4.8"	Hole 8	8"	8"	21"	-14"	
Invert 6											
Invert 7											
Invert 8											

RIGHT-SIDE UP VIEW (int. dimensions)

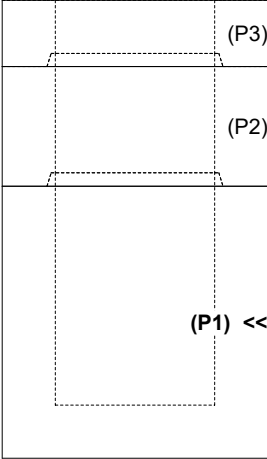

UPSIDE-DOWN VIEW (int. dimensions)

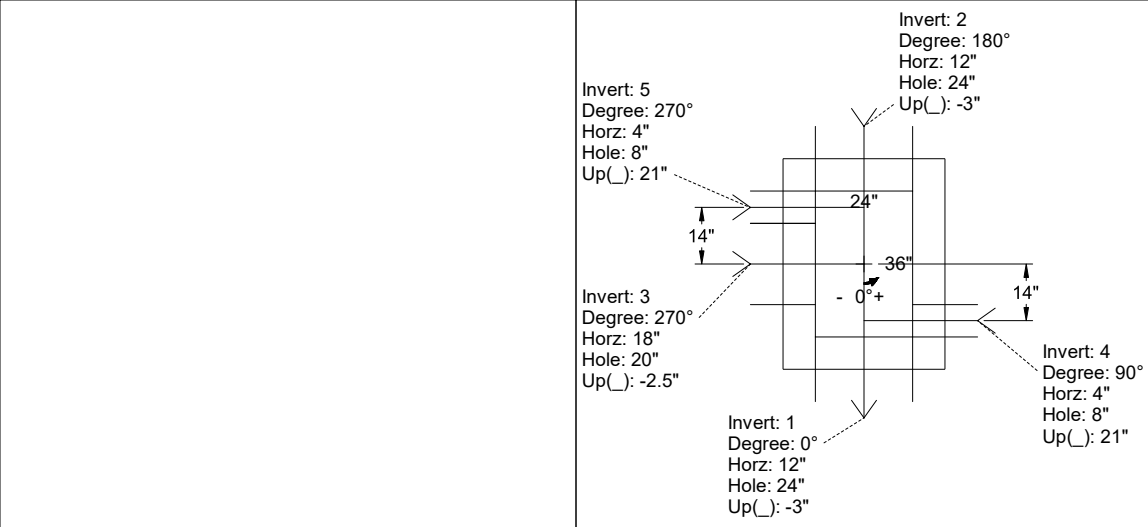

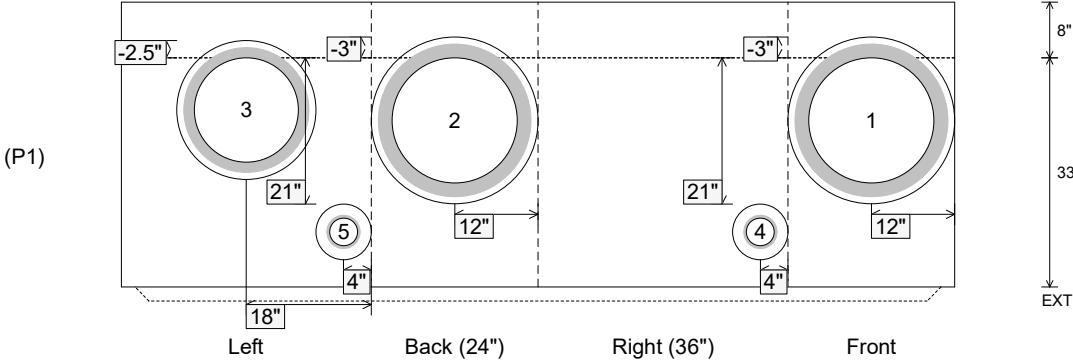INSIDE WALL DIMENSIONS				
				
Left		Back (24")		Right (36")
				Front

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 33" Height (Ext): 41"	Weight (Net): 4165 lb Volume (Net): 1.06cu.yd
----------------------------------	---------------------------------	--	--	--
