

Job Name: 25-3193 - KYTC Kenton Co Call 328 (251320)
Job Location: Independence, KY
Contractor: Eaton Asphalt

Plant: 100
6/30/2026 2:46:44 PM

Tech: Jared - A
PC: J. Jarvis



Structure ID: 603

P4 MH048CN36

ECC CONE w/ 24" HOLE



P5) 24" - CASTING HEIGHT - 8"
P4) 48" - ECC CONE w/ 24" HOLE - 36"
P3) 48" - MH RISER - 36"
P2) 48" - MH RISER - 60"
P1) 48" - MH BASE Custom Ht - 70"
1) CASTING - HOE KY-510 F/C (KY TY.2)
3) 48" - Conseal CS-102 1.00"
3) Hole - 24
17) MH Step ML-10-TDS-NCR - 10"

0 lb
3000 lb
2515 lb
4192 lb
5629 lb
510 lb
0 lb
0 lb
0 lb

15845 lb

Structure Notes: .
KYTC STATE PROJECT
1. HOE KY-510 F/C (KY TY2) PROVIDED BY ICAST.
2. PER KYTC MH A / ASTM C478 SPEC'S.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60.)
- CONE (As .62)
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Structure Total:

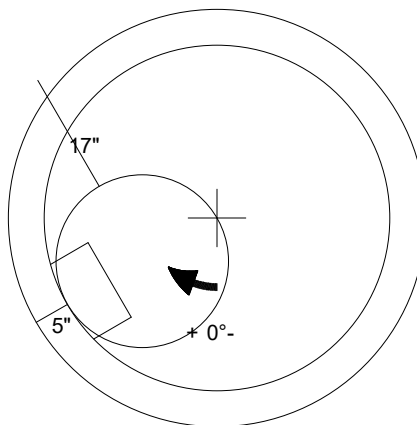

48" - ECC CONE w/ 24" HOLE - 36" - (P4)

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 36"

Weight (Net): 3000 lb
Volume (Net): 0.5cu.yd
