




Job Name: 25-3241P2 - Buck Hills Subdivision Job Location: Lawrenceburg, KY 40342 Contractor: Edmonson Plumbing & Heating Supply					Plant: 100 7/24/2026 12:43:53 PM		Tech: Jared - A PC: C. Goff				
Structure ID: CB 8											
P1 MH048BA30		MH BASE									
P3) 24" x 36" - CASTING HEIGHT - 6" P2) 48" - MH FLAT TOP w/24"x36" Hole - 12" P1) 48" - MH BASE - 30" 1) CASTING - HOE 525 LV SET (F/G/H) 1) 48" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 20" Structure Total: 4897 lb						0 lb 1300 lb 3155 lb 442 lb 0 lb 0 lb 0 lb ----- 4897 lb		Structure Notes: 1. HOE 525 LV SET (F/G/H) PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 808.17'		Rim to Invert: 4'		Slack: 1.3"		Sump: 1.3"		Step Position: 125°			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	804.17'	0°	0"	15" HDPE	17.6"	Hole 20	20"	20.629"	0"	0"	
Invert 2	804.17'	250°	126.536"	15" HDPE	17.6"	Hole 20	20"	20.629"	0"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

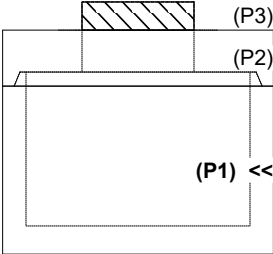


RIGHT-SIDE UP VIEW (int. dimensions)

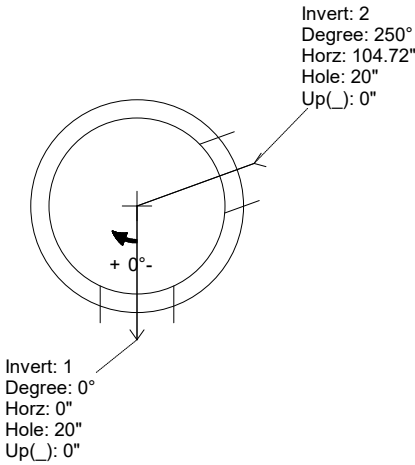

UPSIDE-DOWN VIEW (int. dimensions)

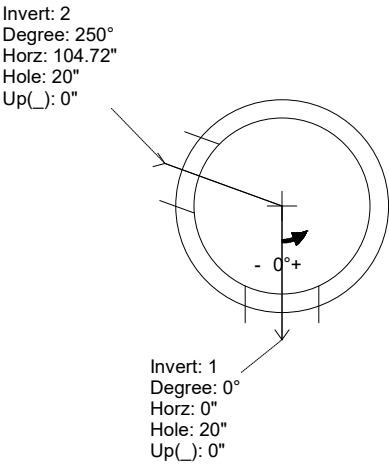

INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 30" Height (Ext): 36"	Weight (Net): 3155 lb Volume (Net): 0.81cu.yd
----------------------------------	---------------------------------	--	--	--
