

Job Name: 25-3241P2 - Buck Hills Subdivision
Job Location: Lawrenceburg, KY 40342
Contractor: Edmonson Plumbing & Heating Supply

Plant: 100

7/24/2026 12:44:47 PM

Tech: Jared - A

PC: C. Goff



Structure ID: CB 8

P2 MH048LD12-24X36RECT

MH FLAT TOP w/24"x36" Hole

- P3) 24" x 36" - CASTING HEIGHT - 6"
P2) 48" - MH FLAT TOP w/24"x36" Hole - 12"
P1) 48" - MH BASE - 30"
1) CASTING - HOE 525 LV SET (F/G/H)
1) 48" - Conseal CS-102 1.00"
1) 24" x 36" - Conseal CS-102 1.00"
2) Hole - 20



Structure Total:

0 lb
1300 lb
3155 lb
442 lb
0 lb
0 lb
0 lb

4897 lb

Structure Notes:

1. HOE 525 LV SET (F/G/H) PROVIDED BY ICAST.
2. PER ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60).
 - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
 - RISER/WALLS (As .12)
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

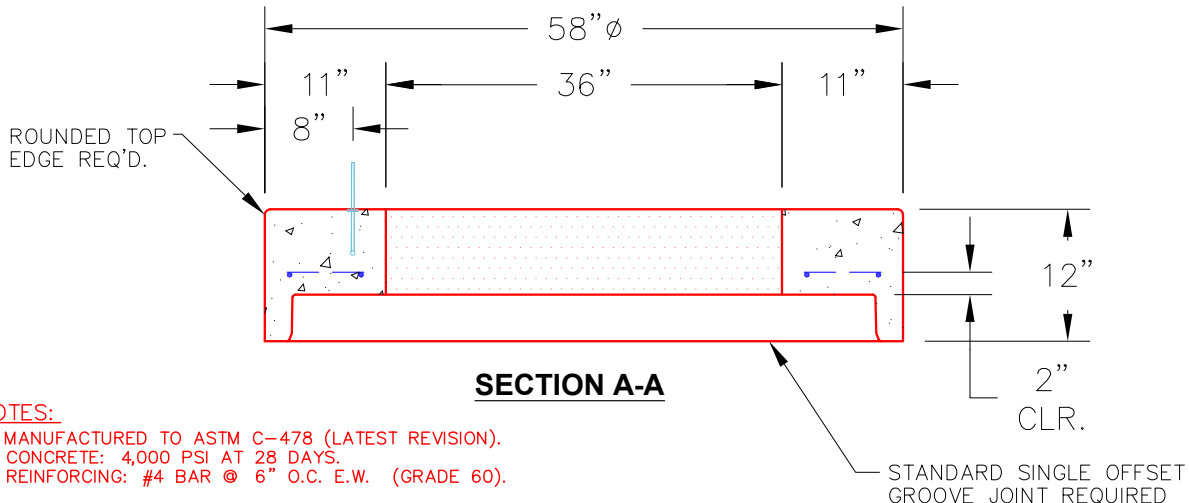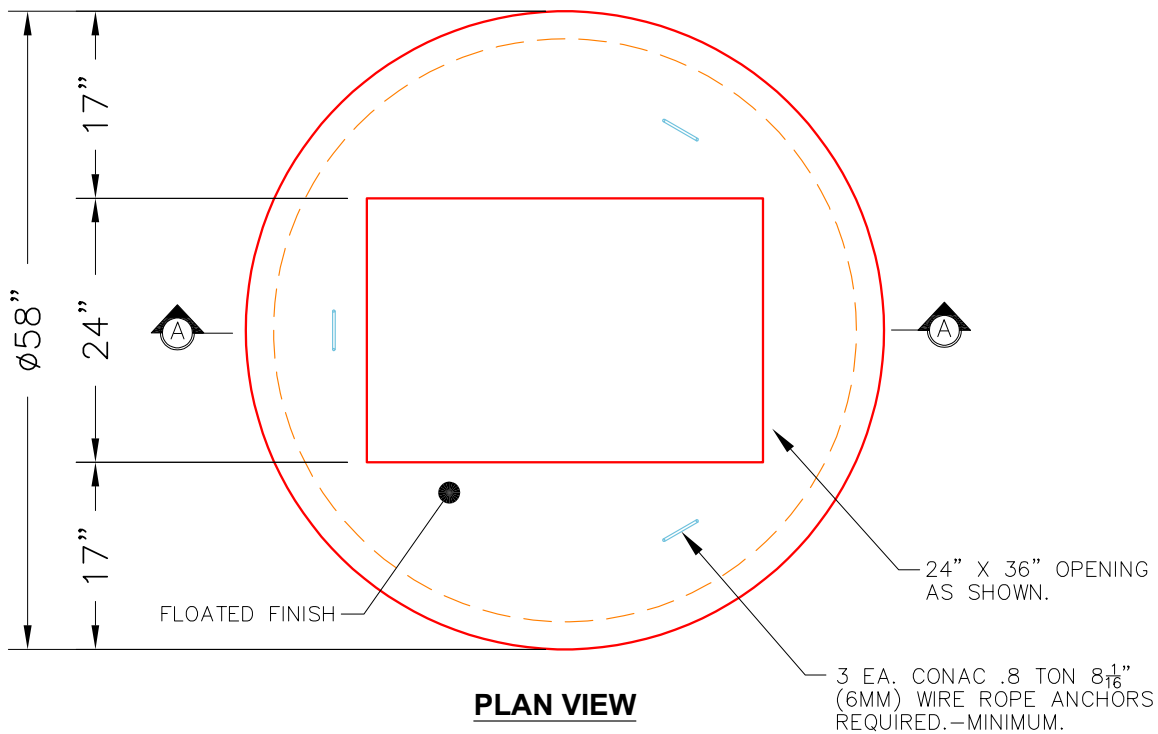

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #4 BAR @ 6" O.C. E.W. (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 12"

Weight (Net): 1300 lb
Volume (Net): 0.46cu.yd
