




Job Name: 25-3241P2 - Buck Hills Subdivision Job Location: Lawrenceburg, KY 40342 Contractor: Edmonson Plumbing & Heating Supply					Plant: 100 7/24/2026 12:43:55 PM		Tech: Jared - A PC: C. Goff				
Structure ID: MH B1											
P1		MH048BAEVF									
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE - 30" P1) 48" - MH BASE w/FLANGE (08F/08EF) - 25" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) CASTING - HOE MC-420 F/C Sanitary 1) 48" - Conseal CS-231 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 NYLO 1) Quik-Lok - QL-08-C 1) PSX - 8QRS-S NYLO					0 lb 2050 lb 4526 lb 1440 lb 0 lb 0 lb 340 lb 0 lb 0 lb 8 lb 1 lb 6 lb ----- Structure Total: 8372 lb		Structure Notes: 1. HOE MC-420 F/C SANITARY PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 786.25'		Rim to Invert: 5'		Slack: 0"		Sump: 2"		Step Position: 0°			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	781.25'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"	
Invert 2	781.35'	260°	131.598"	8" PVC SDR35	8.5"	Quik-Lok QL-08-C	10.75"	10.842"	1.825"	0"	
Invert 3	781.5'	210°	106.291"	4" PVC SDR35	4.25"	PSX 8QRS-S NYLO	8"	8.038"	3"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

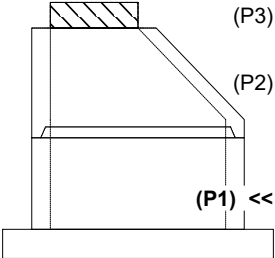


RIGHT-SIDE UP VIEW (int. dimensions)

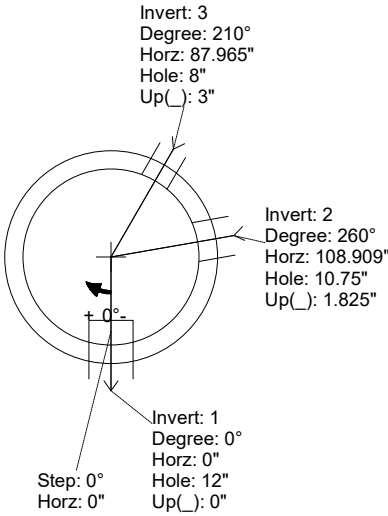

UPSIDE-DOWN VIEW (int. dimensions)

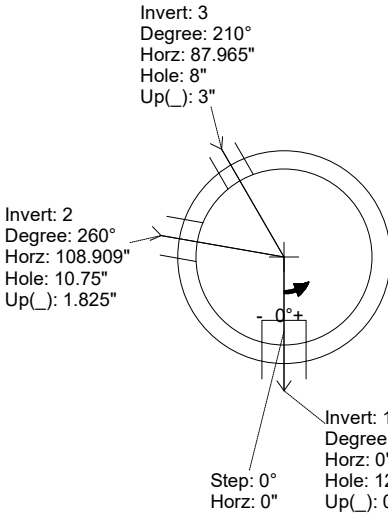


INSIDE WALL DIMENSIONS




Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 8"	Height (Int): 25" Height (Ext): 33"	Weight (Net): 4526 lb Volume (Net): 1.16cu.yd
----------------------------------	---------------------------------	--	--	--


Job Name: 25-3241P2 - Buck Hills Subdivision Job Location: Lawrenceburg, KY 40342 Contractor: Edmonson Plumbing & Heating Supply					Plant: 100 7/24/2026 12:43:55 PM		Tech: Jared - A PC: C. Goff				
Structure ID: MH B1											
P1 MH048BAEVF		MH BASE w/FLANGE (08F/08EF)									
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE - 30" P1) 48" - MH BASE w/FLANGE (08F/08EF) - 25" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) CASTING - HOE MC-420 F/C Sanitary 1) 48" - Conseal CS-231 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 NYLO 1) Quik-Lok - QL-08-C 1) PSX - 8QRS-S NYLO					0 lb 2050 lb 4526 lb 1440 lb 0 lb 0 lb 340 lb 0 lb 0 lb 8 lb 1 lb 6 lb		Structure Notes: 1. HOE MC-420 F/C SANITARY PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W. INVERT CHANNEL DRAWING FULL HEIGHT INVERT				
Rim: 786.25' Rim to Invert: 5' Slack: 0" Sump: 2" Step Position: 0"					Structure Total: 8372 lb						
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	781.25'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"	
Invert 2	781.35'	260°	131.598"	8" PVC SDR35	8.5"	Quik-Lok QL-08-C	10.75"	10.842"	1.825"	0"	
Invert 3	781.5'	210°	106.291"	4" PVC SDR35	4.25"	PSX 8QRS-S NYLO	8"	8.038"	3"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

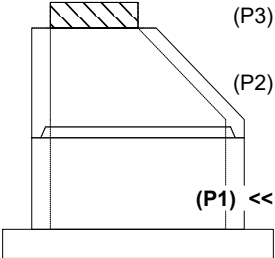


RIGHT-SIDE UP VIEW (int. dimensions)

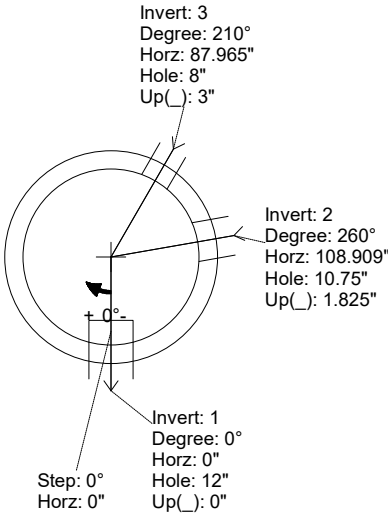

UPSIDE-DOWN VIEW (int. dimensions)

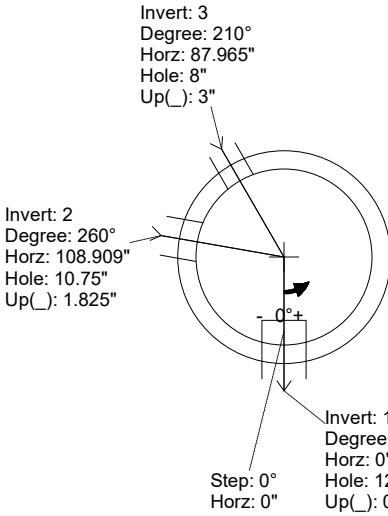

INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 8"	Height (Int): 25" Height (Ext): 33"	Weight (Net): 4526 lb Volume (Net): 1.16cu.yd
----------------------------------	---------------------------------	--	--	--
