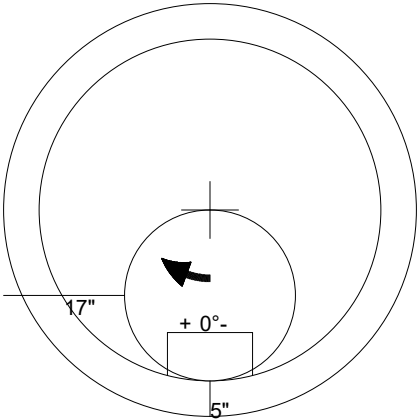



Job Name: 25-3241P2 - Buck Hills Subdivision Job Location: Lawrenceburg, KY 40342 Contractor: Edmonson Plumbing & Heating Supply		Plant: 100 7/24/2026 12:44:48 PM	Tech: Jared - A PC: C. Goff	
Structure ID: MH B1				
P2 MH048CN30		ECC CONE w/ 24" HOLE		
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE - 30" P1) 48" - MH BASE w/FLANGE (08F/08EF) - 25" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) CASTING - HOE MC-420 F/C Sanitary 1) 48" - Conseal CS-231 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 NYLO 1) Quik-Lok - QL-08-C 1) PSX - 8QRS-S NYLO		0 lb 2050 lb 4526 lb 1440 lb 0 lb 0 lb 340 lb 0 lb 0 lb 0 lb 8 lb 1 lb 6 lb ----- Structure Total: 8372 lb	<u>Structure Notes:</u> 1. HOE MC-420 F/C SANITARY PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
				
 48" - ECC CONE w/ 24" HOLE - 30" - (P2)				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 30"	Weight (Net): 2050 lb Volume (Net): 0.41cu.yd
