

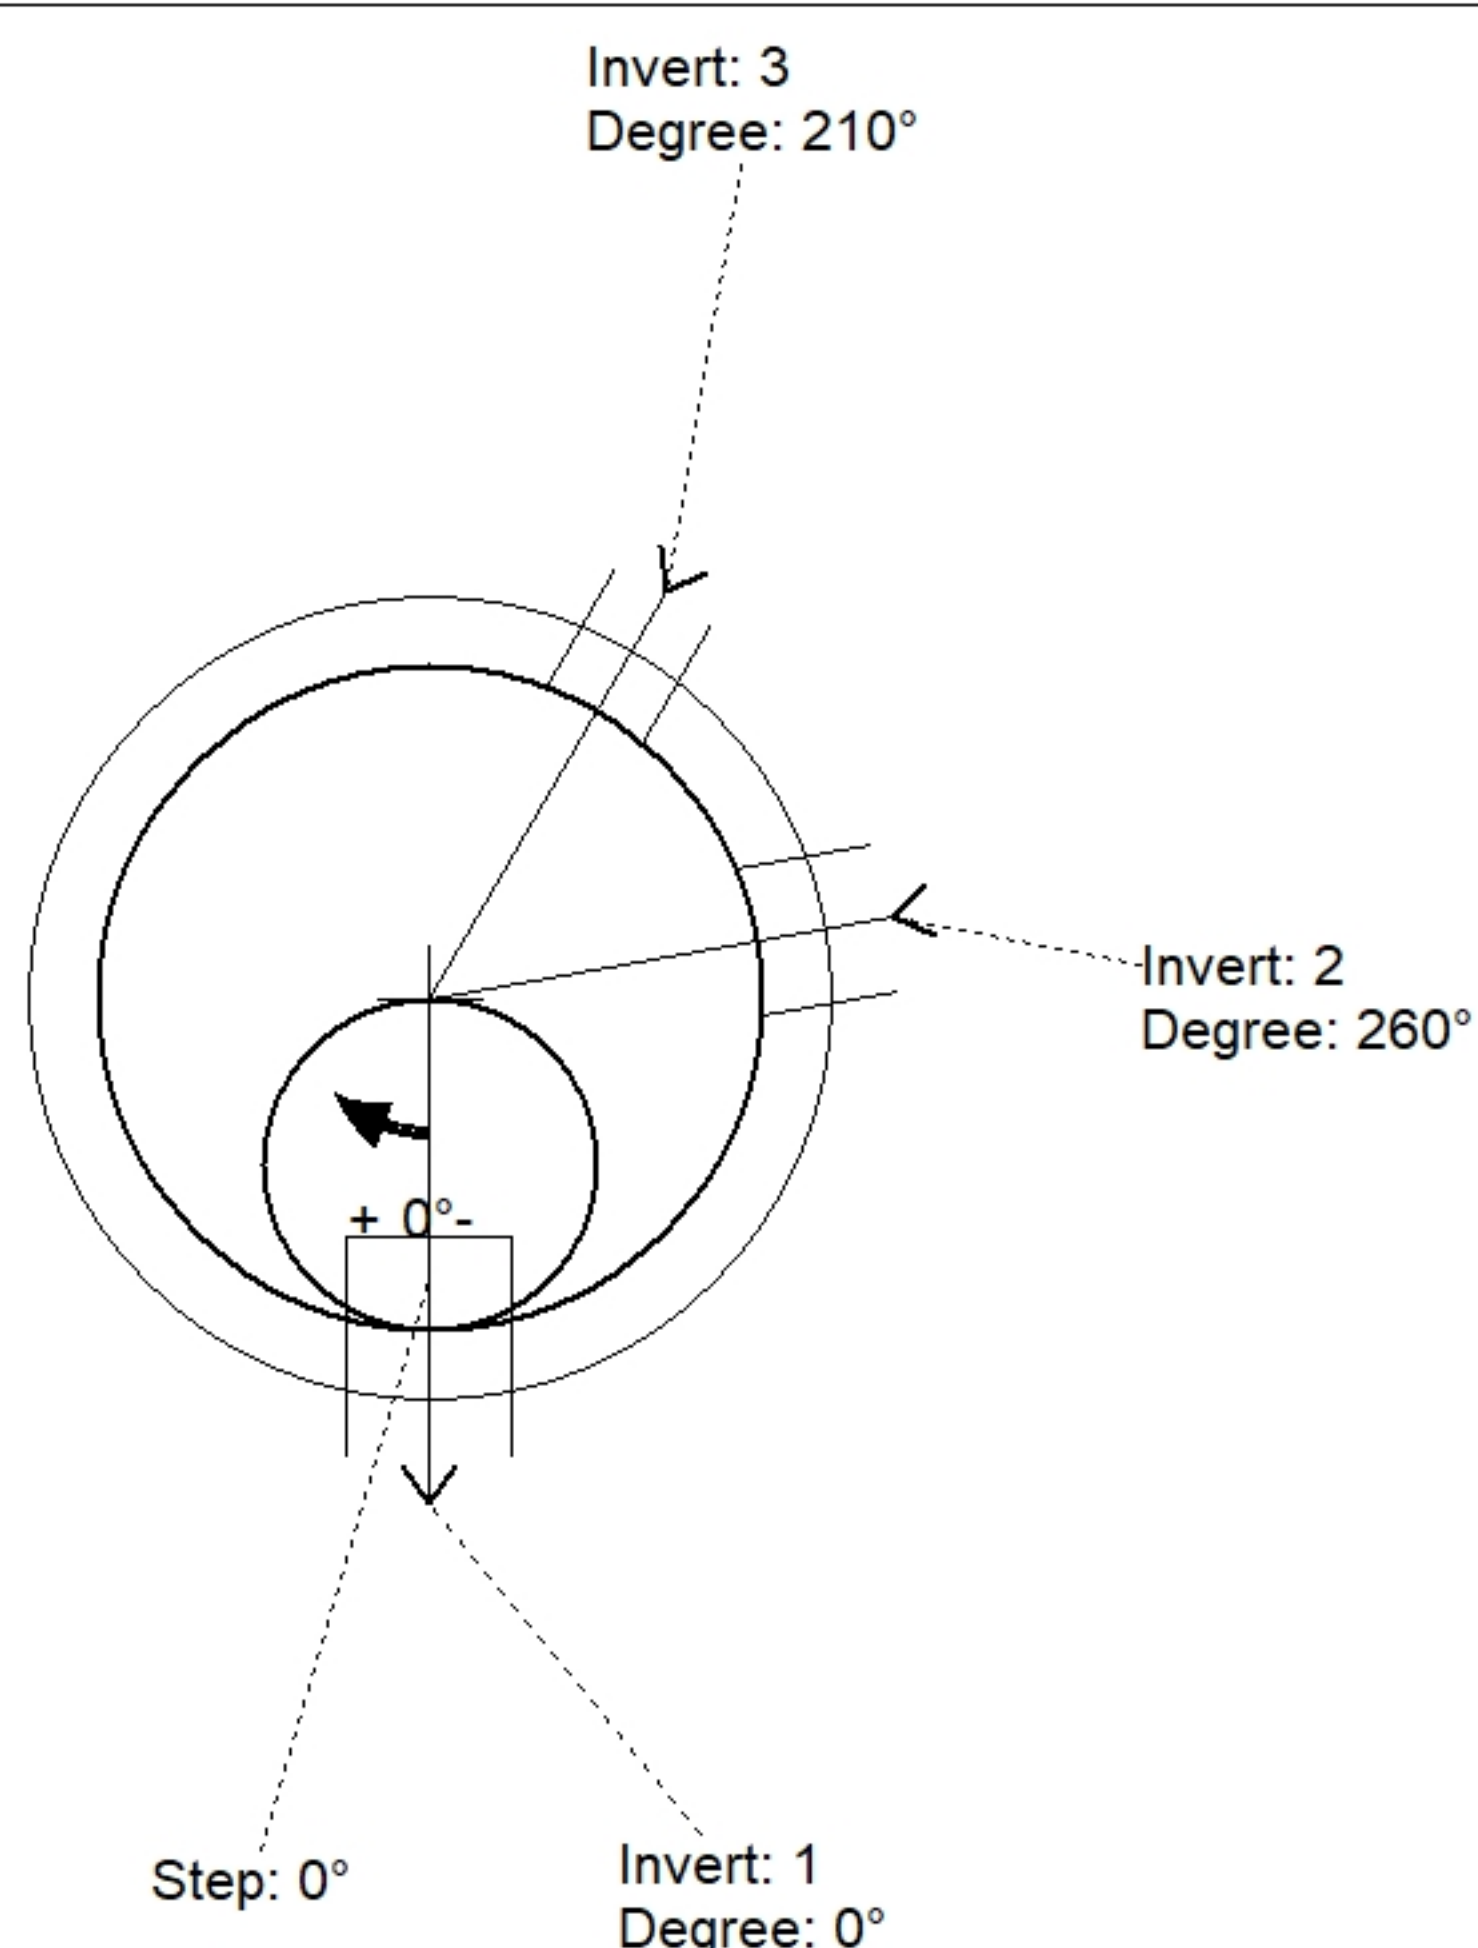


Floor (Bot): 780.417'
Overall Height: 5.833'
Slack: 0"

P3) 24" - CASTING HEIGHT - 7"	0 lb
P2) 48" - ECC CONE w/ 24" HOLE - 30"	2050 lb
P1) 48" - MH BASE w/FLANGE (08F/08EF) - 25"	4526 lb
1) 48" - MH INVERT CHANNEL - FULL HEIGHT	1440 lb
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)	0 lb
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212	0 lb
1) CASTING - HOE MC-420 F/C Sanitary	340 lb
1) 48" - Conseal CS-231 1.00" (Double)	0 lb
1) 24" - Conseal CS-102 1.00" (Double)	0 lb
1) PSX - 12-08 NYLO	8 lb
1) Quik-Lok - QL-08-C	1 lb
1) PSX - 8QRS-S NYLO	6 lb
Structure Total:	8372 lb

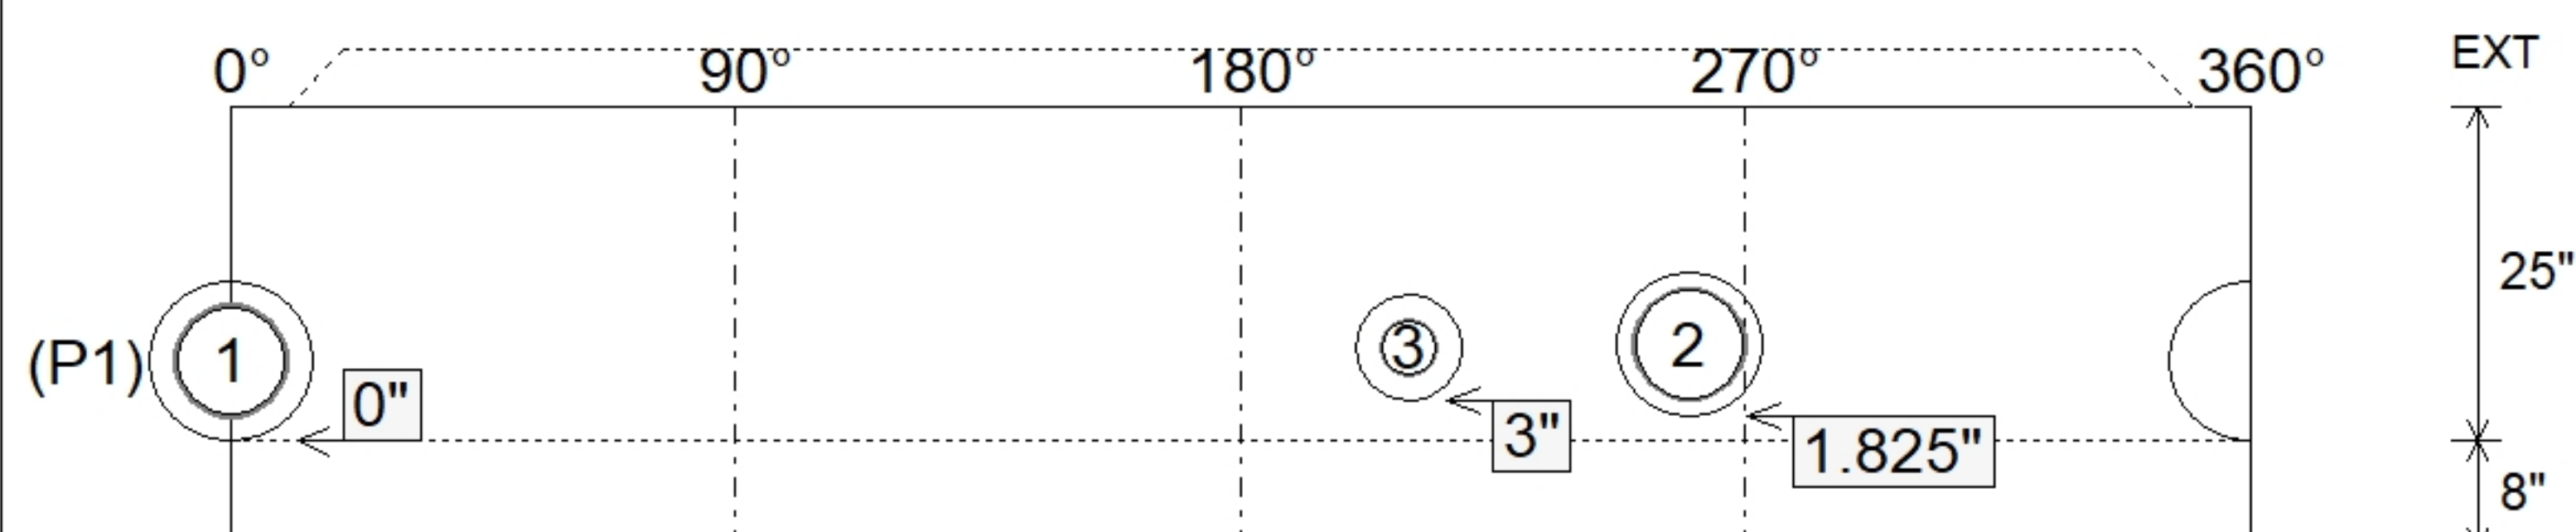

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	786.25'							
Reducer								
Invert 1	781.25'	0°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	0"	P1
Invert 2	781.35'	260°	8" PVC SDR35	8.5"	10.75"	Quik-Lok QL-08-C	1.825"	P1
Invert 3	781.5'	210°	4" PVC SDR35	4.25"	8"	PSX 8QRS-S NYLO	3"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

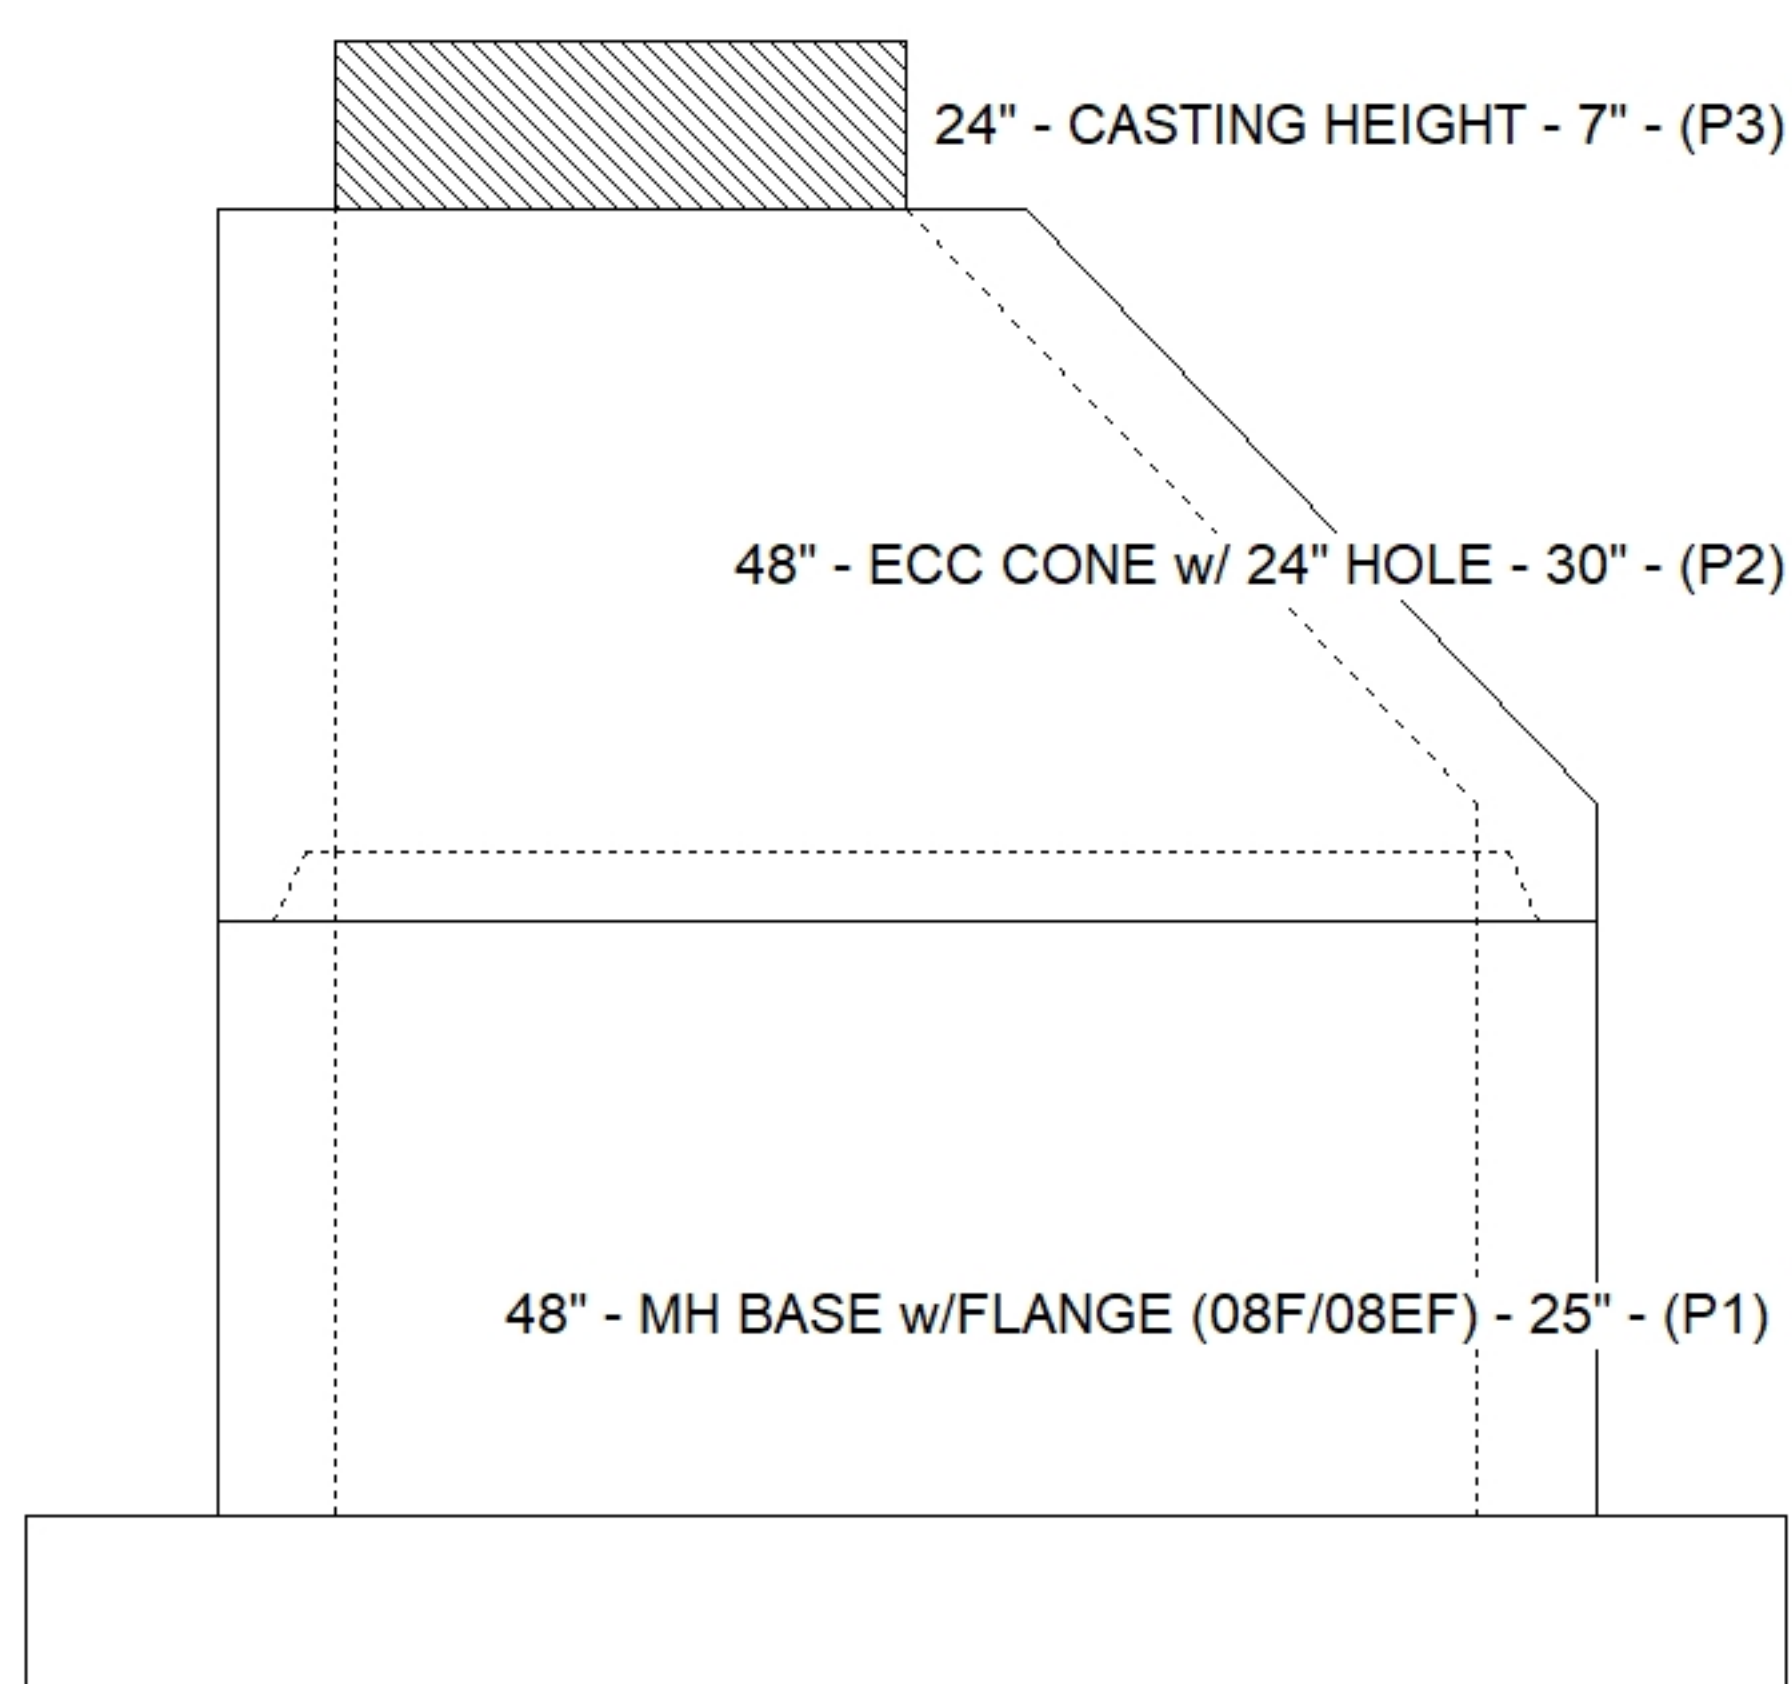

SUBMITTAL
APPROVED BY:
