

Job Name: 25-3241P2 - Buck Hills Subdivision Job Location: Lawrenceburg, KY 40342 Contractor: Edmonson Plumbing & Heating Supply					Plant: 100		Tech: Jared - A			
					7/24/2026 12:43:57 PM		PC: C. Goff			
Structure ID: MH B3 P1 MH048BAEVF MH BASE w/FLANGE (08F/08EF)										
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE - 30" P2) 48" - MH RISER - 36" P1) 48" - MH BASE w/FLANGE (08F/08EF) - 22" 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-420 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 1) PSX - 8QRS-S NYLO					0 lb 2050 lb 2515 lb 4307 lb 0 lb 0 lb 1440 lb 340 lb 0 lb 0 lb 16 lb 6 lb ----- Structure Total: 10675 lb		Structure Notes: 1. HOE MC-420 F/C SANITARY PROVIDED BY ICAST 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 811.69' Rim to Invert: 7.82' Slack: 0.84" Sump: 2" Step Position: 0										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	803.87'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"
Invert 2	803.97'	110°	55.676"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.2"	0"
Invert 3	804.25'	205°	103.76"	4" PVC SDR35	4.25"	PSX 8QRS-S NYLO	8"	8.038"	4.56"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

INSIDE WALL DIMENSIONS


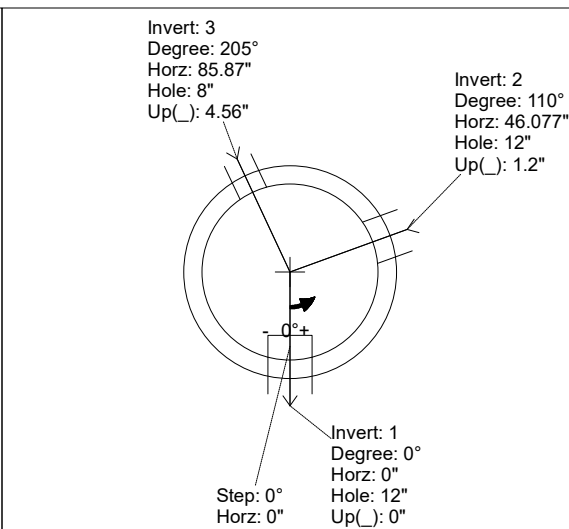
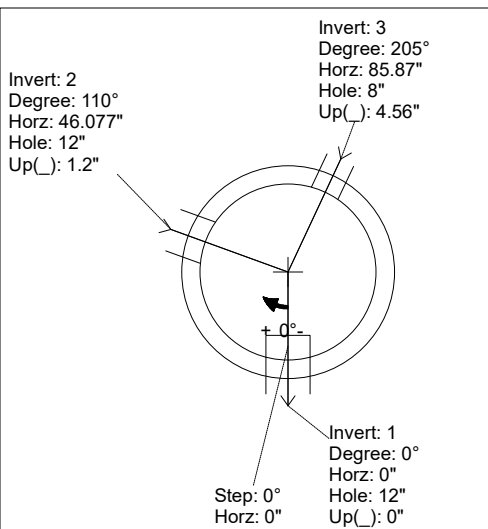
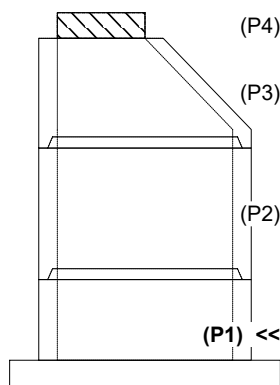
Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: n/a


Wall Thickness: 5"
Floor Height: 8"

Height (Int): 22"
Height (Ext): 30"

Weight (Net): 4307 lb
Volume (Net): 1.1cu.yd

[illegible]

INSIDE WALL DIMENSIONS



Weight (Net): 4307 lb
Volume (Net): 1.1cu.yd
