



Job Name: 25-3241P2 - Buck Hills Subdivision Job Location: Lawrenceburg, KY 40342 Contractor: Edmonson Plumbing & Heating Supply					Plant: 100 7/24/2026 12:45:29 PM		Tech: Jared - A PC: C. Goff				
Structure ID: MH B3											
P2		MH048RS36		MH RISER							
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE - 30" P2) 48" - MH RISER - 36" P1) 48" - MH BASE w/FLANGE (08F/08EF) - 22" 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-420 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 1) PSX - 8QRS-S NYLO					0 lb 2050 lb 2515 lb 4307 lb 0 lb 0 lb 1440 lb 340 lb 0 lb 0 lb 16 lb 6 lb		Structure Notes: 1. HOE MC-420 F/C SANITARY PROVIDED BY ICAST 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 811.69' Rim to Invert: 7.82' Slack: 0.84" Sump: 2" Step Position: 0					Structure Total: 10675 lb						
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

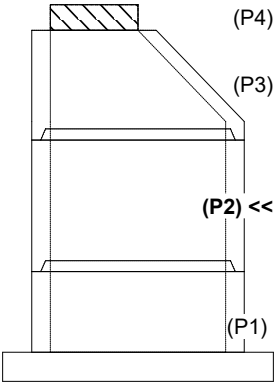


RIGHT-SIDE UP VIEW (int. dimensions)



Step: 0°
Horz: 0"

INSIDE WALL DIMENSIONS

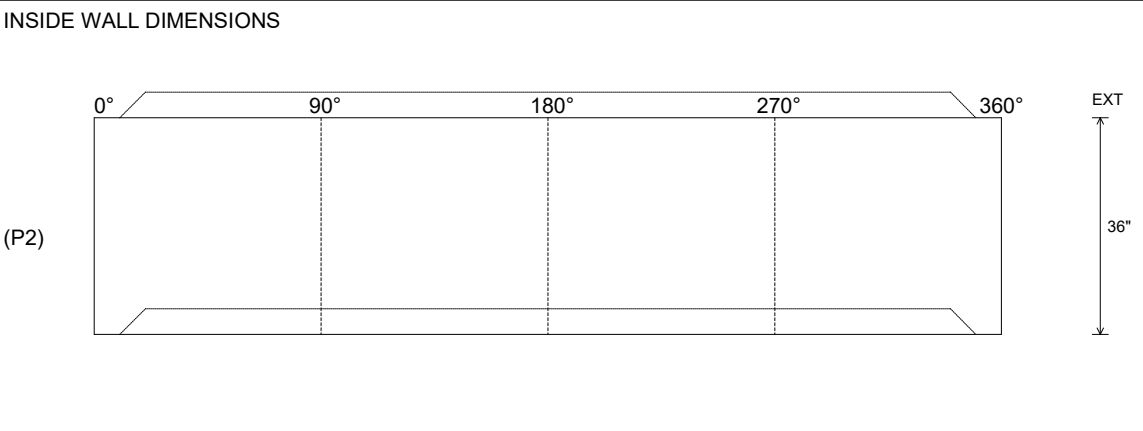

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 36" Height (Ext): 36"	Weight (Net): 2515 lb Volume (Net): 0.64cu.yd
----------------------------------	------------------------------------	--	--	--
