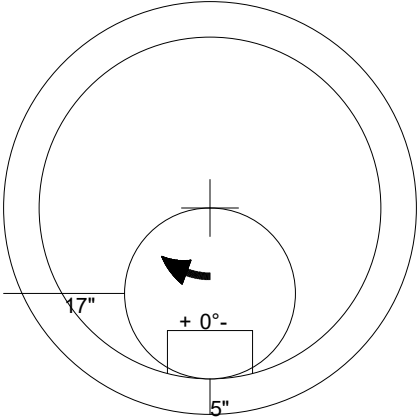



Job Name: 25-3241P2 - Buck Hills Subdivision		Plant: 100	Tech: Jared - A	
Job Location: Lawrenceburg, KY 40342		7/24/2026 12:44:50 PM	PC: C. Goff	
Contractor: Edmonson Plumbing & Heating Supply				
Structure ID: MH B5				
P2 MH048CN30		ECC CONE w/ 24" HOLE		
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE - 30" P1) 48" - MH BASE w/FLANGE (08F/08EF) - 25" 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-420 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 NYLO 1) PSX - 8QRS-S NYLO		0 lb 2050 lb 4565 lb 0 lb 0 lb 1440 lb 340 lb 0 lb 0 lb 0 lb 8 lb 6 lb ----- Structure Total: 8409 lb	Structure Notes: 1. HOE MC-420 F/C SANITARY PROVIDED BY ICAST 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
				
				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 30"	Weight (Net): 2050 lb Volume (Net): 0.41cu.yd
