



Floor (Bot): 838.917'
Overall Height: 5.833'
Slack: 0"

P3) 24" - CASTING HEIGHT - 7"	0 lb
P2) 48" - ECC CONE w/ 24" HOLE - 30"	2050 lb
P1) 48" - MH BASE w/FLANGE (08F/08EF) - 25"	4565 lb
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)	0 lb
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212	0 lb
1) 48" - MH INVERT CHANNEL - FULL HEIGHT	1440 lb
1) CASTING - HOE MC-420 F/C Sanitary	340 lb
1) 48" - Conseal CS-102 1.00" (Double)	0 lb
1) 24" - Conseal CS-102 1.00" (Double)	0 lb
1) PSX - 12-08 NYLO	8 lb
1) PSX - 8QRS-S NYLO	6 lb


Structure Total:	8409 lb

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Remarks
Rim	844.75'							
Reducer								
Invert 1	839.75'	0°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	0"	Pipe
Invert 2	840'	130°	4" PVC SDR35	4.25"	8"	PSX 8QRS-S NYLO	3"	Pipe
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" - CASTING HEIGHT - 7" - (P3)

48" - ECC CONE w/ 24" HOLE - 30" - (P2)

48" - MH BASE w/FLANGE (08F/08EF) - 25" - (P1)

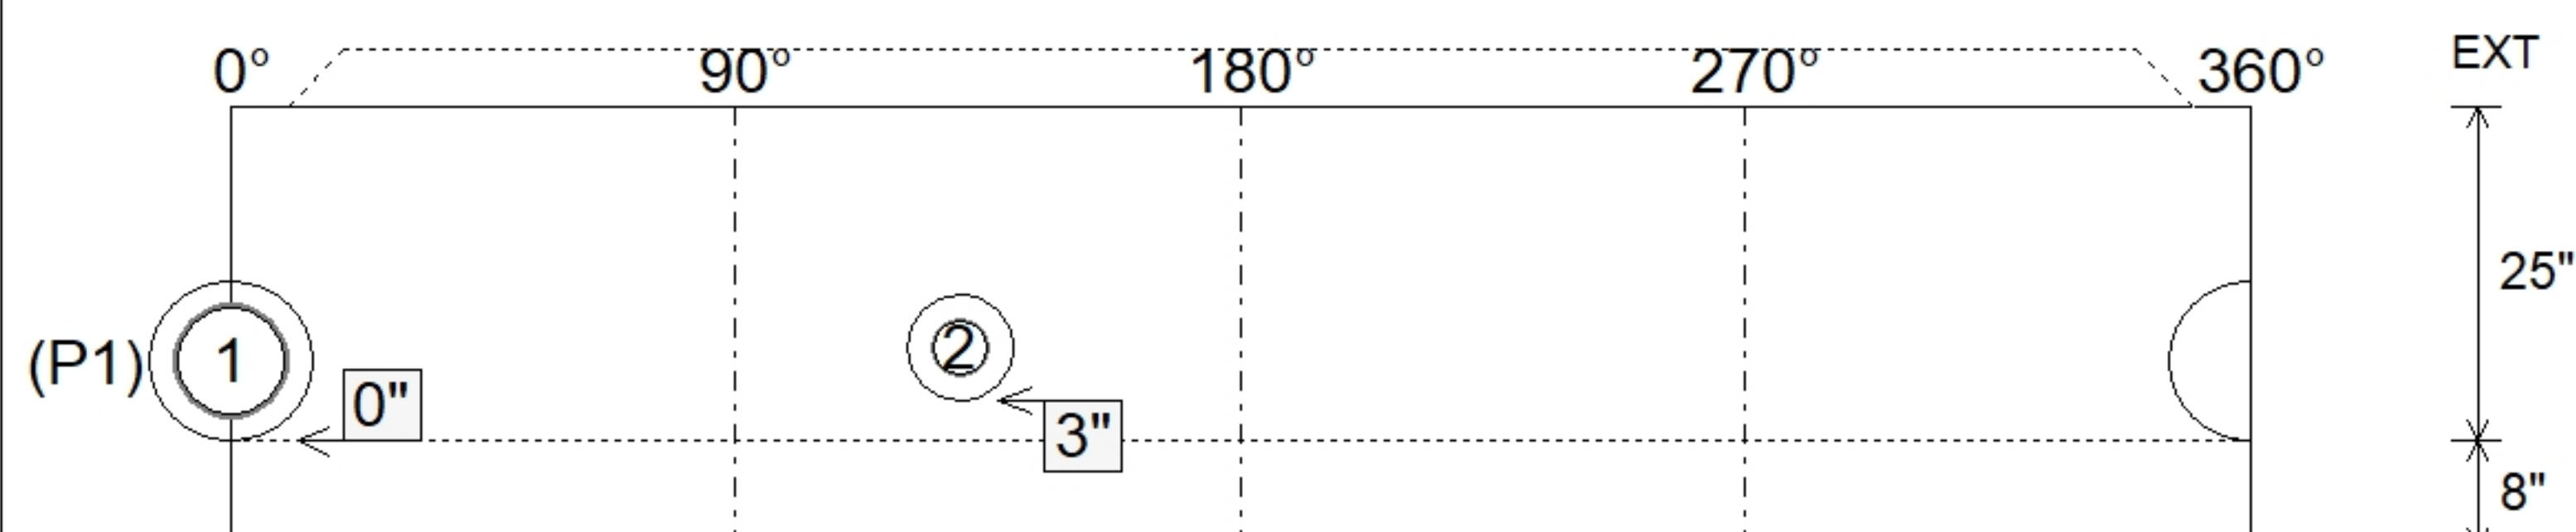

SUBMITTAL
APPROVED BY:
