

Job Name: 25-3241P2 - Buck Hills Subdivision Job Location: Lawrenceburg, KY 40342 Contractor: Edmonson Plumbing & Heating Supply					Plant: 100		Tech: Jared - A			
					7/24/2026 12:43:59 PM		PC: C. Goff			
Structure ID: MH C1										
P1 MH048BAEVF			MH BASE w/FLANGE (08F/08EF)							
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE - 36" P1) 48" - MH BASE w/FLANGE (08F/08EF) - 31" 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-420 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO					0 lb 3000 lb 4957 lb 0 lb 0 lb 1440 lb 340 lb 0 lb 0 lb 16 lb ----- Structure Total: 9753 lb		Structure Notes: 1. HOE MC-420 F/C SANITARY PROVIDED BY ICAST 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 807' Rim to Invert: 6' Slack: 0" Sump: 2" Step Position: 0										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	801'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"
Invert 2	801.1'	240°	121.475"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.2"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

INSIDE WALL DIMENSIONS


Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 8"	Height (Int): 31" Height (Ext): 39"	Weight (Net): 4957 lb Volume (Net): 1.27cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 25-3241P2 - Buck Hills Subdivision Job Location: Lawrenceburg, KY 40342 Contractor: Edmonson Plumbing & Heating Supply					Plant: 100 7/24/2026 12:43:59 PM		Tech: Jared - A PC: C. Goff			
Structure ID: MH C1										
P1 MH048BAEVF		MH BASE w/FLANGE (08F/08EF)								
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE - 36" P1) 48" - MH BASE w/FLANGE (08F/08EF) - 31" 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-420 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO					0 lb 3000 lb 4957 lb 0 lb 0 lb 1440 lb 340 lb 0 lb 0 lb 16 lb ----- Structure Total: 9753 lb		Structure Notes: 1. HOE MC-420 F/C SANITARY PROVIDED BY ICAST 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W. INVERT CHANNEL DRAWING FULL HEIGHT INVERT			
Rim: 807' Rim to Invert: 6' Slack: 0" Sump: 2" Step Position: 0										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	801'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"
Invert 2	801.1'	240°	121.475"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.2"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

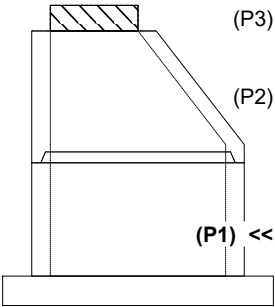

(P3)
(P2)
(P1) <<

RIGHT-SIDE UP VIEW (int. dimensions)

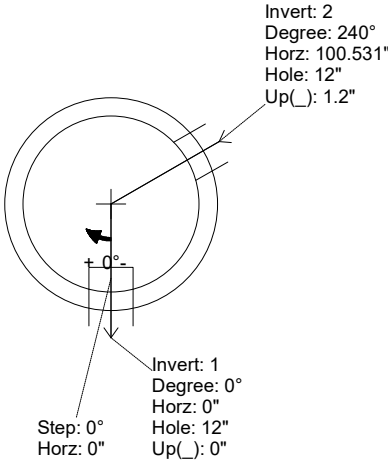


Invert: 2
Degree: 240°
Horz: 100.531"
Hole: 12"
Up(): 1.2"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 12"
Up(): 0"

Step: 0°
Horz: 0"

UPSIDE-DOWN VIEW (int. dimensions)

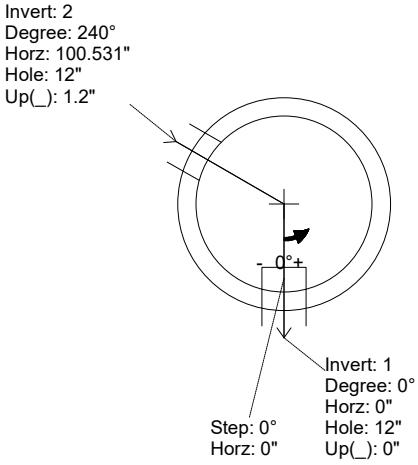


Invert: 2
Degree: 240°
Horz: 100.531"
Hole: 12"
Up(): 1.2"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 12"
Up(): 0"

Step: 0°
Horz: 0"

INSIDE WALL DIMENSIONS

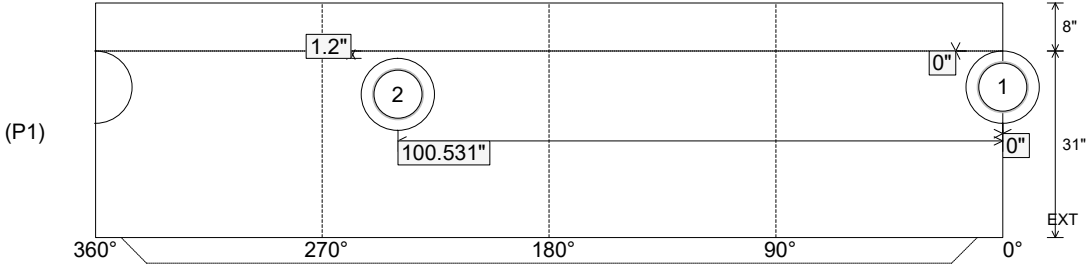

(P1)

1.2"
100.531"
0"
31"
EXT

360° 270° 180° 90° 0°

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 8"	Height (Int): 31" Height (Ext): 39"	Weight (Net): 4957 lb Volume (Net): 1.27cu.yd
----------------------------------	---------------------------------	--	--	--
