

**Contractor: Phillips Brothers**

Plant: 100




Slack: 0.52"

- FLOOR (As .12) #5 BARS AT 6" C.C.E.W.

P2) 30" x 48" - CASTING HEIGHT - 8"  
P1) 30" x 48" - BOX BASE 8inW, 8inF, Variable Ht - 39"  
1) SECONDARY POUR - WALLS  
1) 30" x 48" - Conseal CS-102 1.00"  
2) Hole - 26  
2) Hole - 22



0 lb  
5636 lb  
0 lb  
0 lb  
0 lb  
0 lb

Structure Total: 5636 lb

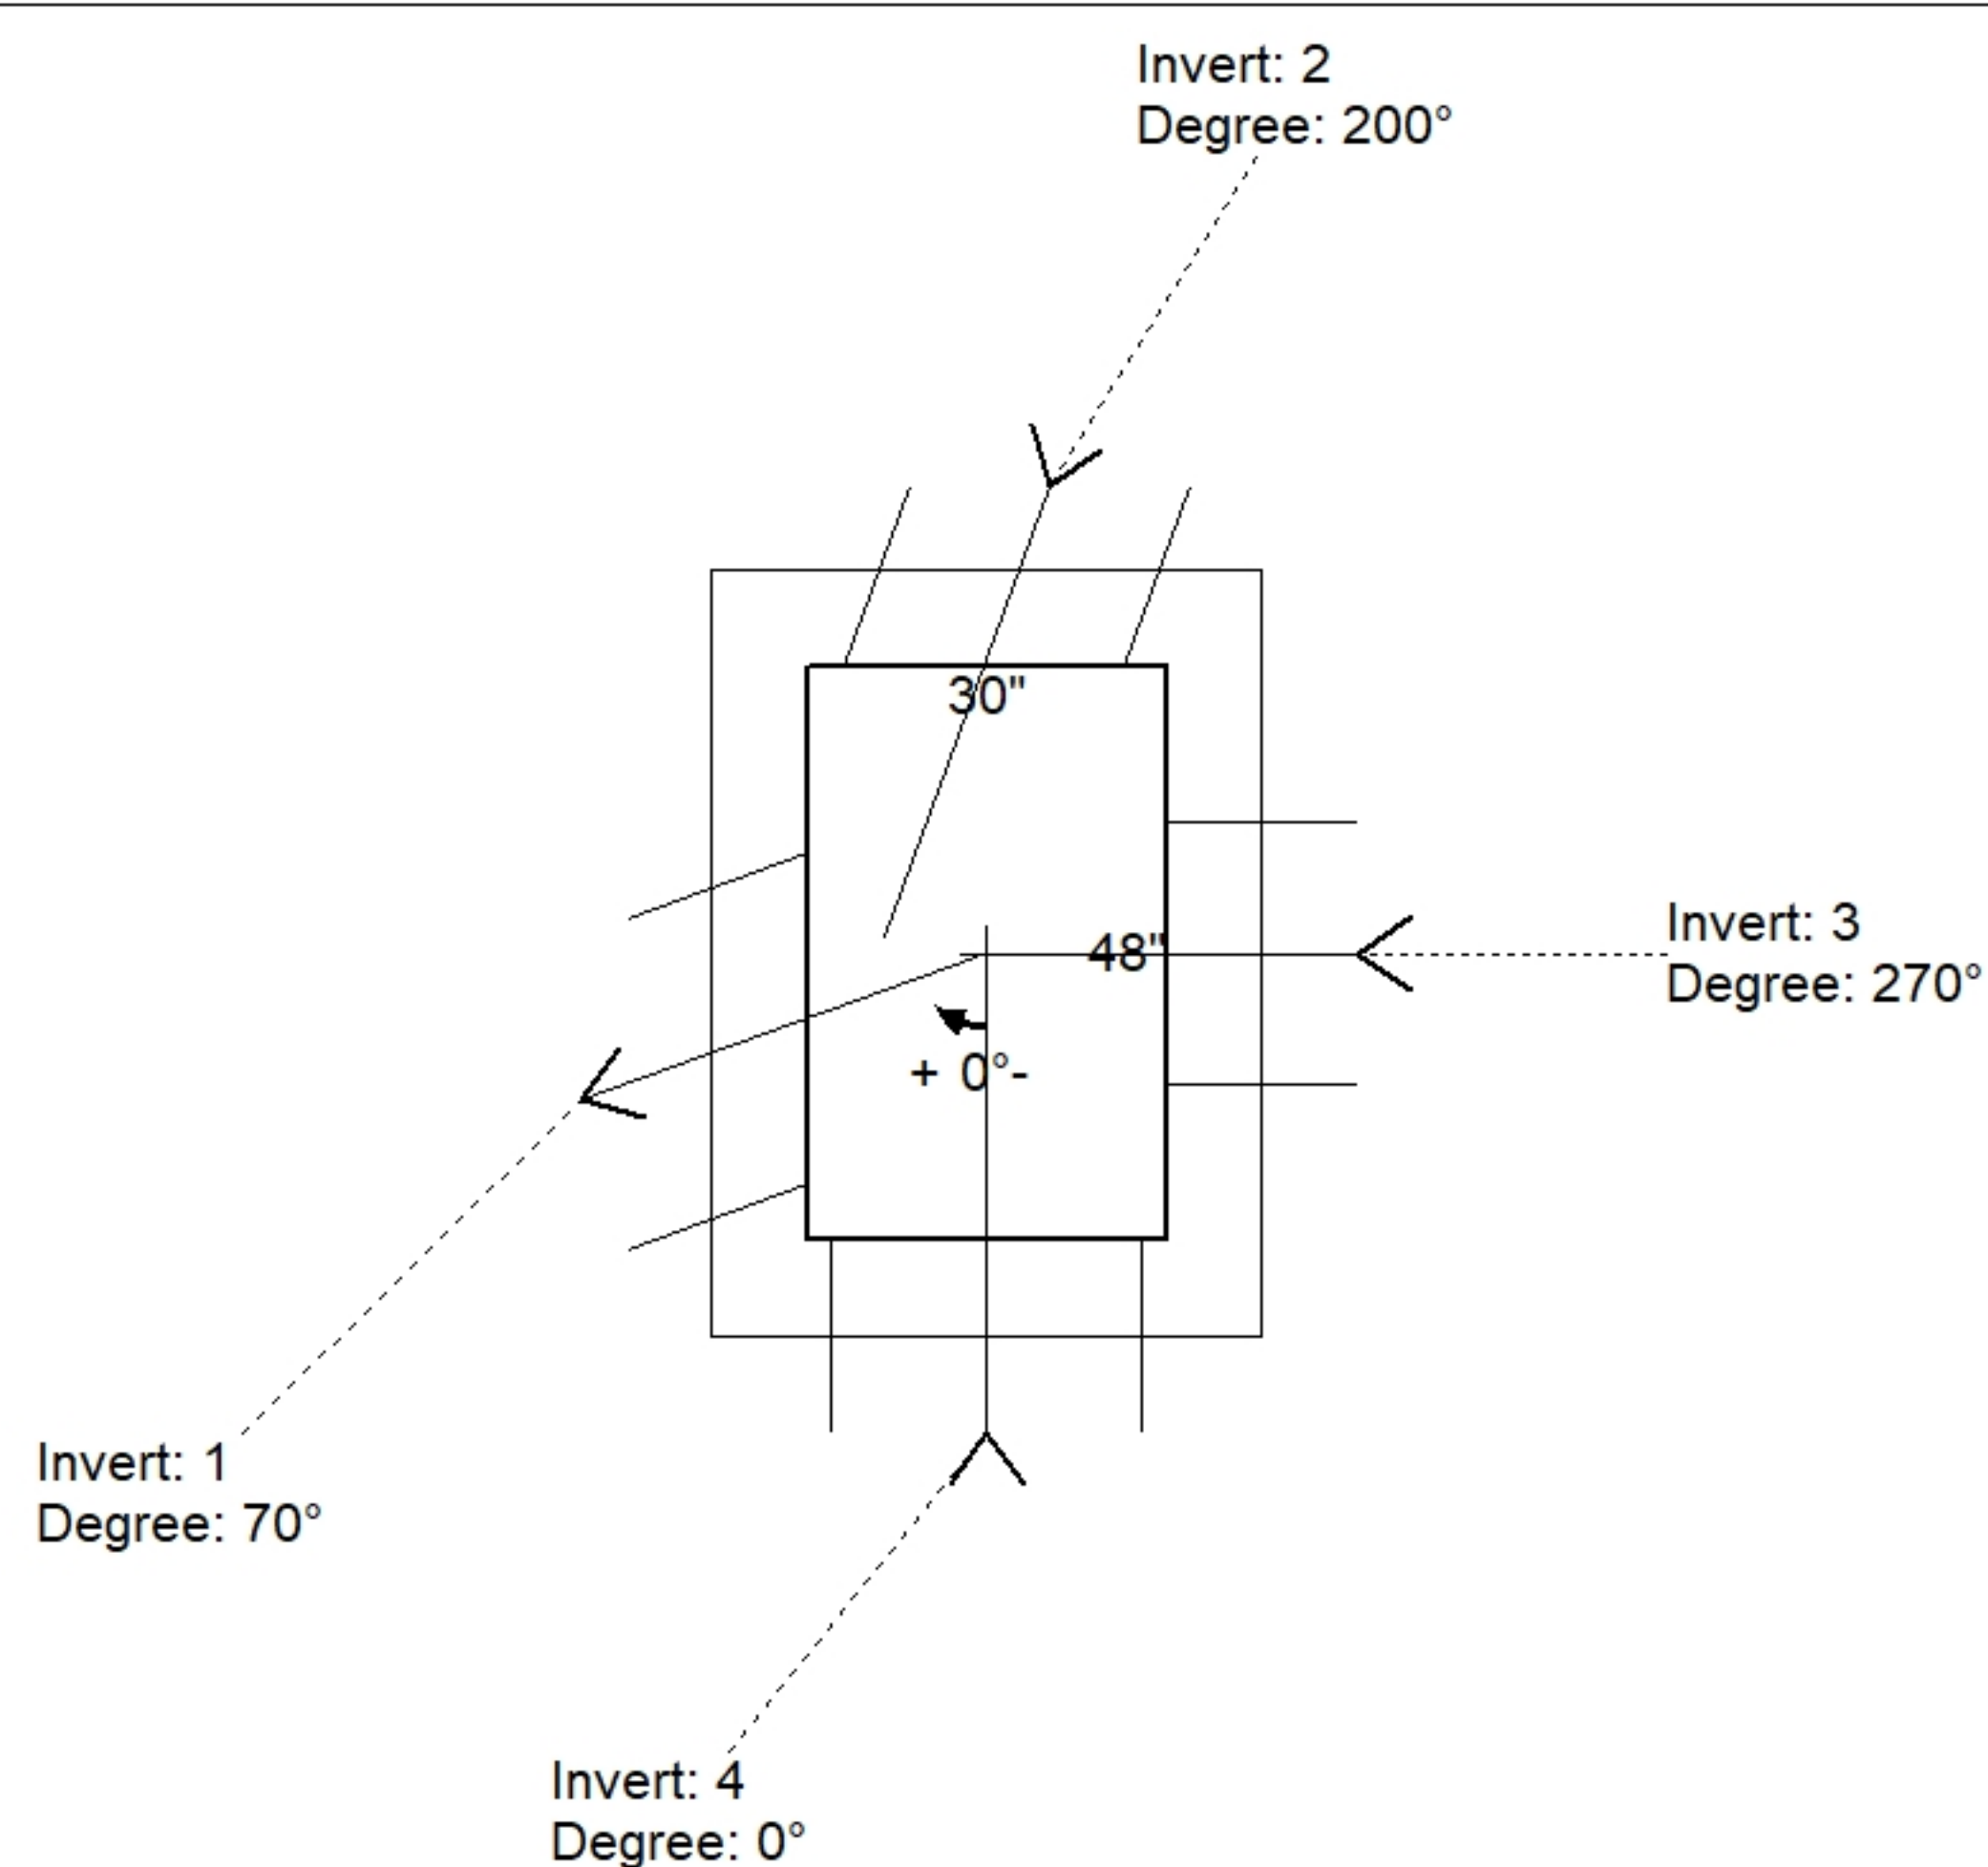

| Position | Elev    | Angle | Pipe           | Pipe OD | Hole | Connector | Up (') | Ref |
|----------|---------|-------|----------------|---------|------|-----------|--------|-----|
| Rim      | 739.23' |       |                |         |      |           |        |     |
| Reducer  |         |       |                |         |      |           |        |     |
| Invert 1 | 735.27' | 70°   | 18" RCP B WALL | 23"     | 26"  | Hole 26   | -2.5"  | P1  |
| Invert 2 | 735.27' | 200°  | 15" RCP B WALL | 19.5"   | 22"  | Hole 22   | -2.25" | P1  |
| Invert 3 | 735.27' | 270°  | 15" RCP B WALL | 19.5"   | 22"  | Hole 22   | -2.25" | P1  |
| Invert 4 | 735.27' | 0°    | 18" RCP B WALL | 23"     | 26"  | Hole 26   | -2.5"  | P1  |
| Invert 5 |         |       |                |         |      |           |        |     |
| Invert 6 |         |       |                |         |      |           |        |     |
| Invert 7 |         |       |                |         |      |           |        |     |
| Invert 8 |         |       |                |         |      |           |        |     |

### Default - Interior Dimensions

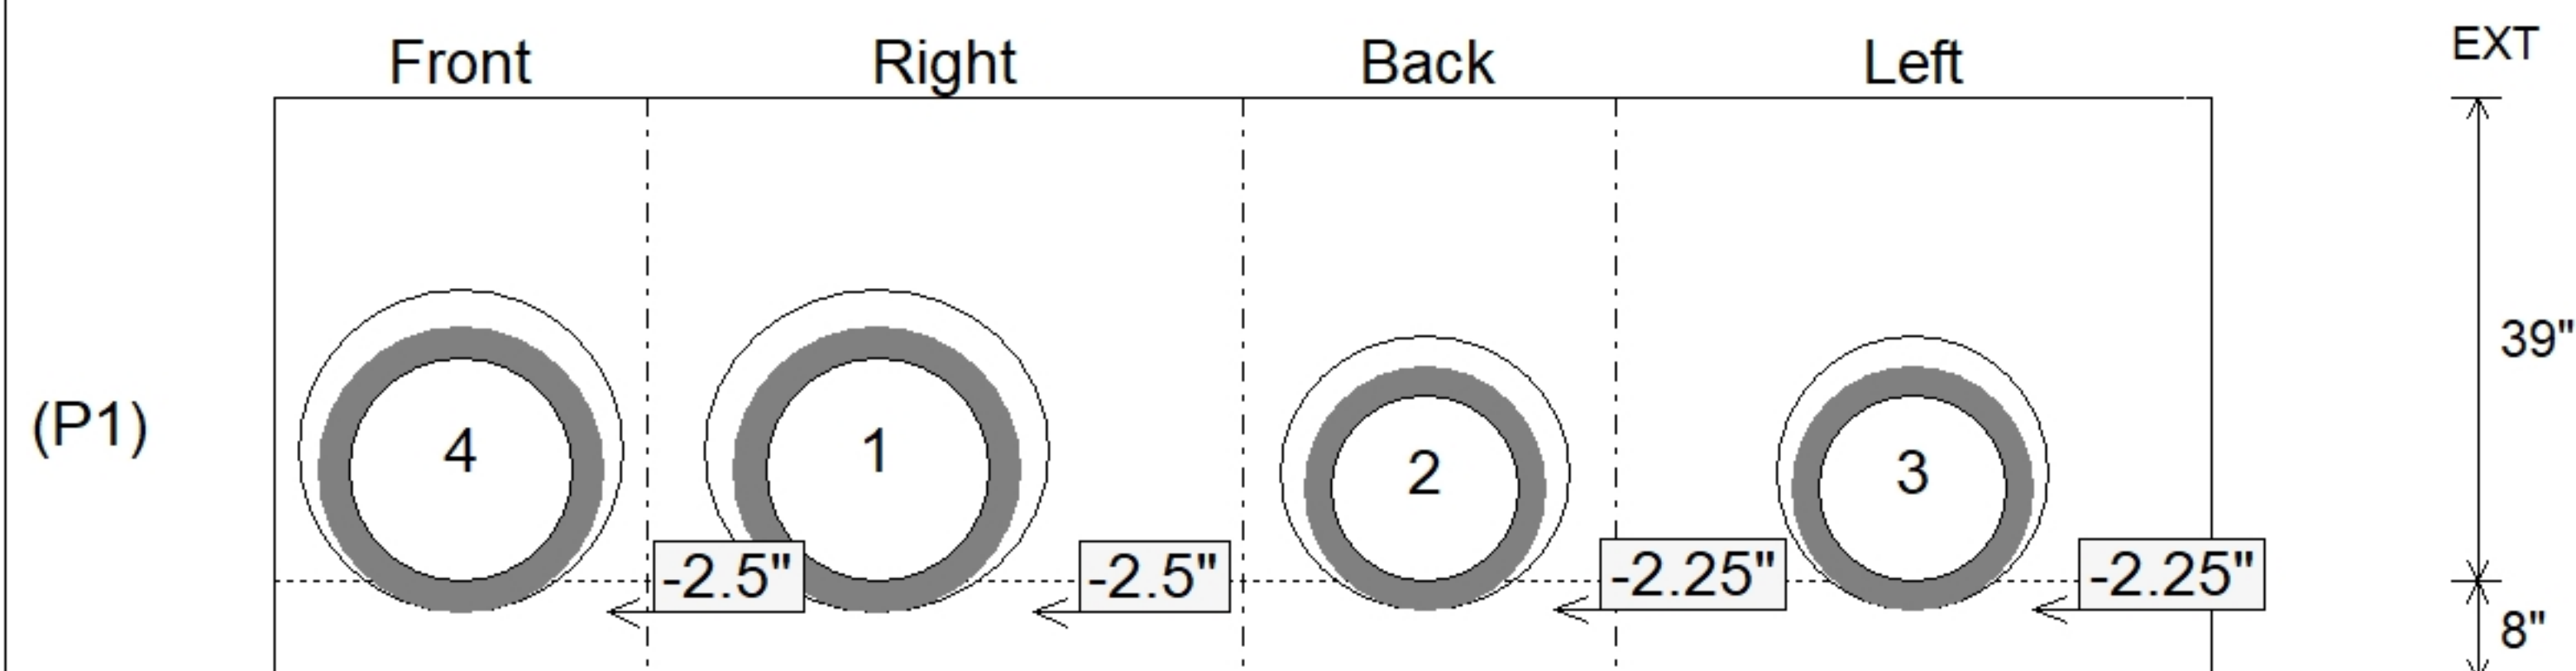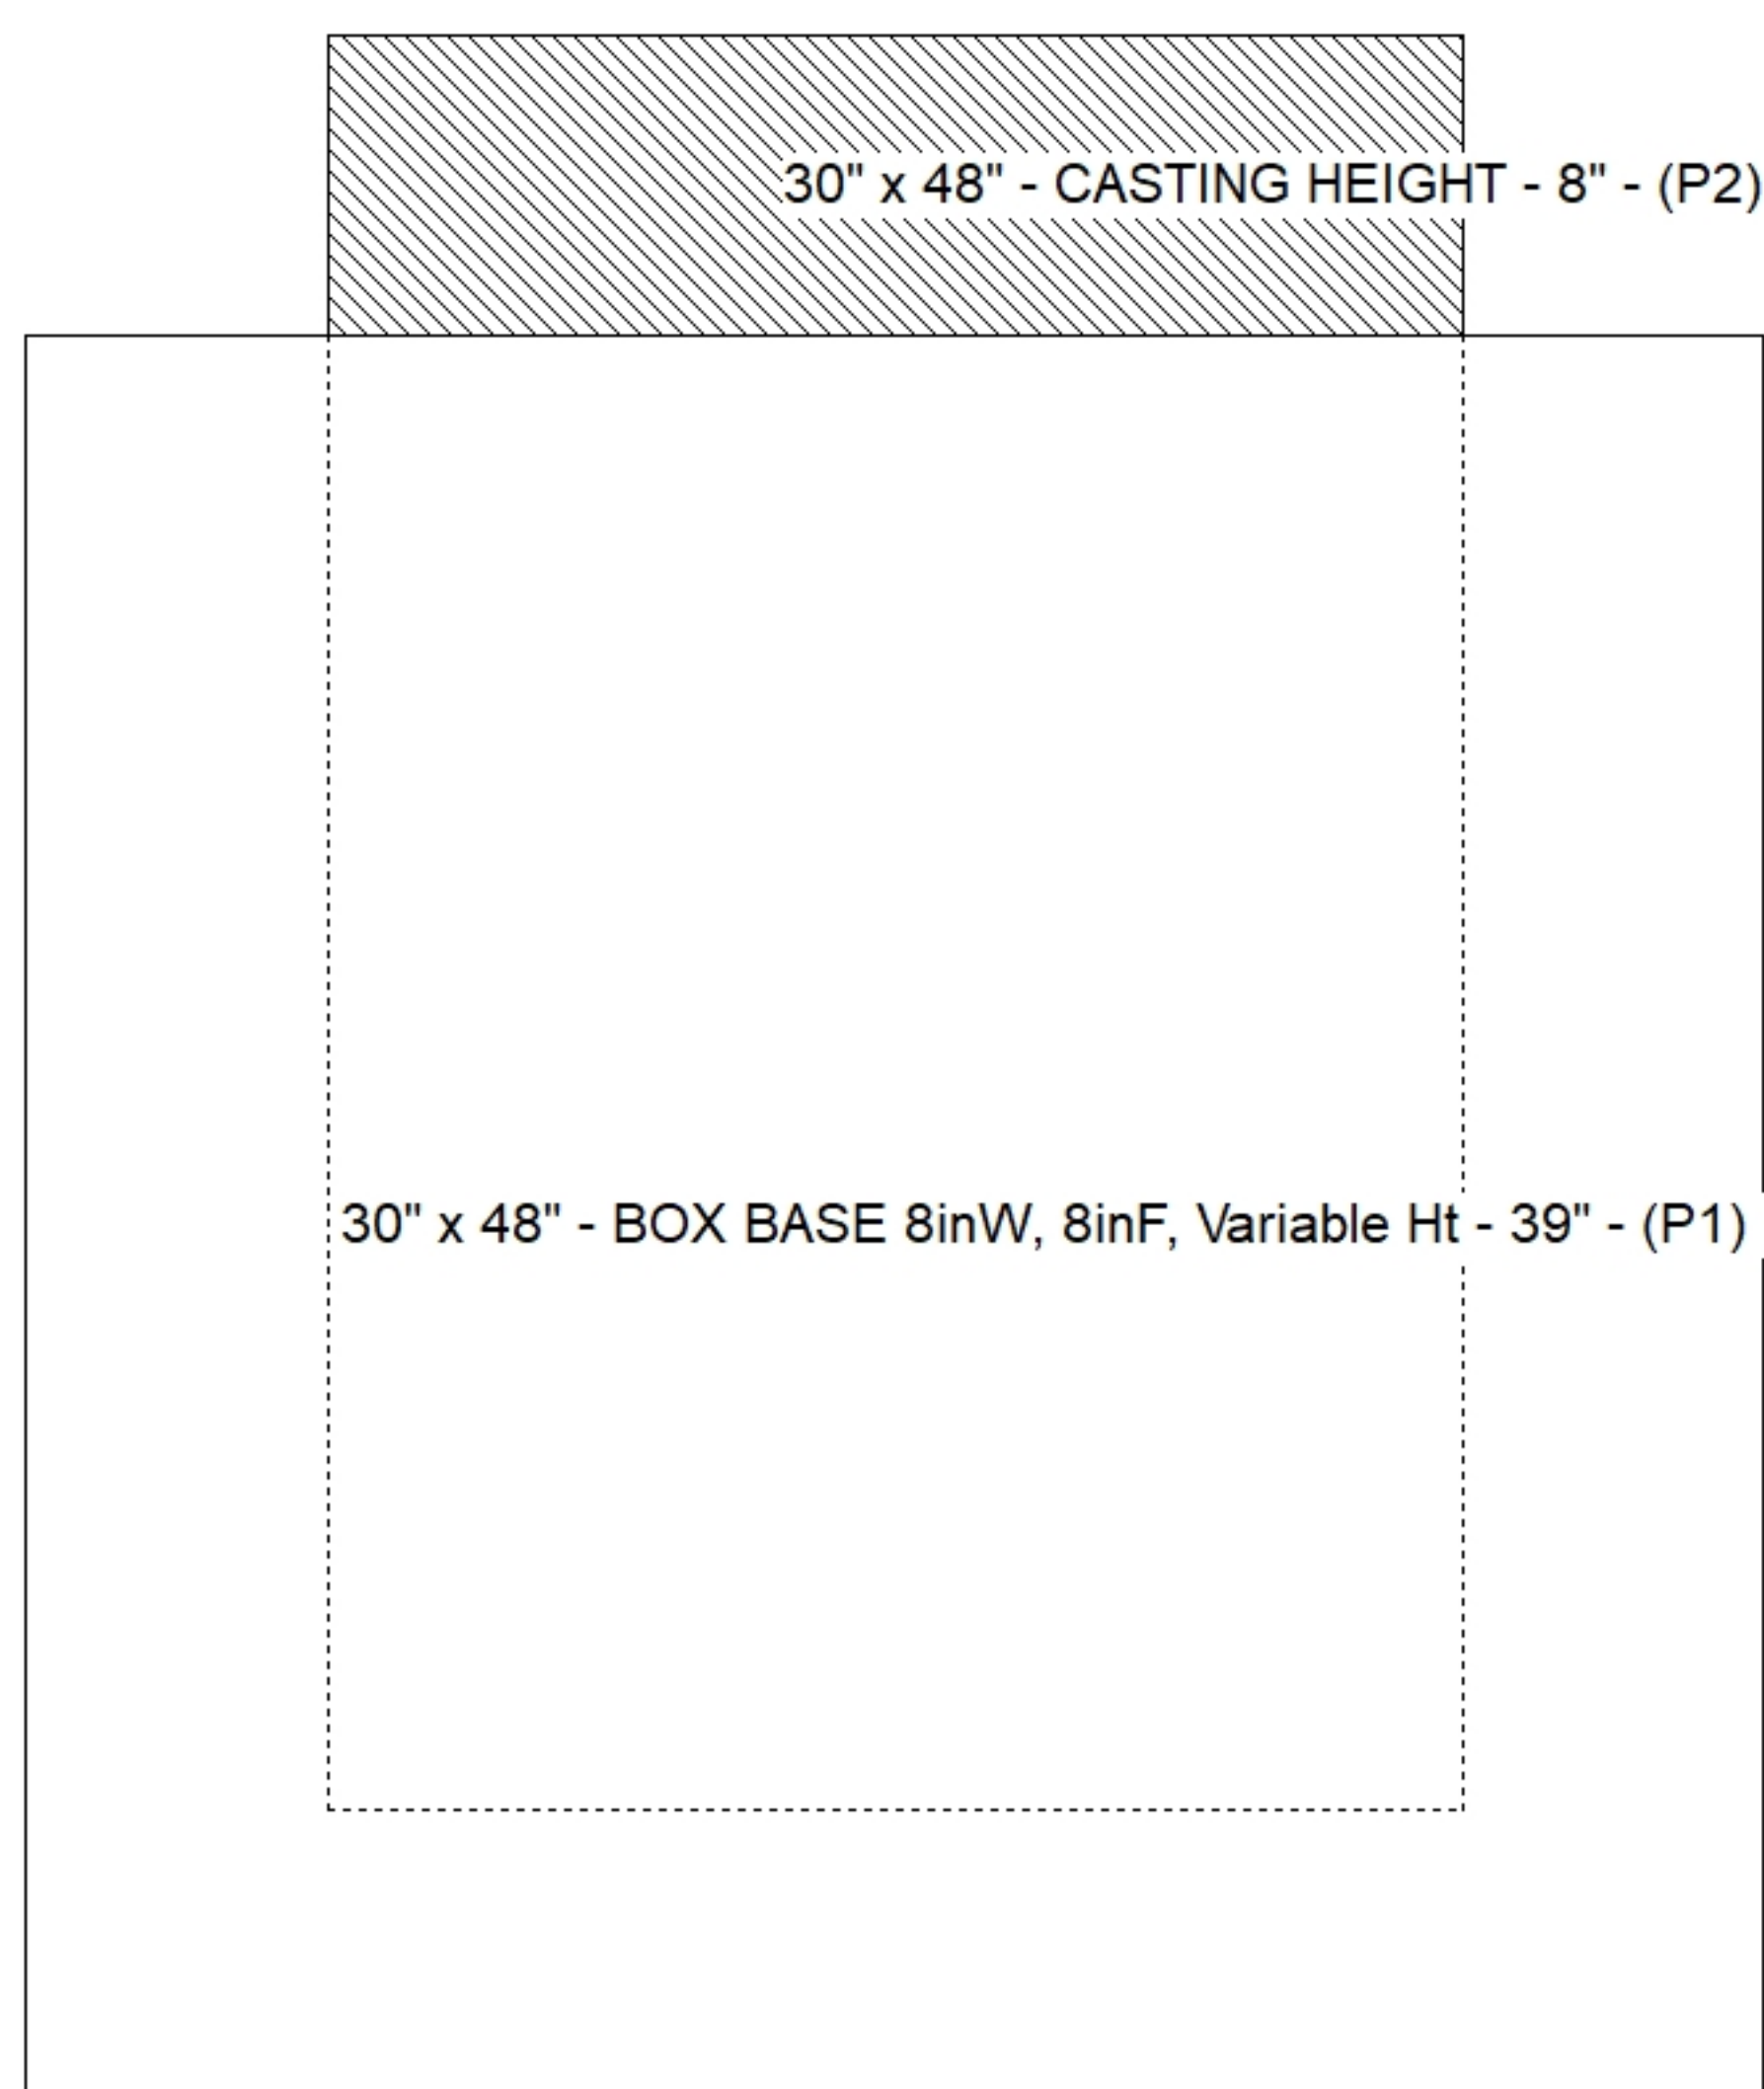

SUBMITTAL  
APPROVED BY:
