

Contractor: Phillips Brothers

TECH: J. Horsley - F

Plant: 100




Slack: 0"

REINFORCING PER ASTM A615 (GRADE 60).
- WALLS (As .12) #5 BARS AT 6" C.C.E.W.
- FLOOR (As .12) #5 BARS AT 6" C.C.E.W

P2) 36" x 48" - P.I.P. - BY OTHERS - 8"
P1) 36" x 48" - BOX BASE 8inW, 8inF, Variable Ht - 58"
1) 36" x 48" - Conseal CS-102 1.00"
1) Hole - 30
2) Hole - 32
1) Hole - 26


0 lb
8110 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 8110 lb

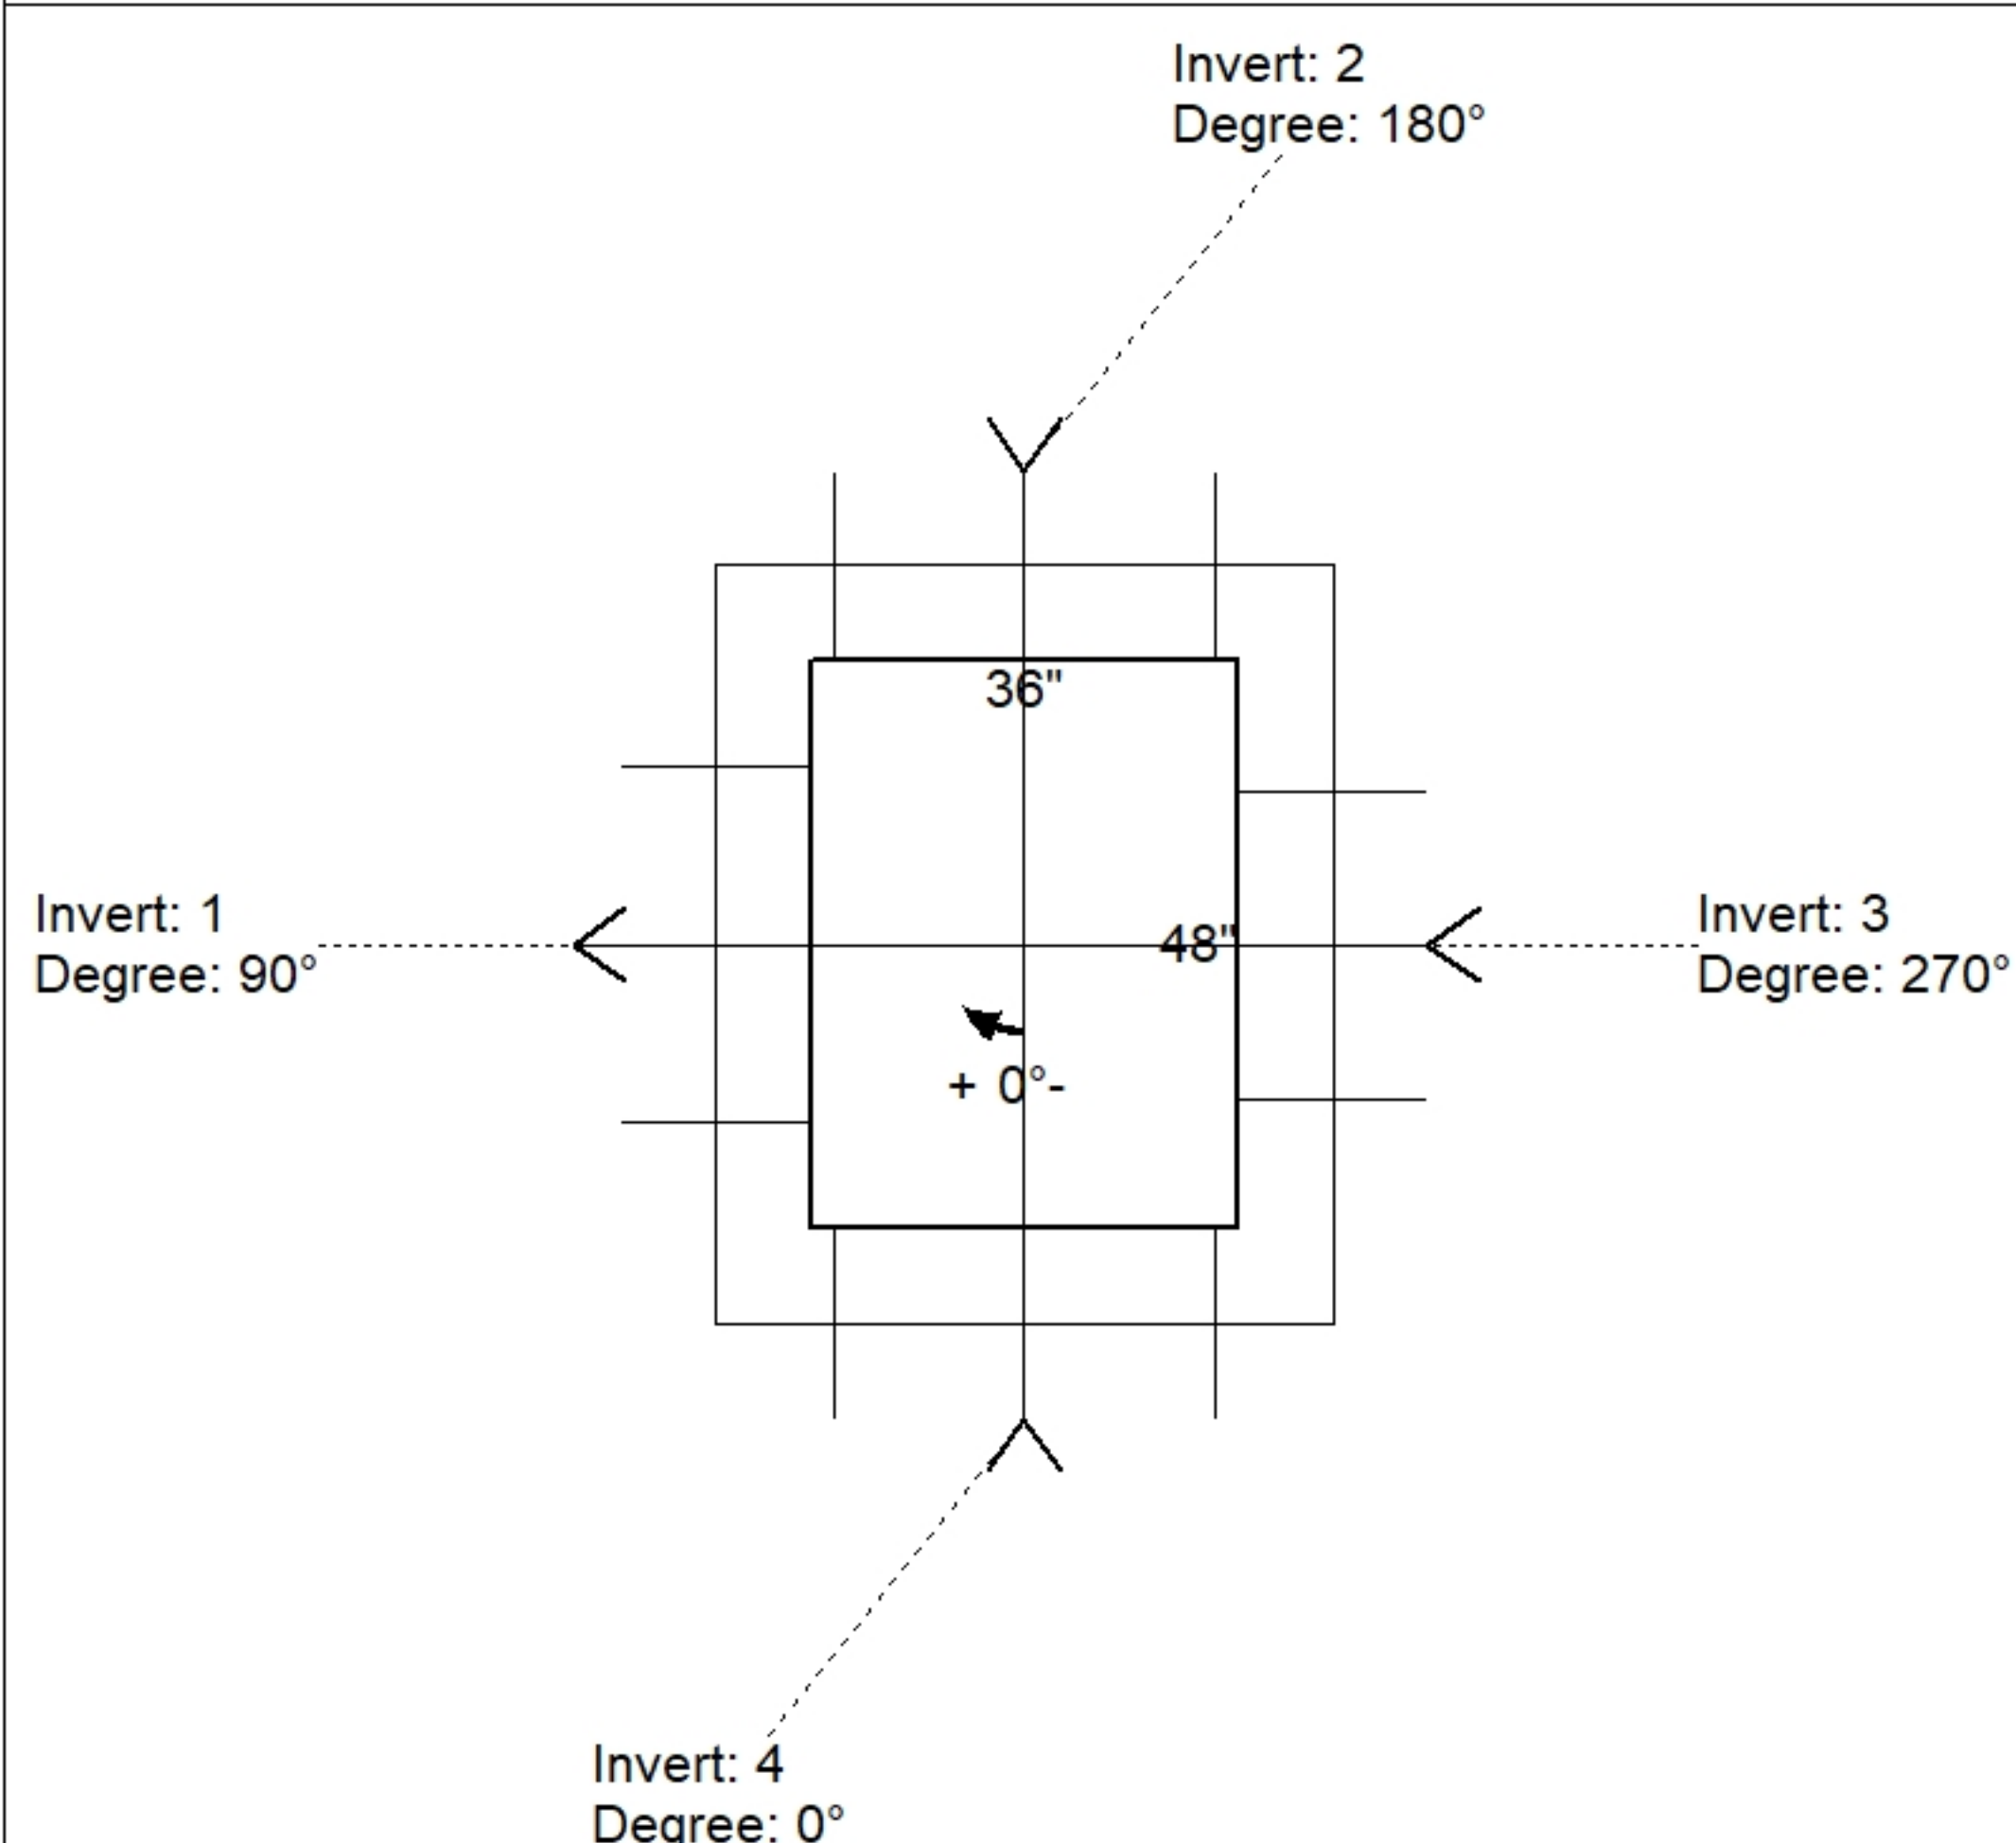

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	739.62'							
Reducer								
Invert 1	734.12'	90°	24" HDPE	27.8"	30"	Hole 30	-1.9"	P1
Invert 2	734.12'	180°	24" RCP B WALL	30"	32"	Hole 32	-3"	P1
Invert 3	734.75'	270°	18" RCP B WALL	23"	26"	Hole 26	5.06"	P1
Invert 4	734.12'	0°	24" RCP B WALL	30"	32"	Hole 32	-3"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

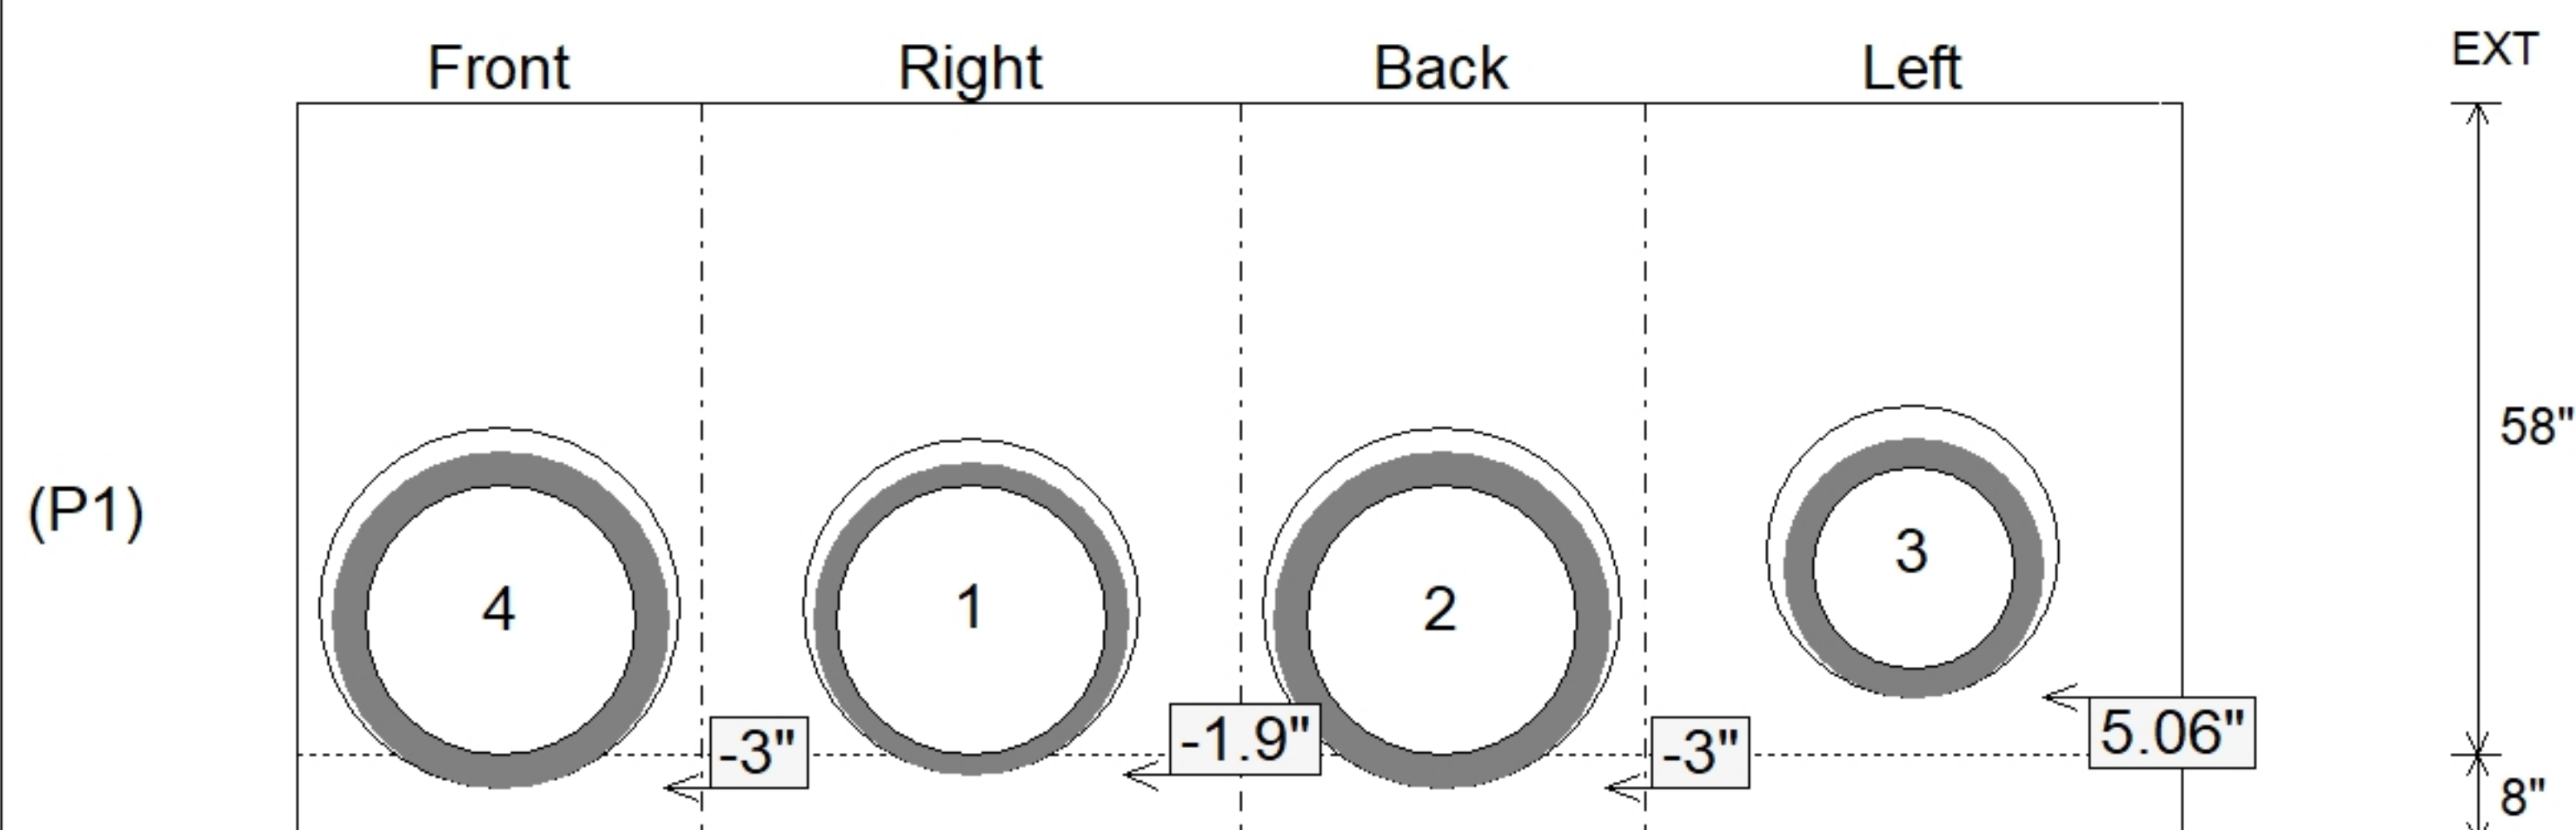

Submittal Drawing
5/11/2026 8:23:34 AM

SUBMITTAL
APPROVED BY:
