


Contractor: Phillips Brothers

Plant: 100




Slack: 0.52"

Structure Total: 9022 lb

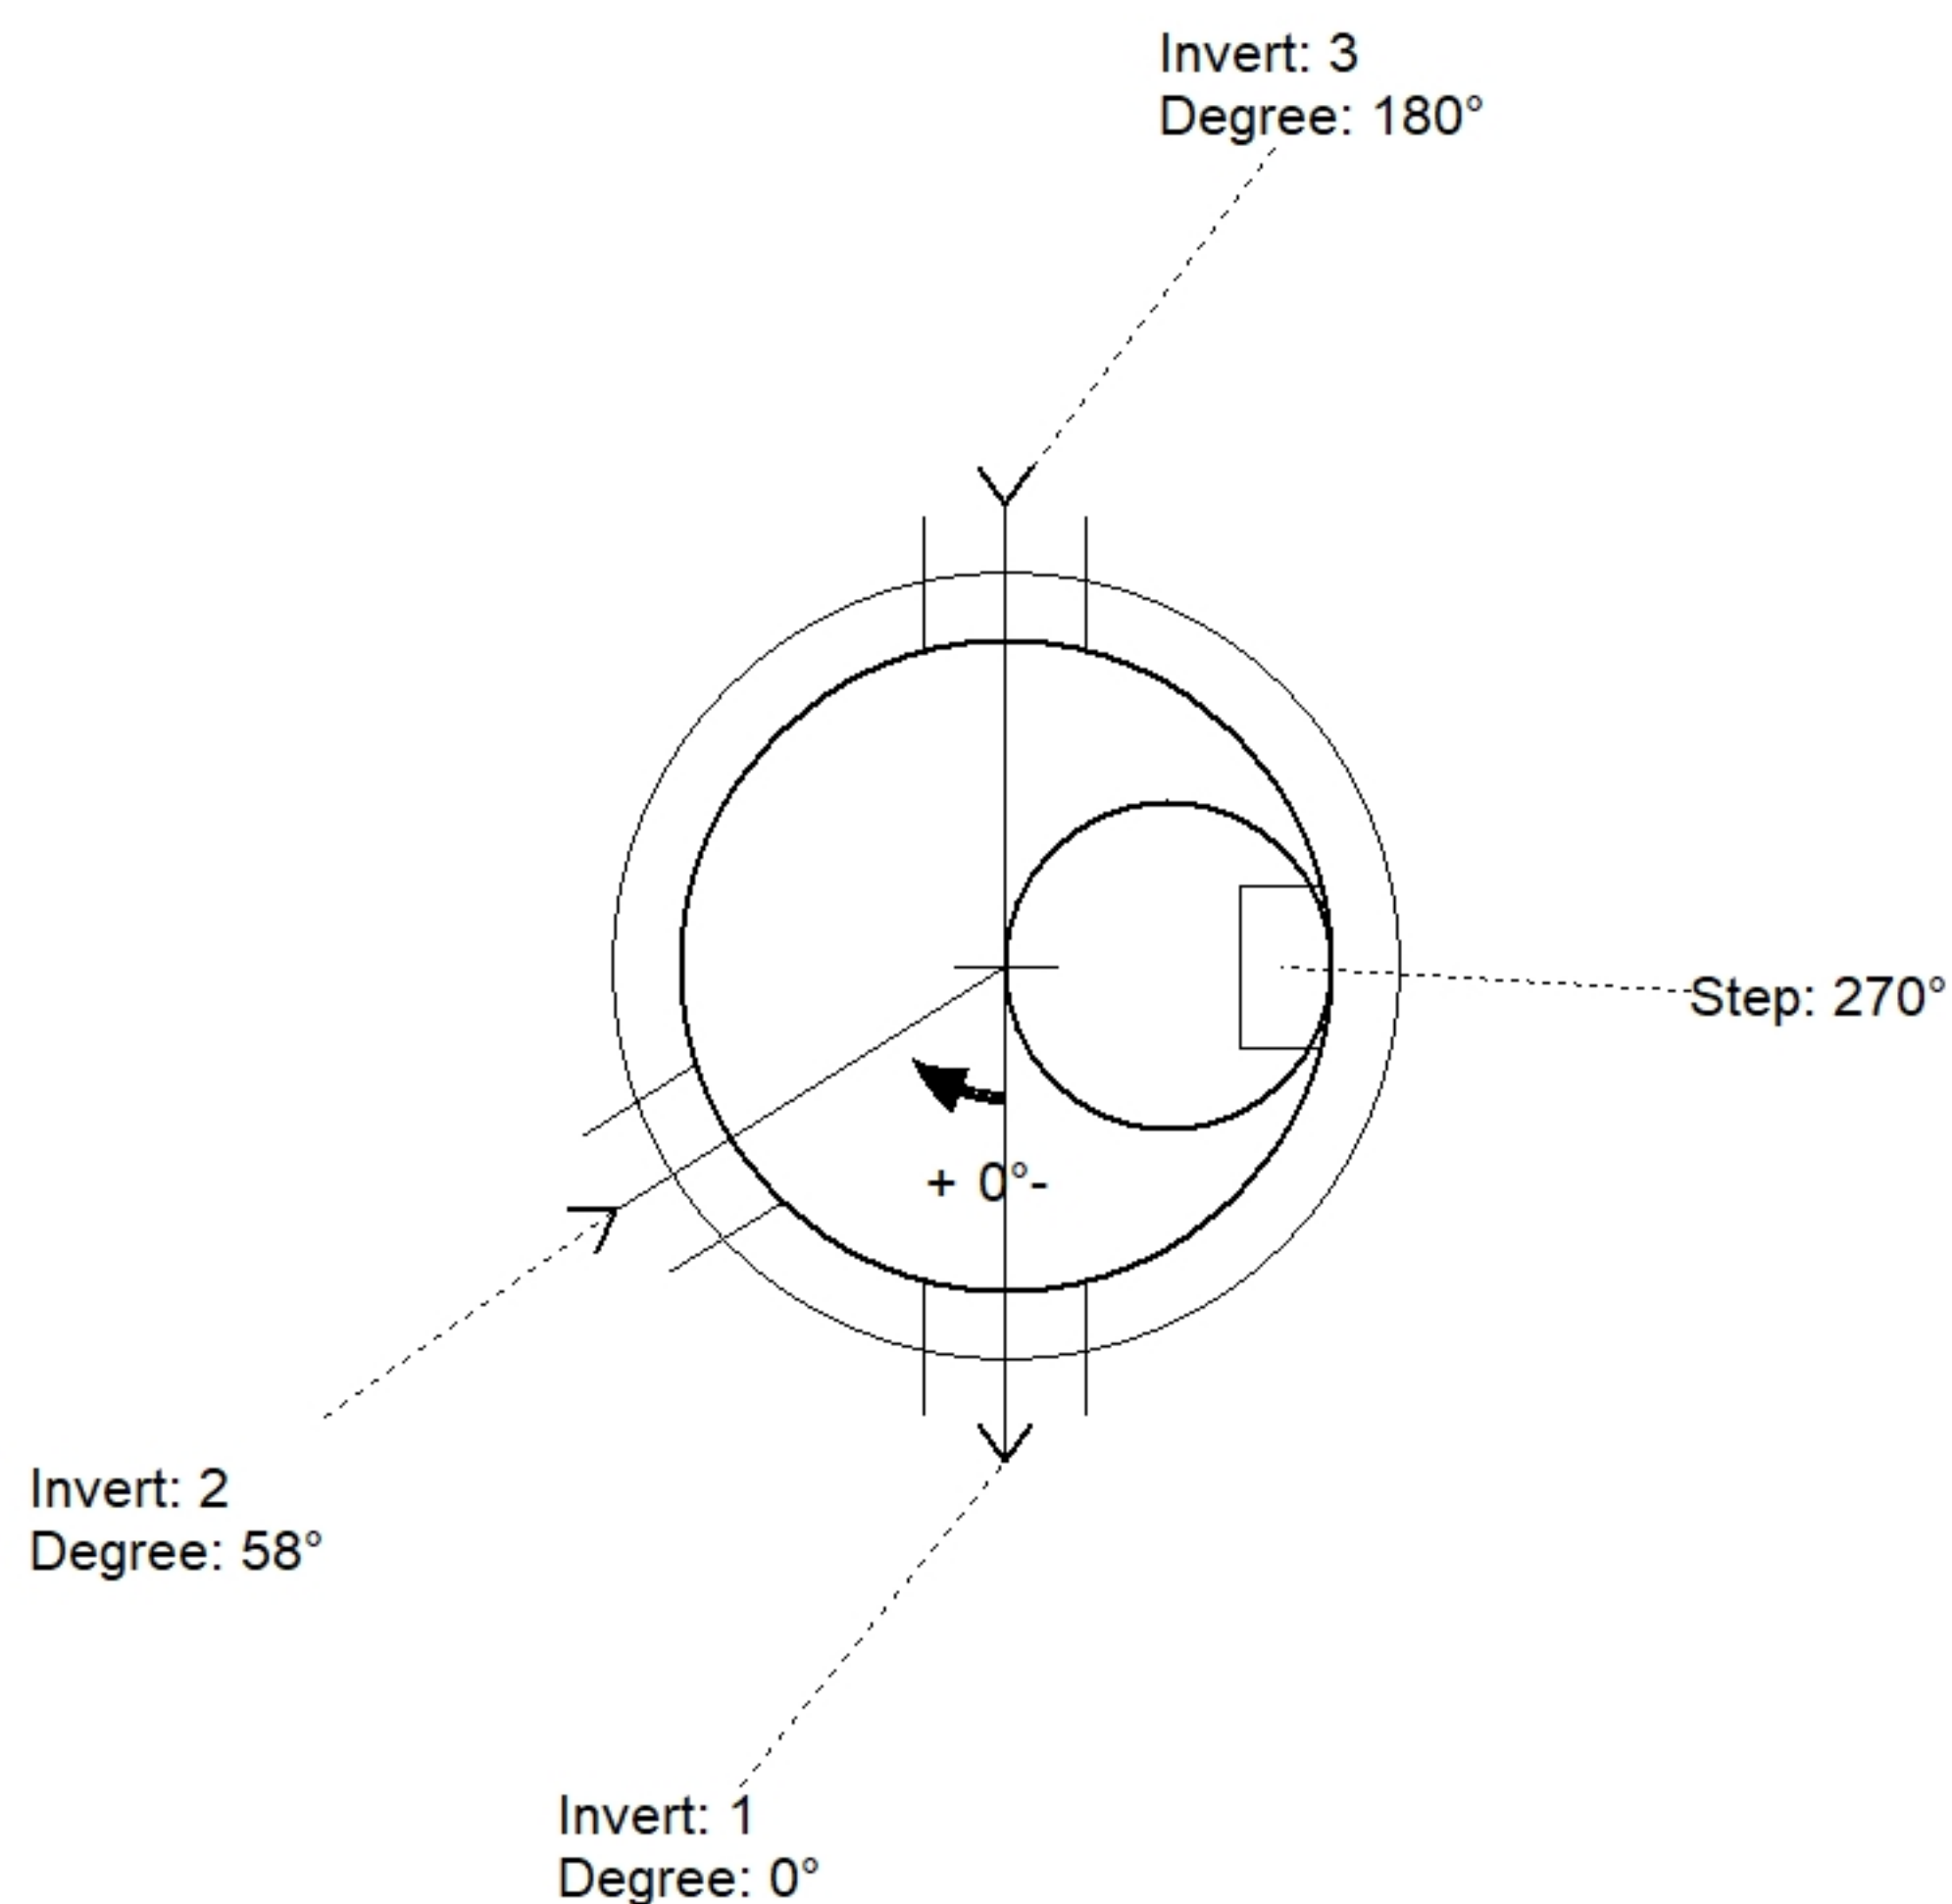

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	738.5'							
Reducer								
Invert 1	727.54'	0°	8" PVC SDR35	8.5"	12" x 16"	DOGHOUSE 12"x16"	0"	P2
Invert 2	731.1'	58°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	44.72"	P2
Invert 3	727.56'	180°	8" PVC SDR35	8.5"	12" x 16"	DOGHOUSE 12"x16"	0.24"	P2
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

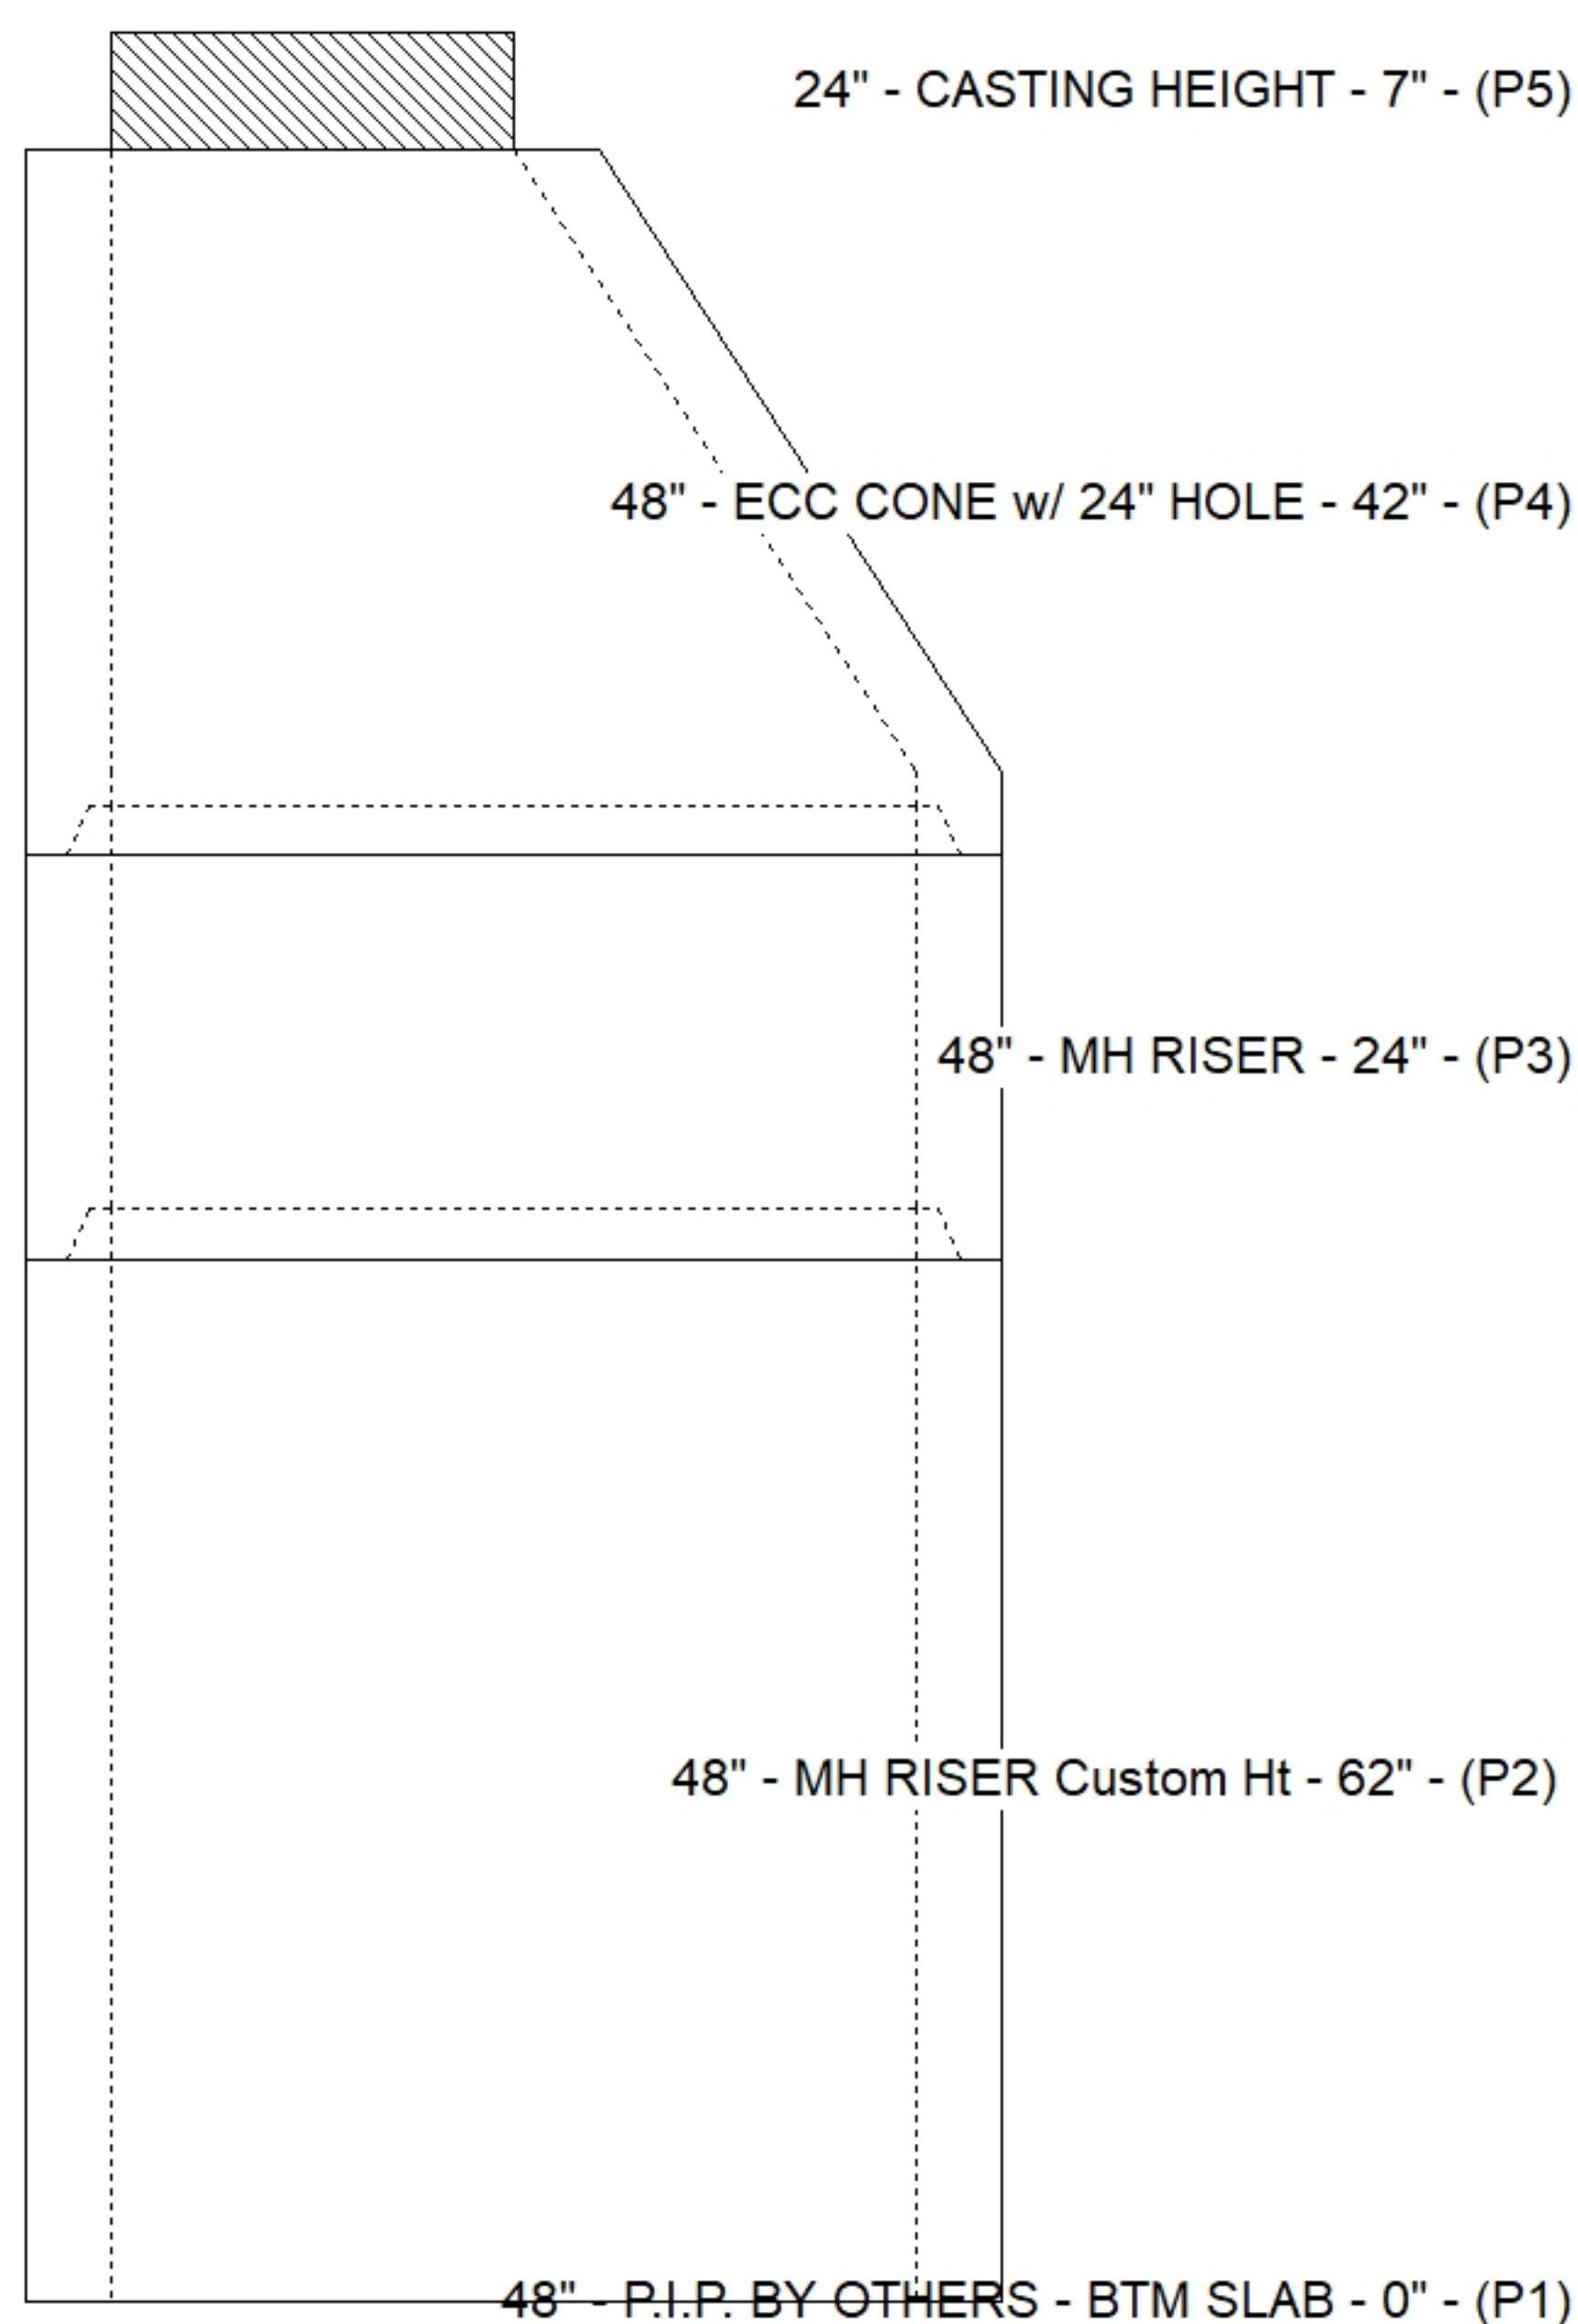

SUBMITTAL
APPROVED BY:
