

Contractor: Louisville Paving and Construction

TECH: Jared - F

Plant: 100



Size: 48"

Rim to Invert: 7.09'

Floor Height: 6"

Slack: 0.08"


REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

- P3) 32" x 32" - CASTING HEIGHT - 3"
- P2) 48" - MH FLAT TOP w/32"x32" Hole - 12"
- P1) 48" - MH BASE Custom Ht - 70"
- 1) CASTING - HOE 595 F/G
- 1) 48" - Conseal CS-102 1.00"
- 1) 32" x 32" - Conseal CS-102 1.00"
- 1) Hole - 20
- 1) Hole - 22
- 1) Hole - 16


0 lb
1629 lb
5835 lb
376 lb
0 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 7840 lb

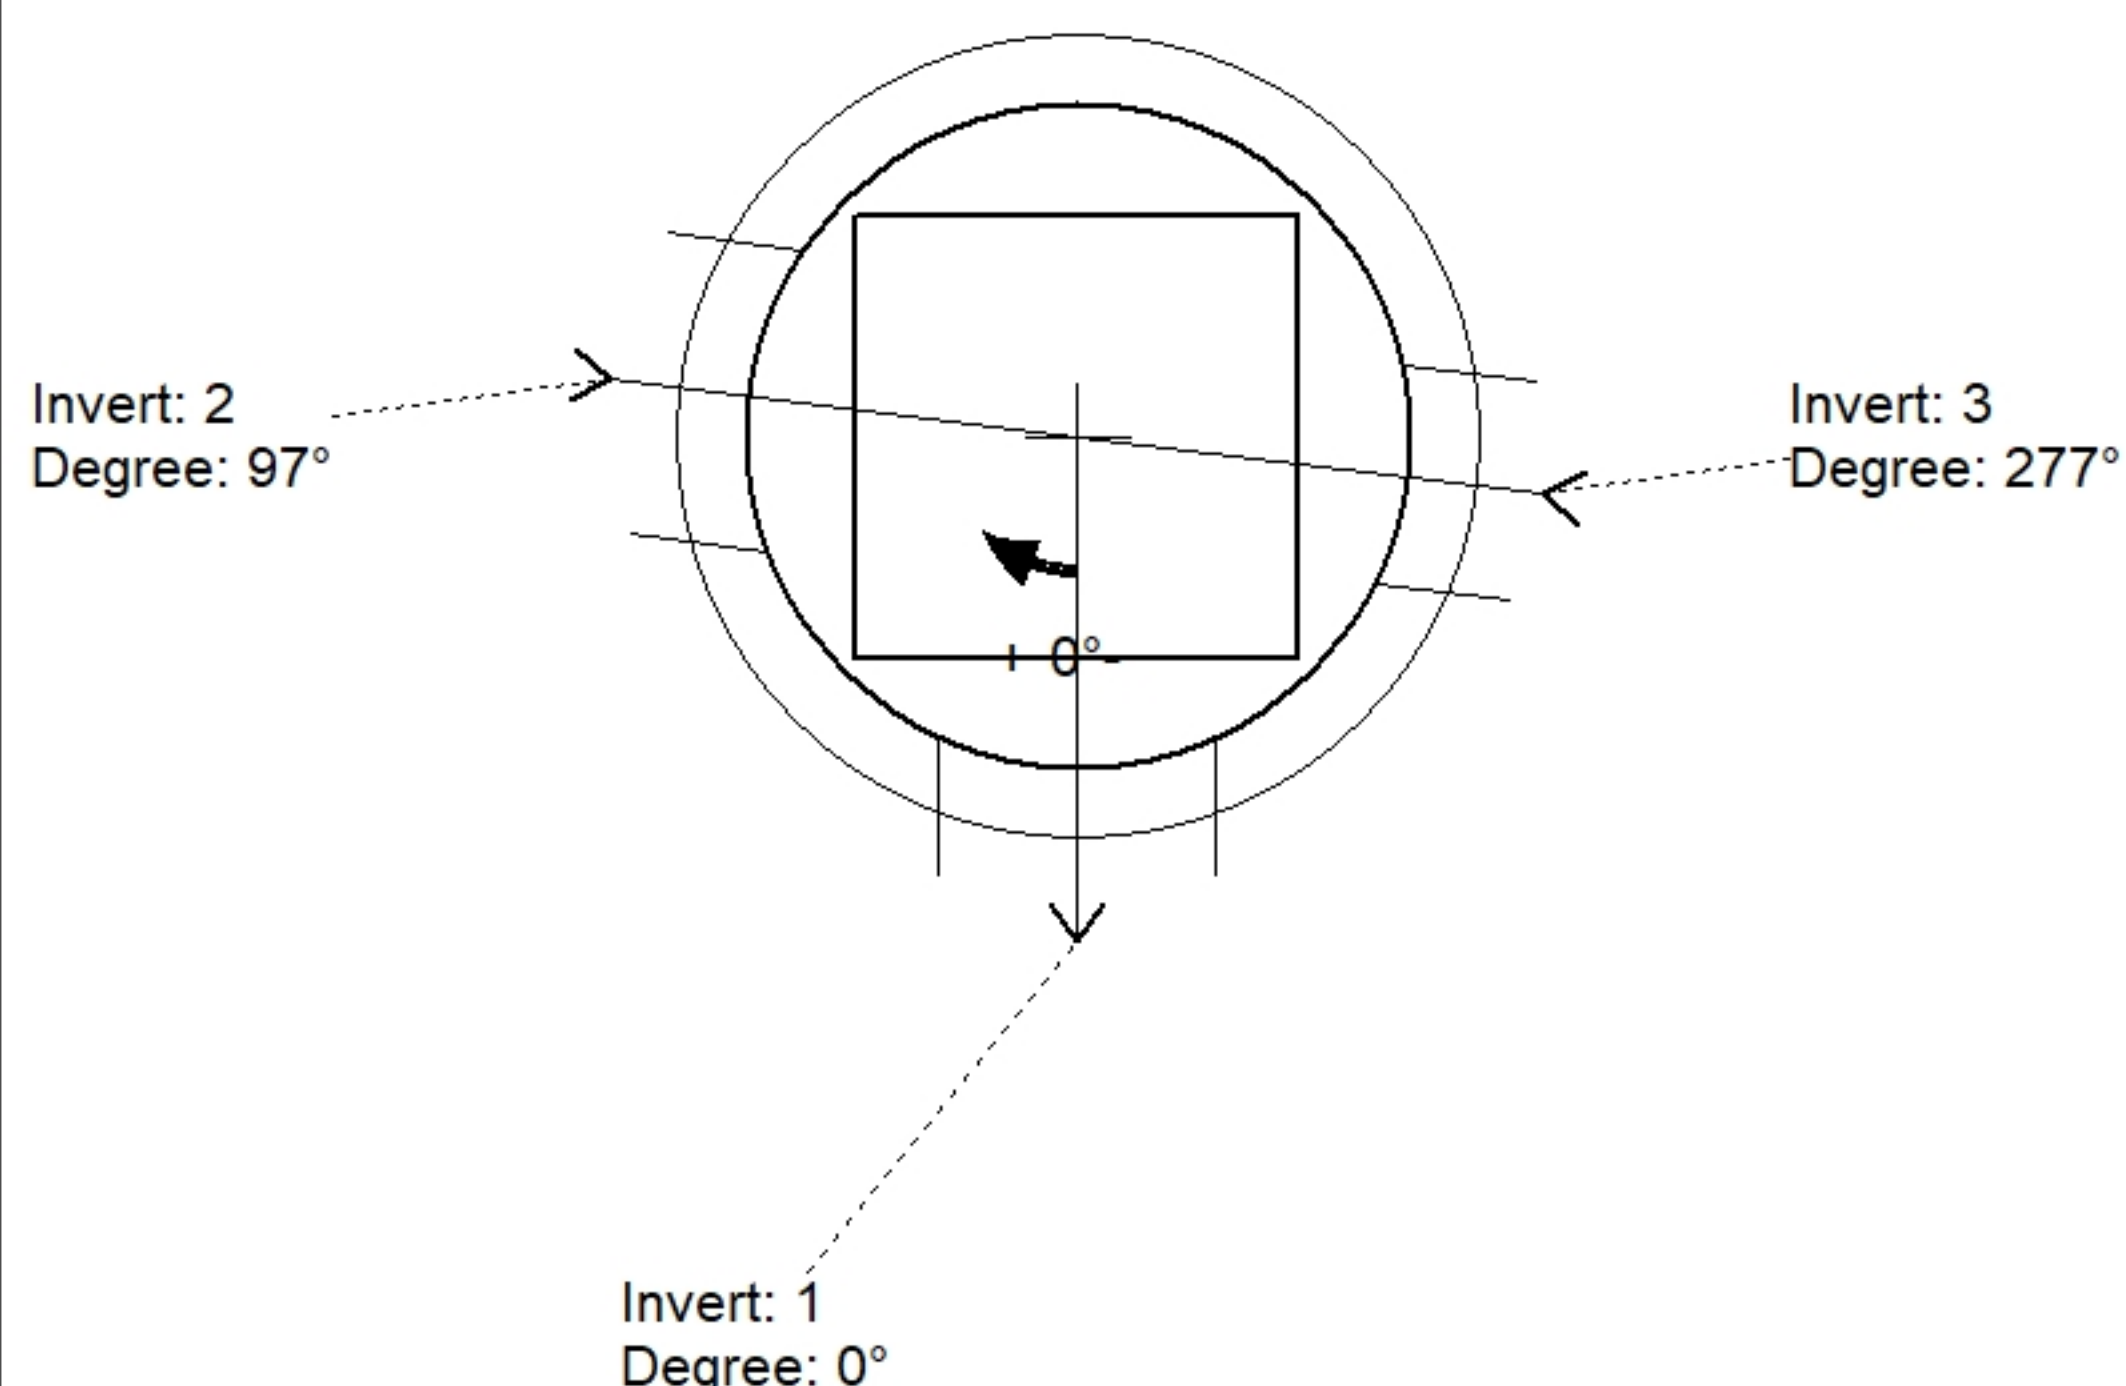

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	457.85'							
Reducer								
Invert 1	450.76'	0°	15" HDPE	17.6"	20"	Hole 20	-1.3"	P1
Invert 2	450.76'	97°	15" RCP B WALL	19.5"	22"	Hole 22	-2.25"	P1
Invert 3	454.38'	277°	12" HDPE	14.5"	16"	Hole 16	42.19"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

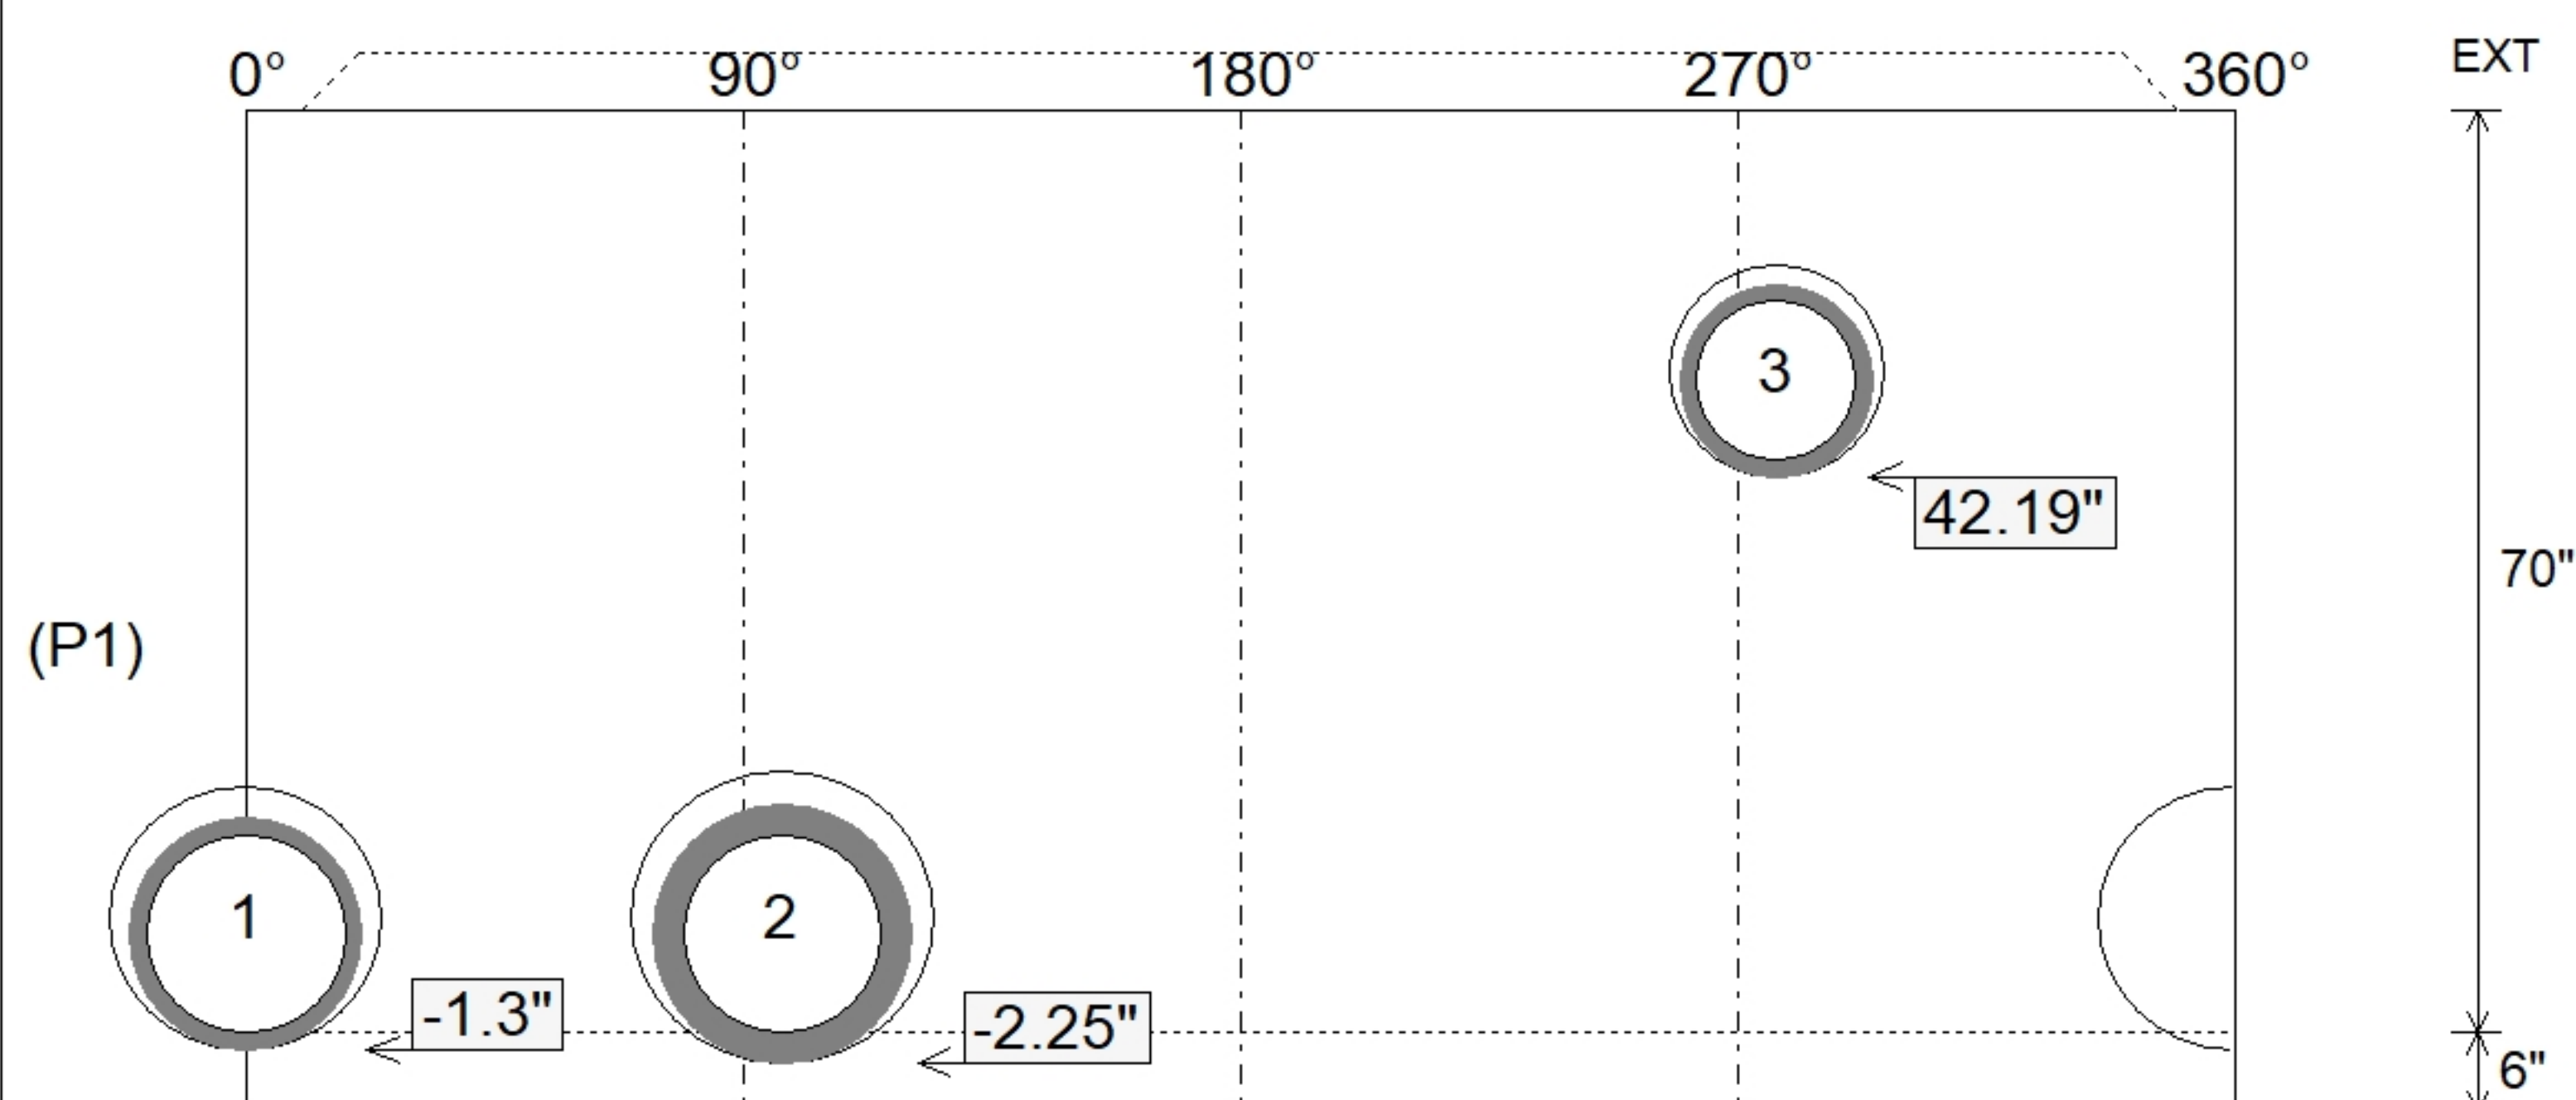

Submittal Drawing
5/6/2026 8:50:35 AM

SUBMITTAL
APPROVED BY:
