

Contractor: Louisville Paving and Construction

TECH: Jared - F

Plant: 100



Size: 48"

Rim to Invert: 6.99'

Floor Height: 6"

Slack: 0.88"


REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

P3) 32" x 32" - CASTING HEIGHT - 3"
P2) 48" - MH FLAT TOP w/32"x32" Hole - 12"
P1) 48" - MH BASE Custom Ht - 68"
1) CASTING - HOE 595 F/G
1) 48" - Conseal CS-102 1.00"
1) 32" x 32" - Conseal CS-102 1.00"
2) Hole - 24
2) Hole - 8
1) Hole - 20


0 lb
1629 lb
5509 lb
376 lb
0 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 7514 lb

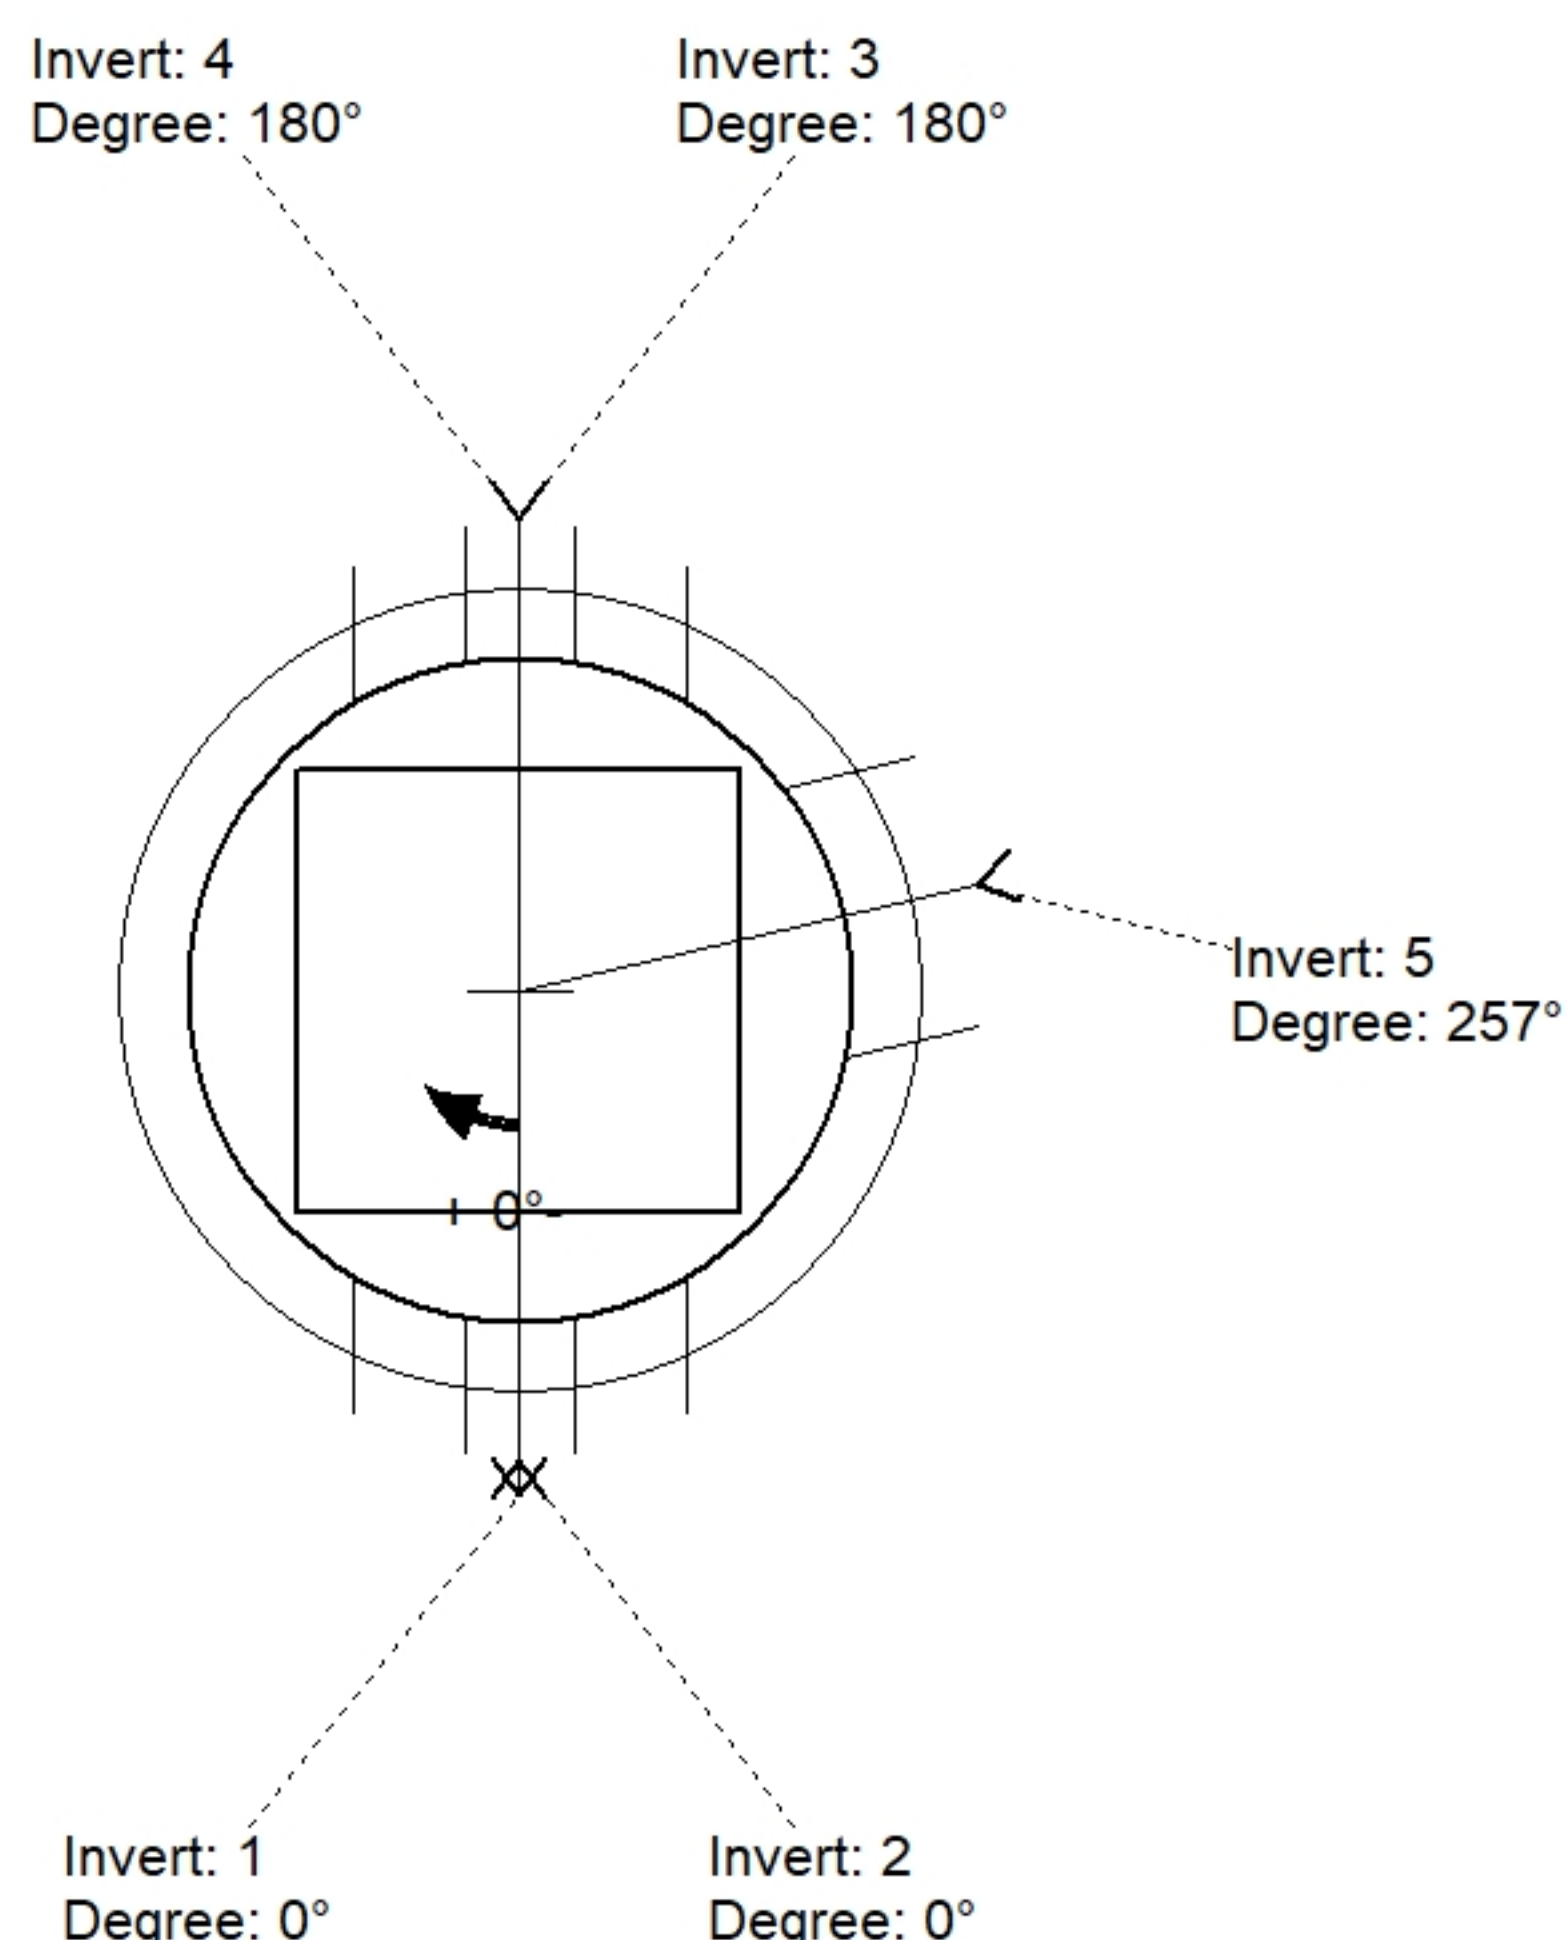

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	454.75'							
Reducer								
Invert 1	447.76'	0°	18" HDPE	21.2"	24"	Hole 24	-1.6"	P1
Invert 2	452.52'	0°	6" PVC SDR35	6.25"	8"	Hole 8	56.995"	P1
Invert 3	447.76'	180°	18" HDPE	21.2"	24"	Hole 24	-1.6"	P1
Invert 4	452.52'	180°	6" PVC SDR35	6.25"	8"	Hole 8	56.995"	P1
Invert 5	449.06'	257°	15" HDPE	17.6"	20"	Hole 20	14.3"	P1
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

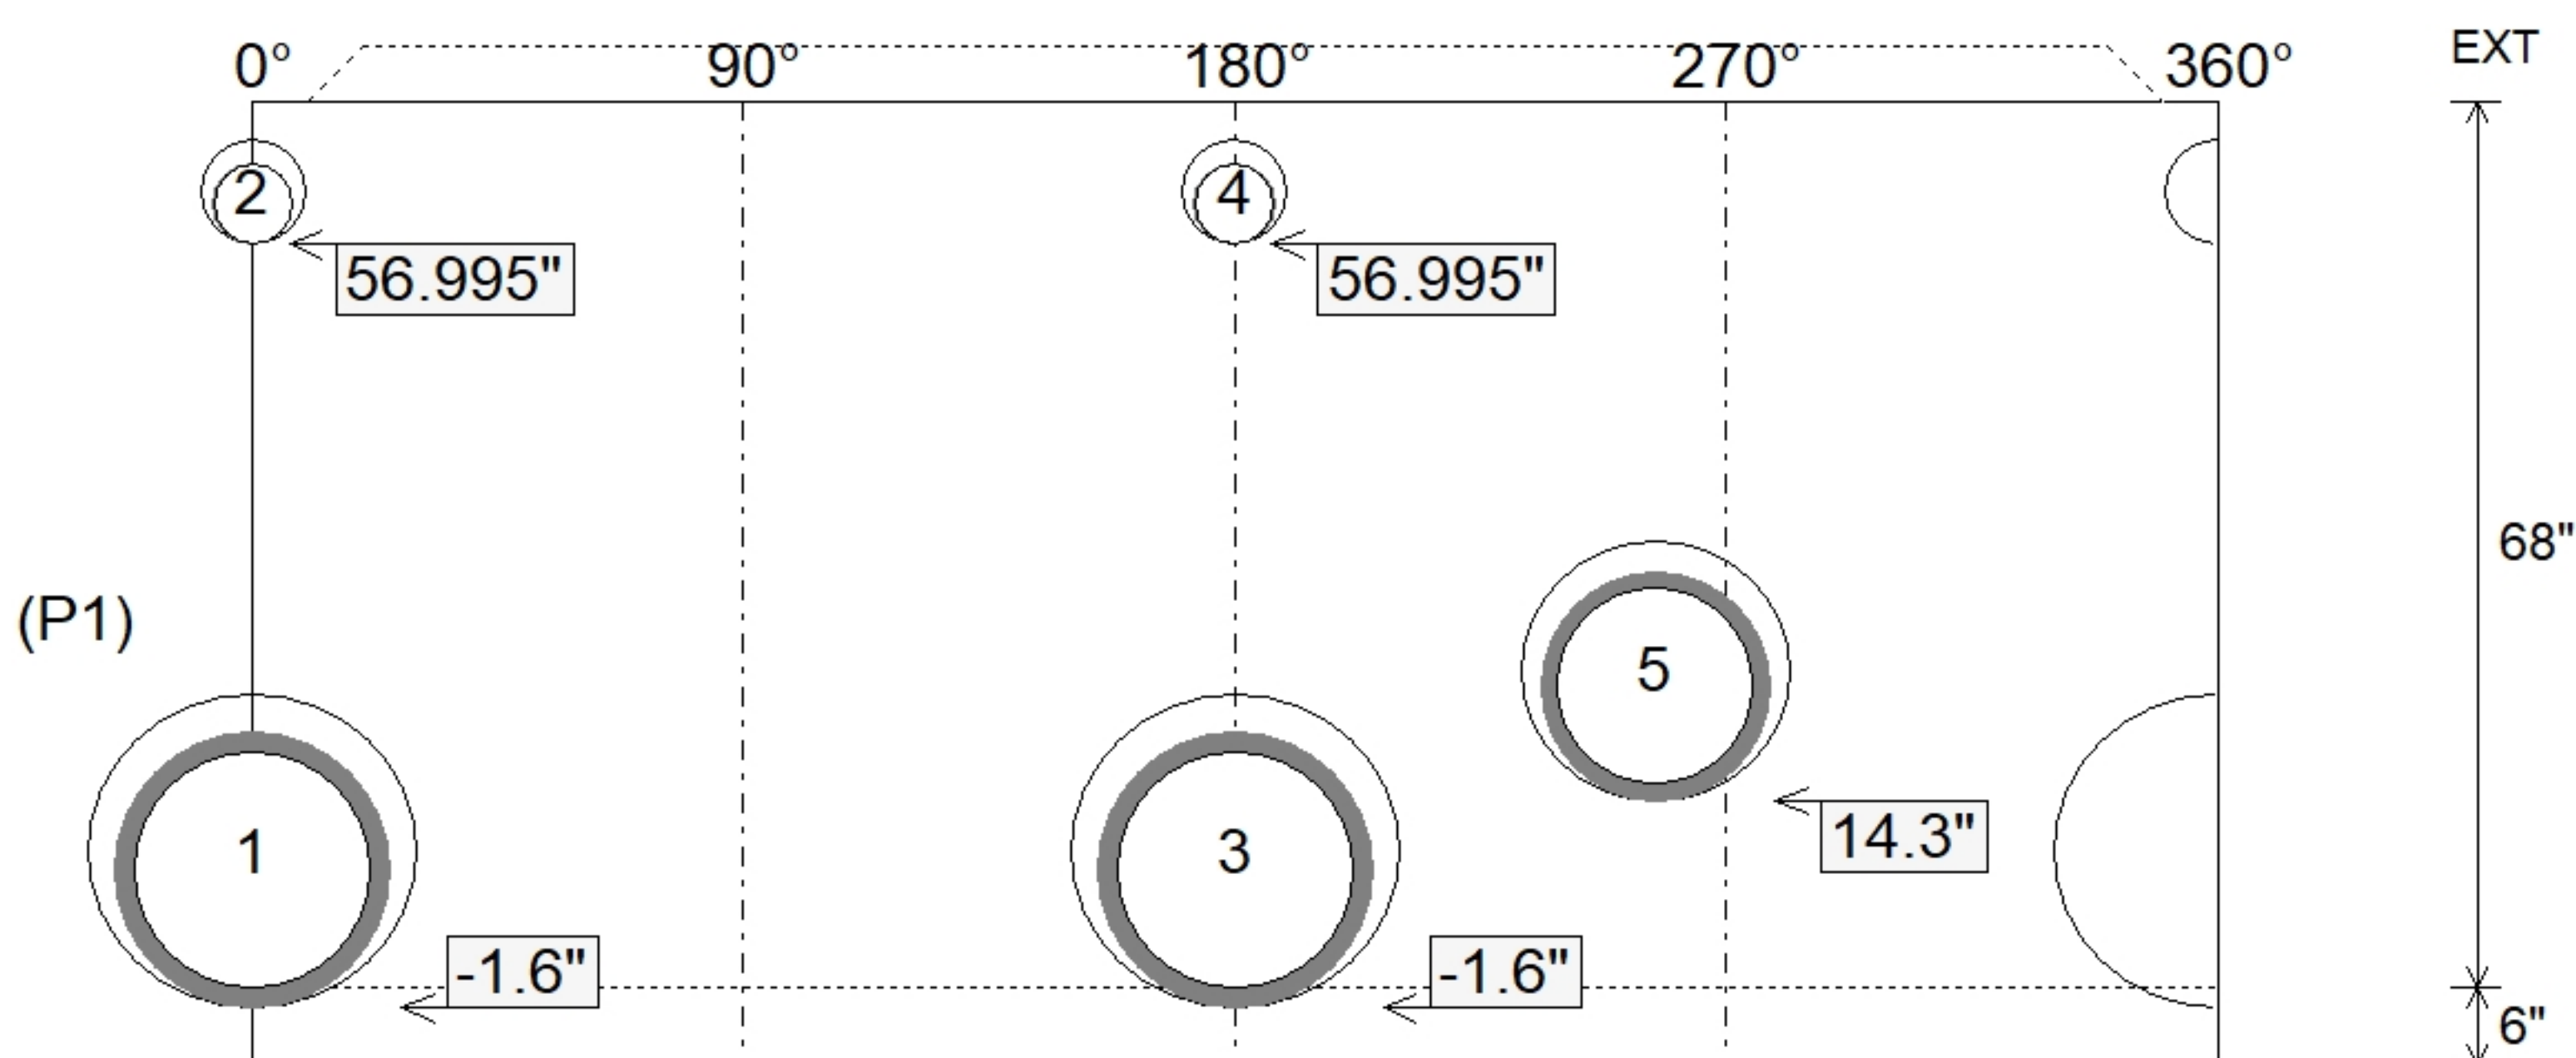

Submittal Drawing
5/6/2026 8:50:35 AM

SUBMITTAL
APPROVED BY:
