

Contractor: Louisville Paving and Construction

TECH: Jared - F

Plant: 100



Size: 48"

Rim to Invert: 7.03'

Floor Height: 6"

Slack: 0.36"


REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

P3) 32" x 32" - CASTING HEIGHT - 3"
P2) 48" - MH FLAT TOP w/32"x32" Hole - 12"
P1) 48" - MH BASE Custom Ht - 69"
1) CASTING - HOE 595 F/G
1) 48" - Conseal CS-102 1.00"
1) 32" x 32" - Conseal CS-102 1.00"
2) Hole - 24


0 lb
1629 lb
5756 lb
376 lb
0 lb
0 lb
0 lb

Structure Total: 7761 lb

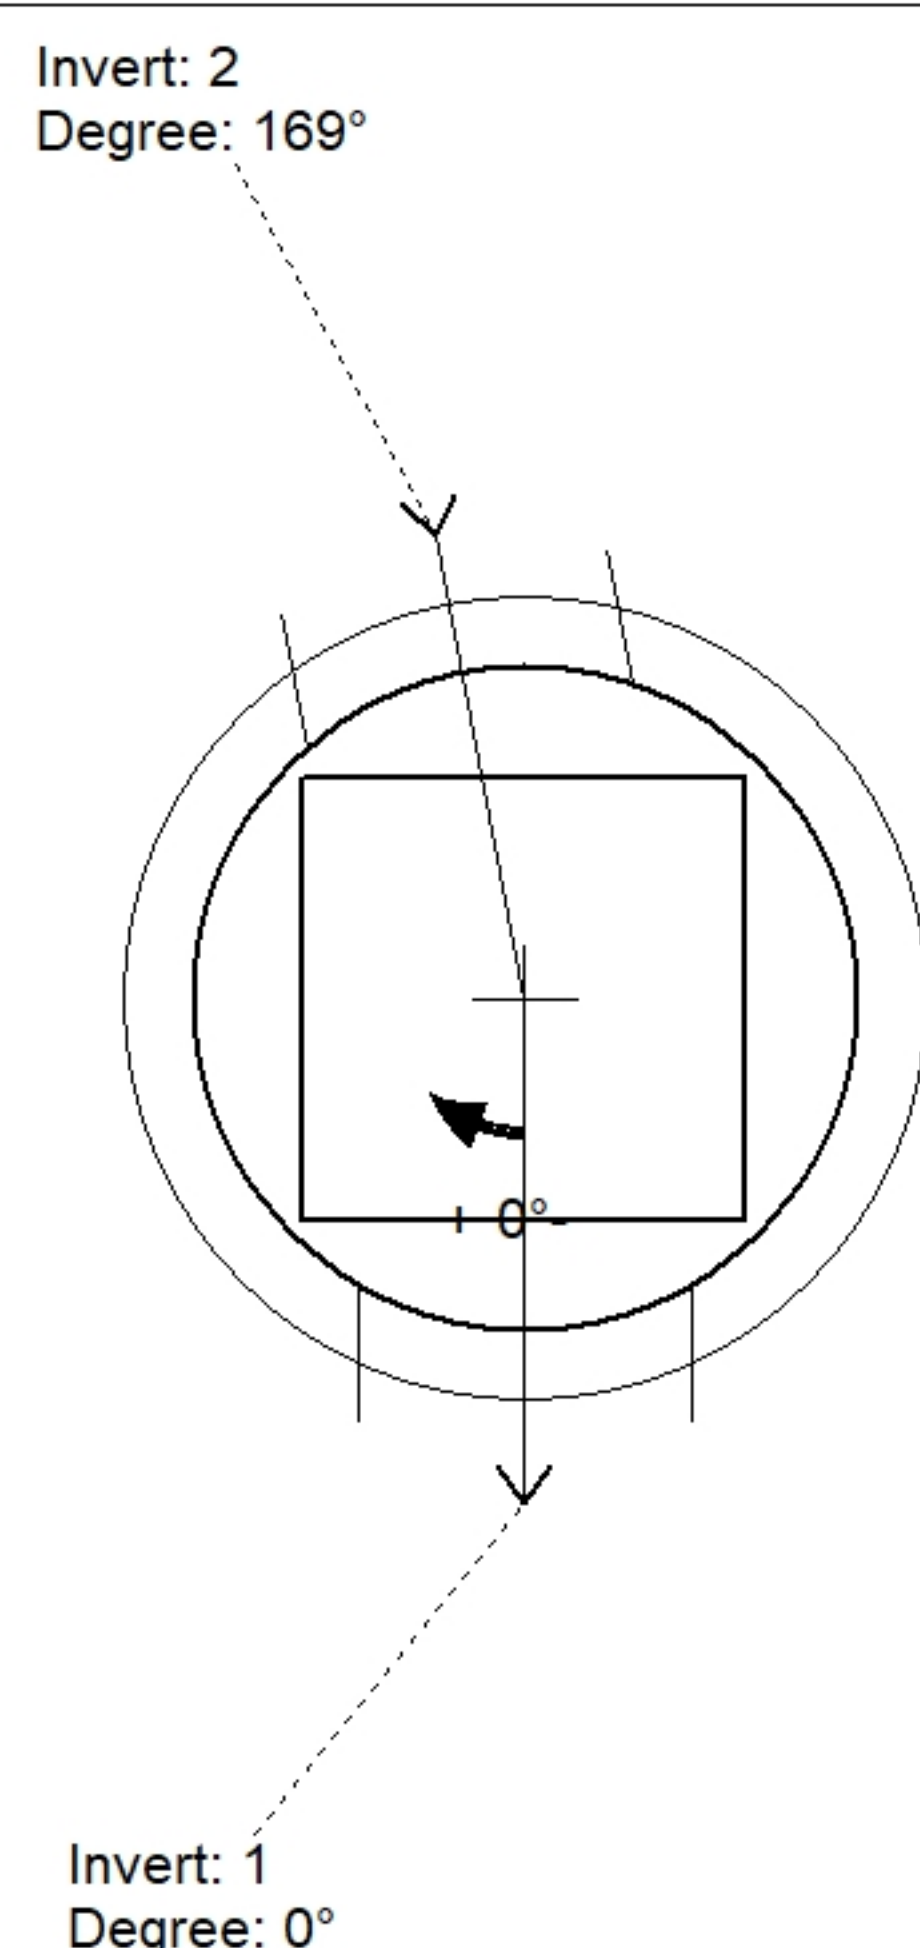

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	453.75'							
Reducer								
Invert 1	446.72'	0°	18" HDPE	21.2"	24"	Hole 24	-1.6"	P1
Invert 2	446.72'	169°	18" HDPE	21.2"	24"	Hole 24	-1.6"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

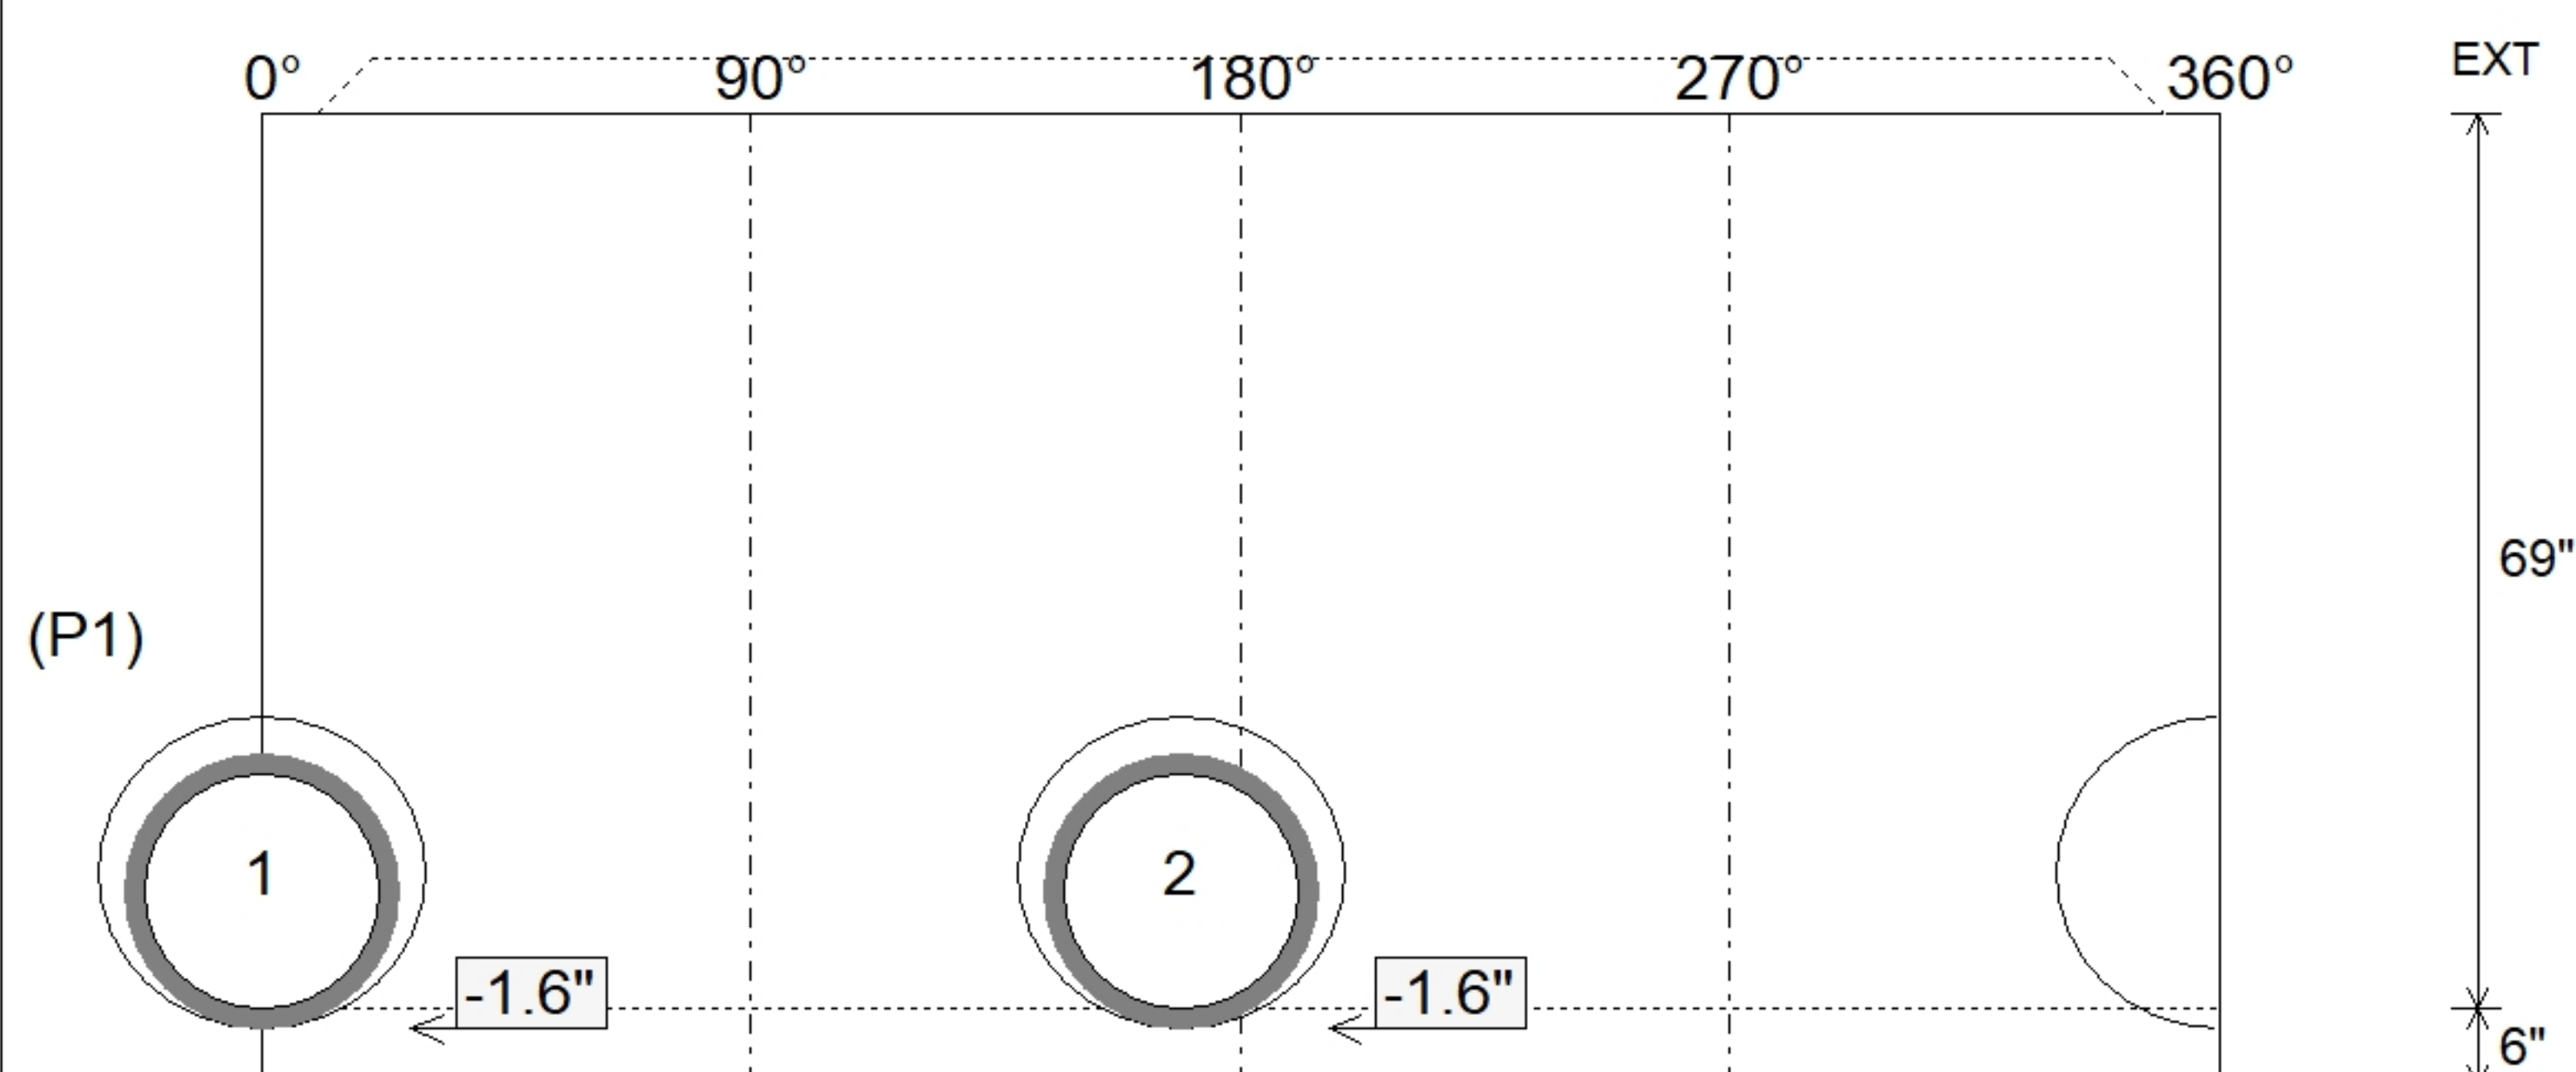

Submittal Drawing
5/6/2026 8:50:35 AM

SUBMITTAL
APPROVED BY:
