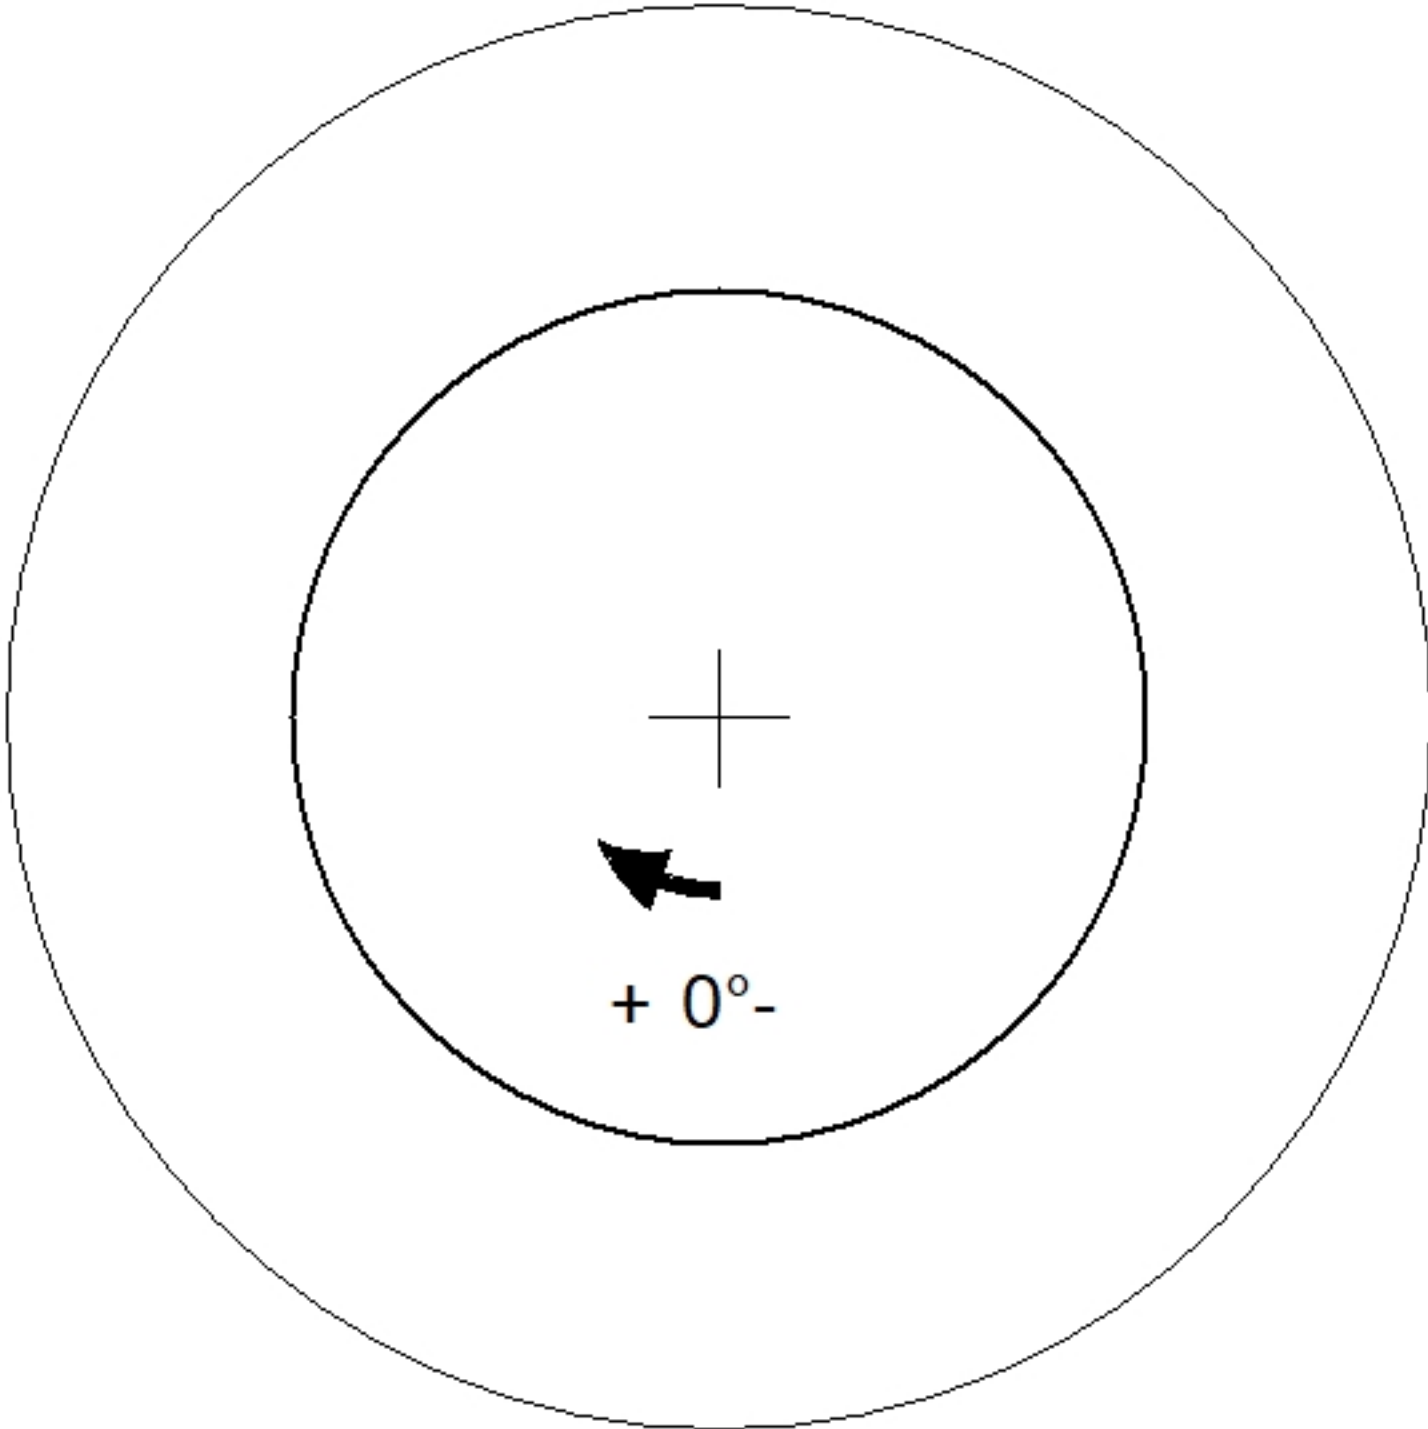


Job Name: 25-3452 - Churchill Downs Skye Terrace Improvements		Plant: 100	Tech: Jared - F	
Job Location: Louisville, KY 40208		5/6/2026 8:00:31 AM	PC: J. Jarvis	
Contractor: Louisville Paving and Construction				
Structure ID: S213				
P4 GR4		GRADE RING		
P5) 24" - CASTING HEIGHT - 7" P4) 24" - GRADE RING - 4" P3) 60" - MH FLAT TOP w/ 24" ECC Hole - 13" P2) 60" - MH RISER SPECIAL - 36" P1) 60" - MH BASE Custom Ht - 43" 1) CASTING - HOE MC-420 F/C Storm 2) 60" - Conseal CS-102 1.00" 2) Hole - 30 1) Hole - 16 7) MH Step ML-10-TDS-NCR - 10"		0 lb 270 lb 2869 lb 3656 lb 6482 lb 340 lb 0 lb 0 lb 0 lb 0 lb ----- 13617 lb Structure Total:	Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE MC-420 F/C STORM) REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .18) - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.	
				
24" - GRADE RING - 4" - (P4)				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Flat	Wall Thickness: 8"	Height (Ext): 4"	Weight (Net): 270 lb Volume (Net): 0.07cu.yd
