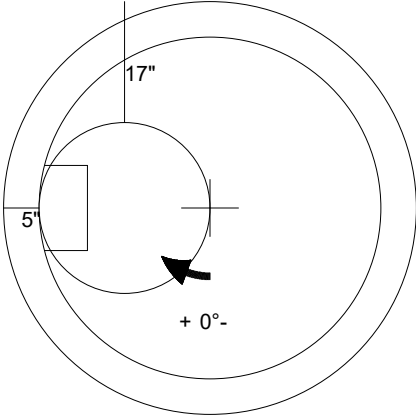



Job Name: 25-3452 - Churchill Downs Skye Terrace Improvements		Plant: 100	Tech: Jared - F	
Job Location: Louisville, KY 40208		7/27/2026 1:04:28 PM	PC: J. Jarvis	
Contractor: Louisville Paving and Construction				
Structure ID: MH 129266				
P3 MH048CN36		ECC CONE w/ 24" HOLE F/G		
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE F/G - 36" P2) 48" - MH RISER T/G - 60" P1) 48" - MH BASE T/n - 30" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-420 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 1) PSX - 16Y NYLO 2) PSX - 12-08 NYLO 9) MH Step ML-10-TDS-NCR - 10"		0 lb 3000 lb 4192 lb 3244 lb 0 lb 0 lb 1440 lb 340 lb 0 lb 0 lb 8 lb 16 lb 0 lb ----- 12240 lb Structure Total:	Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-420 F/C SANITARY). . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
				
 48" - ECC CONE w/ 24" HOLE F/G - 36" - (P3)				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 36"	Weight (Net): 3000 lb Volume (Net): 0.5cu.yd
