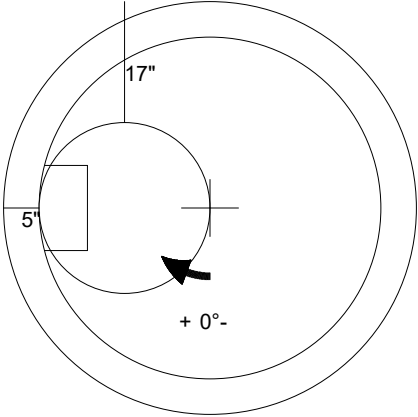



Job Name: 25-3452 - Churchill Downs Skye Terrace Improvements		Plant: 100	Tech: Jared - F	
Job Location: Louisville, KY 40208		7/27/2026 1:04:27 PM	PC: J. Jarvis	
Contractor: Louisville Paving and Construction				
Structure ID: MH 129267				
P2 MH048CN42		ECC CONE w/ 24" HOLE F/G		
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE F/G - 42" P1) 48" - MH BASE T/n - 36" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-420 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 6) MH Step ML-10-TDS-NCR - 10"		0 lb 3200 lb 3749 lb 0 lb 0 lb 1440 lb 340 lb 0 lb 0 lb 0 lb 16 lb 0 lb ----- 8745 lb Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-420 F/C SANITARY). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.		
				
 48" - ECC CONE w/ 24" HOLE F/G - 42" - (P2)				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 42"	Weight (Net): 3200 lb Volume (Net): 0.5cu.yd
