

Job Name: 25-3452 - Churchill Downs Skye Terrace Improvements Job Location: Louisville, KY 40208 Contractor: Louisville Paving and Construction					Plant: 100		Tech: Jared - F					
					7/27/2026 1:03:50 PM		PC: J. Jarvis					
Structure ID: MH 129268												
P1 MH048BA30			MH BASE T/n									
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE F/G - 36" P1) 48" - MH BASE T/n - 30" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-420 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 3) PSX - 12-08 NYLO 5) MH Step ML-10-TDS-NCR - 10"						0 lb 3000 lb 3282 lb 0 lb 0 lb 1440 lb 340 lb 0 lb 0 lb 0 lb 24 lb 0 lb ----- Structure Total: 8086 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-420 F/C SANITARY). . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 454.55' Rim to Invert: 5.94' Slack: 1.28" Sump: 3" Step Position: 270°												
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1	448.61'	0°	0"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	1"	0"		
Invert 2	448.71'	114°	57.75"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	2.25"	0"		
Invert 3	448.71'	211°	106.75"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	2.25"	0"		
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												

RIGHT-SIDE UP VIEW (int. dimensions)


UPSIDE-DOWN VIEW (int. dimensions)

INSIDE WALL DIMENSIONS


Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 30" Height (Ext): 36"	Weight (Net): 3282 lb Volume (Net): 0.84cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 25-3452 - Churchill Downs Skye Terrace Improvements Job Location: Louisville, KY 40208 Contractor: Louisville Paving and Construction					Plant: 100 7/27/2026 1:03:50 PM		Tech: Jared - F PC: J. Jarvis						
Structure ID: MH 129268													
P1		MH048BA30		MH BASE T/n									
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE F/G - 36" P1) 48" - MH BASE T/n - 30" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-420 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 3) PSX - 12-08 NYLO 5) MH Step ML-10-TDS-NCR - 10"						0 lb 3000 lb 3282 lb 0 lb 0 lb 1440 lb 340 lb 0 lb 0 lb 0 lb 24 lb 0 lb ----- 8086 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-420 F/C SANITARY). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.					
Rim: 454.55' Rim to Invert: 5.94' Slack: 1.28' Sump: 3' Step Position: 270°													
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset			
Invert 1	448.61'	0°	0"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	1"	0"			
Invert 2	448.71'	114°	57.75"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	2.25"	0"			
Invert 3	448.71'	211°	106.75"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	2.25"	0"			
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													


RIGHT-SIDE UP VIEW (int. dimensions)

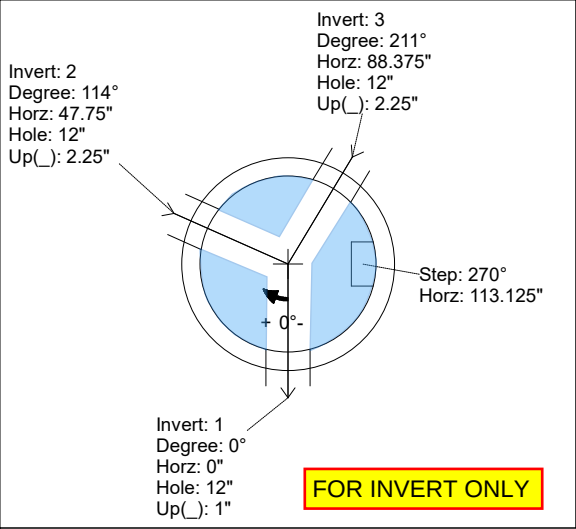

UPSIDE-DOWN VIEW (int. dimensions)

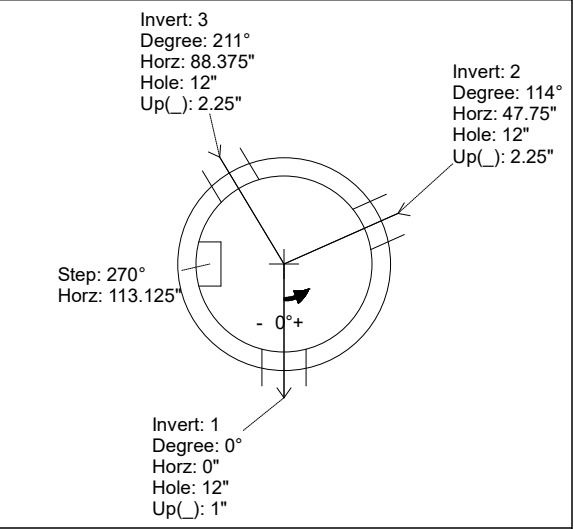

INSIDE WALL DIMENSIONS

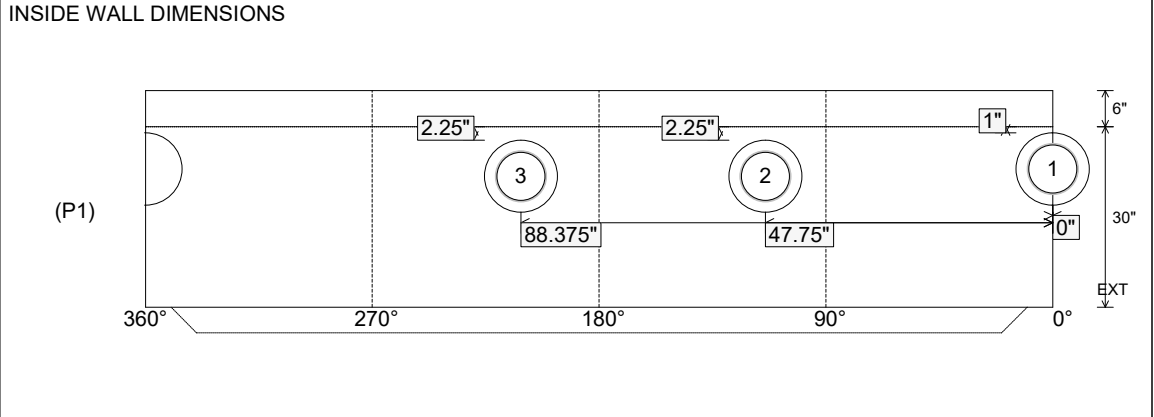

Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: n/a

Wall Thickness: 5"
Floor Height: 6"

Height (Int): 30"
Height (Ext): 36"

Weight (Net): 3282 lb
Volume (Net): 0.84cu.yd
