




Job Name: 25-3452 - Churchill Downs Skye Terrace Improvements Job Location: Louisville, KY 40208 Contractor: Louisville Paving and Construction					Plant: 100 7/27/2026 1:03:52 PM		Tech: Jared - F PC: J. Jarvis				
Structure ID: MH 129269											
P1 MH048BA30		MH BASE T/n									
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE F/G - 36" P1) 48" - MH BASE T/n - 30" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-420 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 NYLO 1) Quik-Lok - QL-04-C 5) MH Step ML-10-TDS-NCR - 10"					0 lb 3000 lb 3359 lb 0 lb 0 lb 1440 lb 340 lb 0 lb 0 lb 0 lb 8 lb 1 lb 0 lb ----- Structure Total: 8148 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-420 F/C SANITARY). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 455.27' Rim to Invert: 5.98' Slack: 1.76" Sump: 3" Step Position: 90°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	449.29'	0°	0"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	1"	0"	
Invert 2	449.39'	209°	105.75"	4" PVC SDR26	4.25"	Quik-Lok QL-04-C	7.5"	7.531"	2.5"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

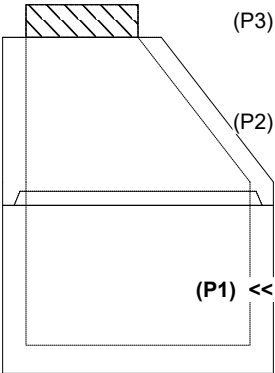


RIGHT-SIDE UP VIEW (int. dimensions)

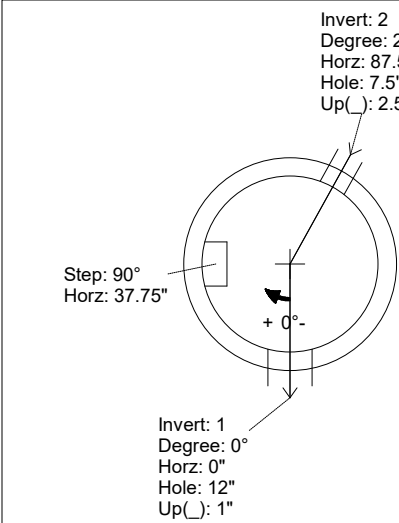

UPSIDE-DOWN VIEW (int. dimensions)

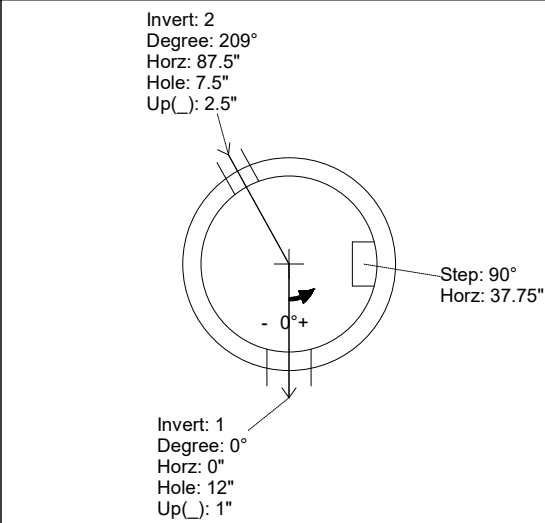

INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 30" Height (Ext): 36"	Weight (Net): 3359 lb Volume (Net): 0.86cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 25-3452 - Churchill Downs Skye Terrace Improvements Job Location: Louisville, KY 40208 Contractor: Louisville Paving and Construction					Plant: 100		Tech: Jared - F					
					7/27/2026 1:03:52 PM		PC: J. Jarvis					
Structure ID: MH 129269												
P1 MH048BA30			MH BASE T/n									
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE F/G - 36" P1) 48" - MH BASE T/n - 30" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-420 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 NYLO 1) Quik-Lok - QL-04-C 5) MH Step ML-10-TDS-NCR - 10"						0 lb 3000 lb 3359 lb 0 lb 0 lb 1440 lb 340 lb 0 lb 0 lb 0 lb 8 lb 1 lb 0 lb ----- Structure Total: 8148 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-420 F/C SANITARY). . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 455.27' Rim to Invert: 5.98' Slack: 1.76" Sump: 3" Step Position: 90°												
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1	449.29'	0°	0"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	1"	0"		
Invert 2	449.39'	209°	105.75"	4" PVC SDR26	4.25"	Quik-Lok QL-04-C	7.5"	7.531"	2.5"	0"		
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

INSIDE WALL DIMENSIONS

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 30" Height (Ext): 36"	Weight (Net): 3359 lb Volume (Net): 0.86cu.yd
----------------------------------	---------------------------------	--	--	--
