



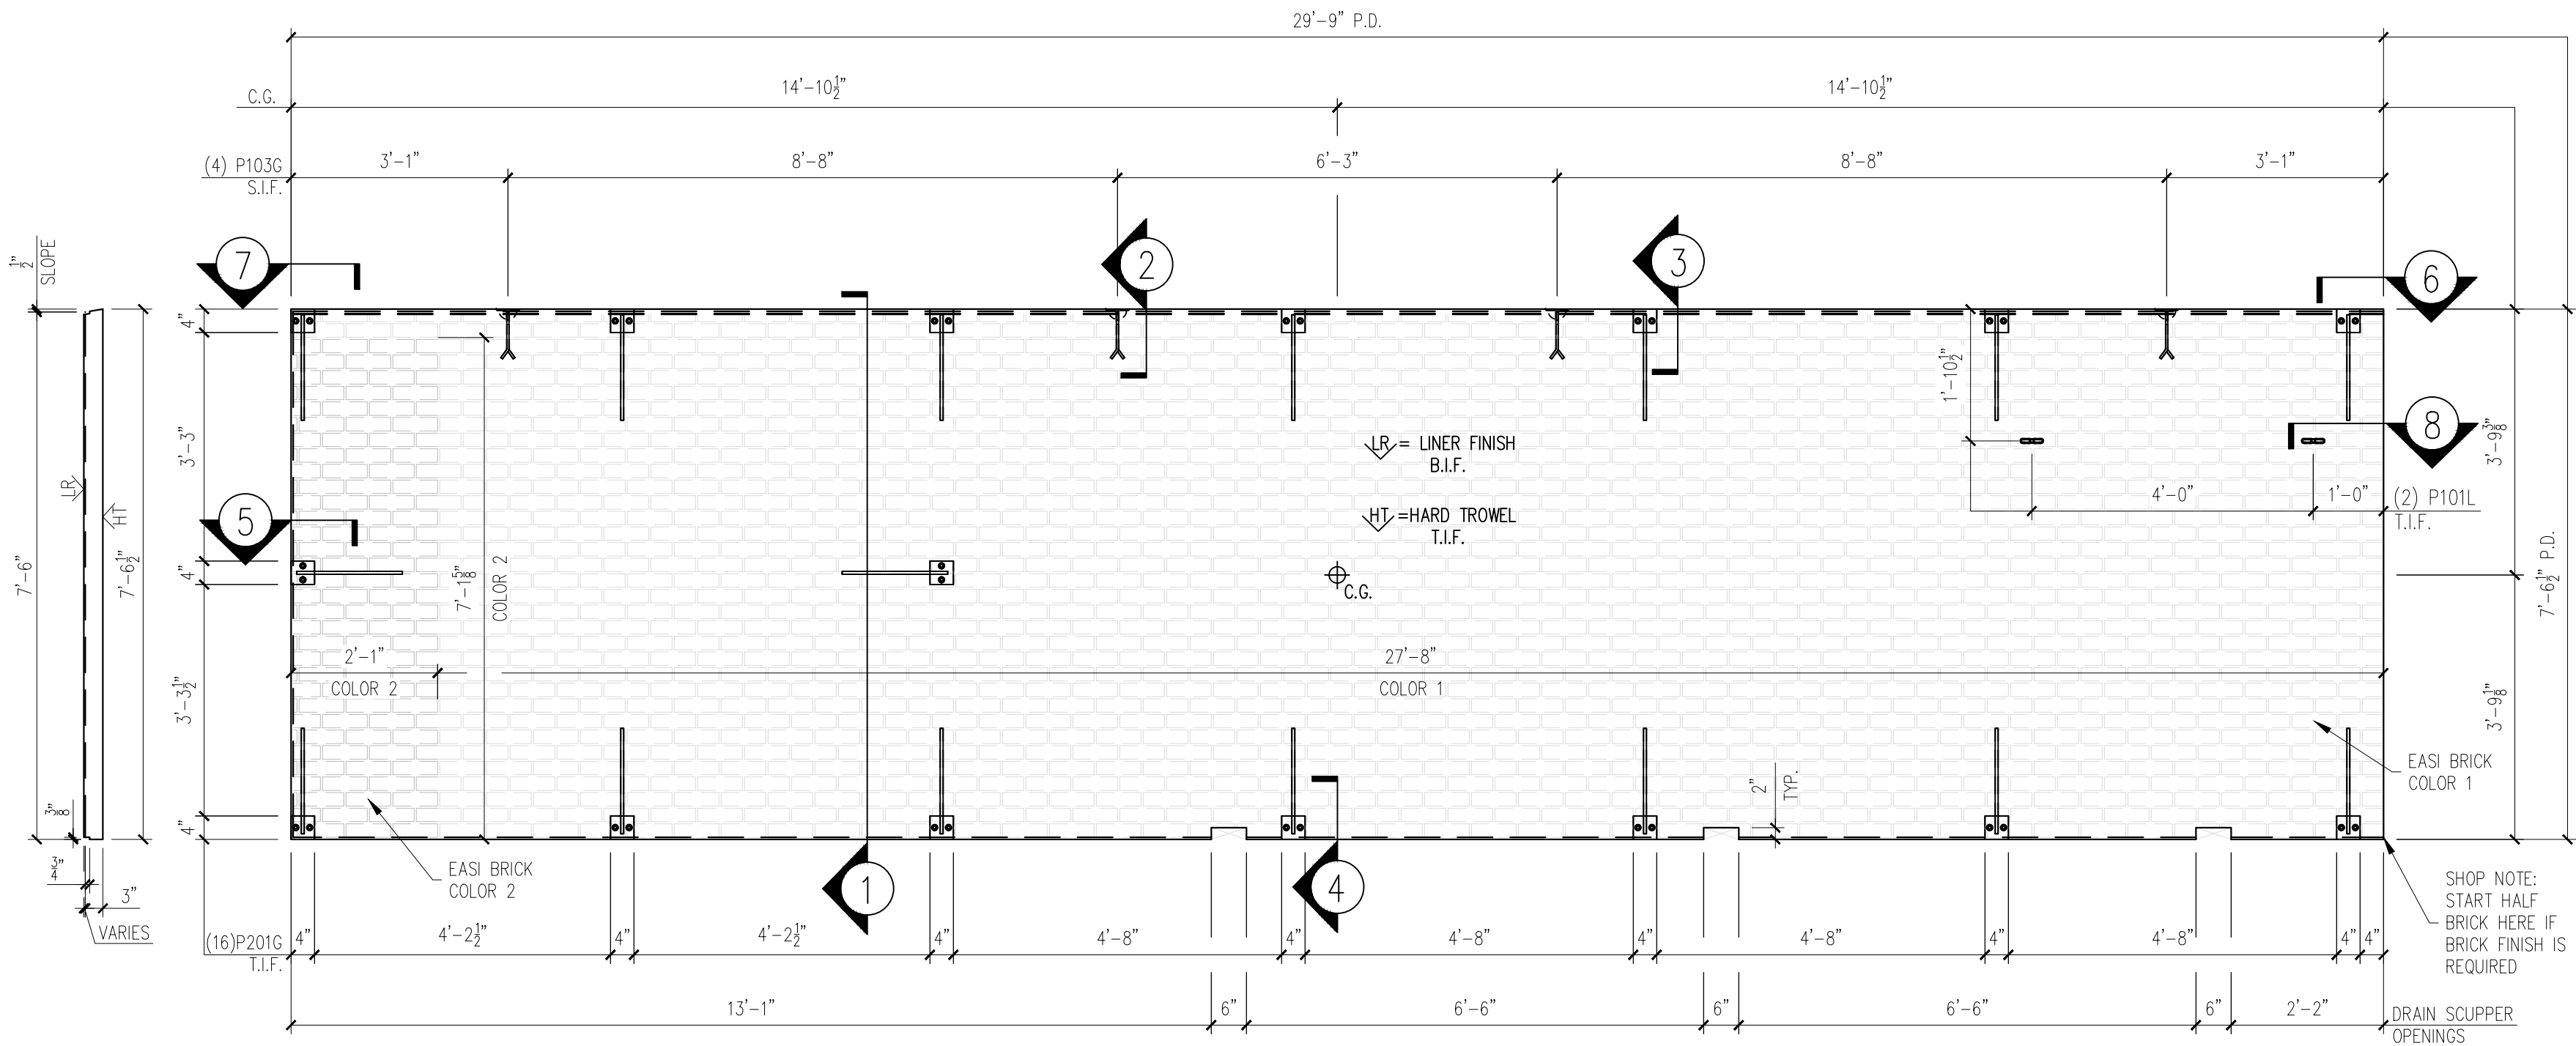

25-3470P6
Baseball Dugout 7B
ID - CVW
Floor - WP-03
Weight - 9,055
1 Required

FORM VIEW
SCALE: 1/2" = 1'-0"

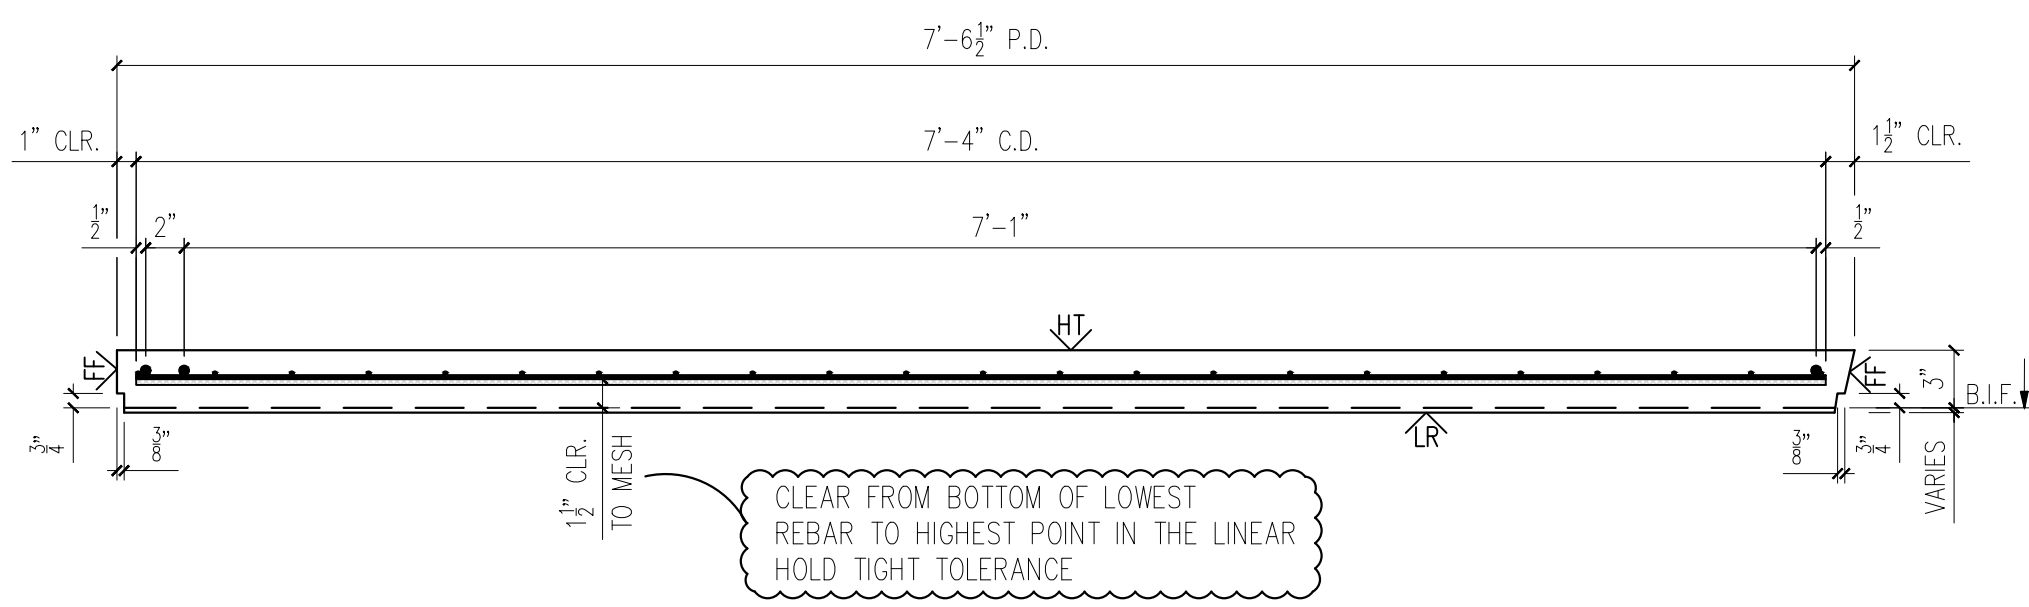

1

MESSAGE CENTER

1. REFER TO DETAILS AND SECTION FOR REINFORCEMENT PLACEMENT

2. SHOP TICKET SHOWS EXTERIOR FINISH CAST FACE DOWN

CHECKED BY: DATE: APPROVED BY: DATE:

BILL OF MATERIALS		
MARK #	DESCRIPTION	QTY.
P103G	2 TON RL-4 TECH ERECTION ANCHOR (79527) (GALV.)	4
P201G	4"x4"x8" W/(2) 8"ØX1 1/2" HAS W/1'-4" BENT REBAR	16
P101L	3/8"Ø X 1 1/2" F-63 FLARED THIN SLAB COIL INSERT (ELECTROPLATED)	2
HANDLING INSTRUCTIONS		
STRIPPING-TILT TABLE		
SHIPPING		
YARD STORAGE		
ERECTION		
CONCRETE INSTRUCTIONS		
CONCRETE RELBRSE @ 2,500 P.S.I.		
CONCRETE @ 28 DAYS: 5,000 P.S.I.		
CONCRETE MIXES		
CONCRETE - GRAY	VOLUME = 2.23	C.Y.
CONCRETE - MIX 1	VOLUME = -	C.Y.
CONCRETE - MIX 2	VOLUME = -	C.Y.
SOFT SOUND	VOLUME = -	C.Y.
TOTALS	VOLUME = 2.23	C.Y.
WEIGHT: 9,055 LBS.		
FINISHING INSTRUCTIONS		
LR = LINER FINISH		
FF = FORM FINISH		
HT = HARD TROWEL FINISH		
H = 7'-6 1/2"	SQ.FT.(T.I.F.) = 222.79	
W = 29'-9"	SQ.FT.(T.I.F.) = -	
D = 3"	SQ.FT.(T.I.F.) = -	
CONTROL NUMBERS:		
-		
PRODUCT BUILDING		SALES ORDER NUMBER
SHEET NUMBER		NUMBER REQUIRED
1 OF 2		1

EASI EASI-SET® WORLDWIDE

5119 Catlett Rd. • Midland, VA 22728 • info@EasiSet.com

WWW.EasiSet.com • 800-547-4045 • Fax 540-439-2541

REV	INI	DESCRIPTION	DATE
1	-	-	-
2	-	-	-
3	-	-	-
4	-	-	-
5	-	-	-

PROJECT: 60'x10'x9'-10" BASEBALL DUGOUT

5185 FORT CAMPBELL BOULEVARD

HOPKINSVILLE, KY 42240

CONTRACTOR: CHRISTIAN COUNTY SCHOOLS


SCALE NTS

DRAWN BY FTL

CHECK BY WCR


ISSUE DATE 07.30.26

PIECE MARK WP-03

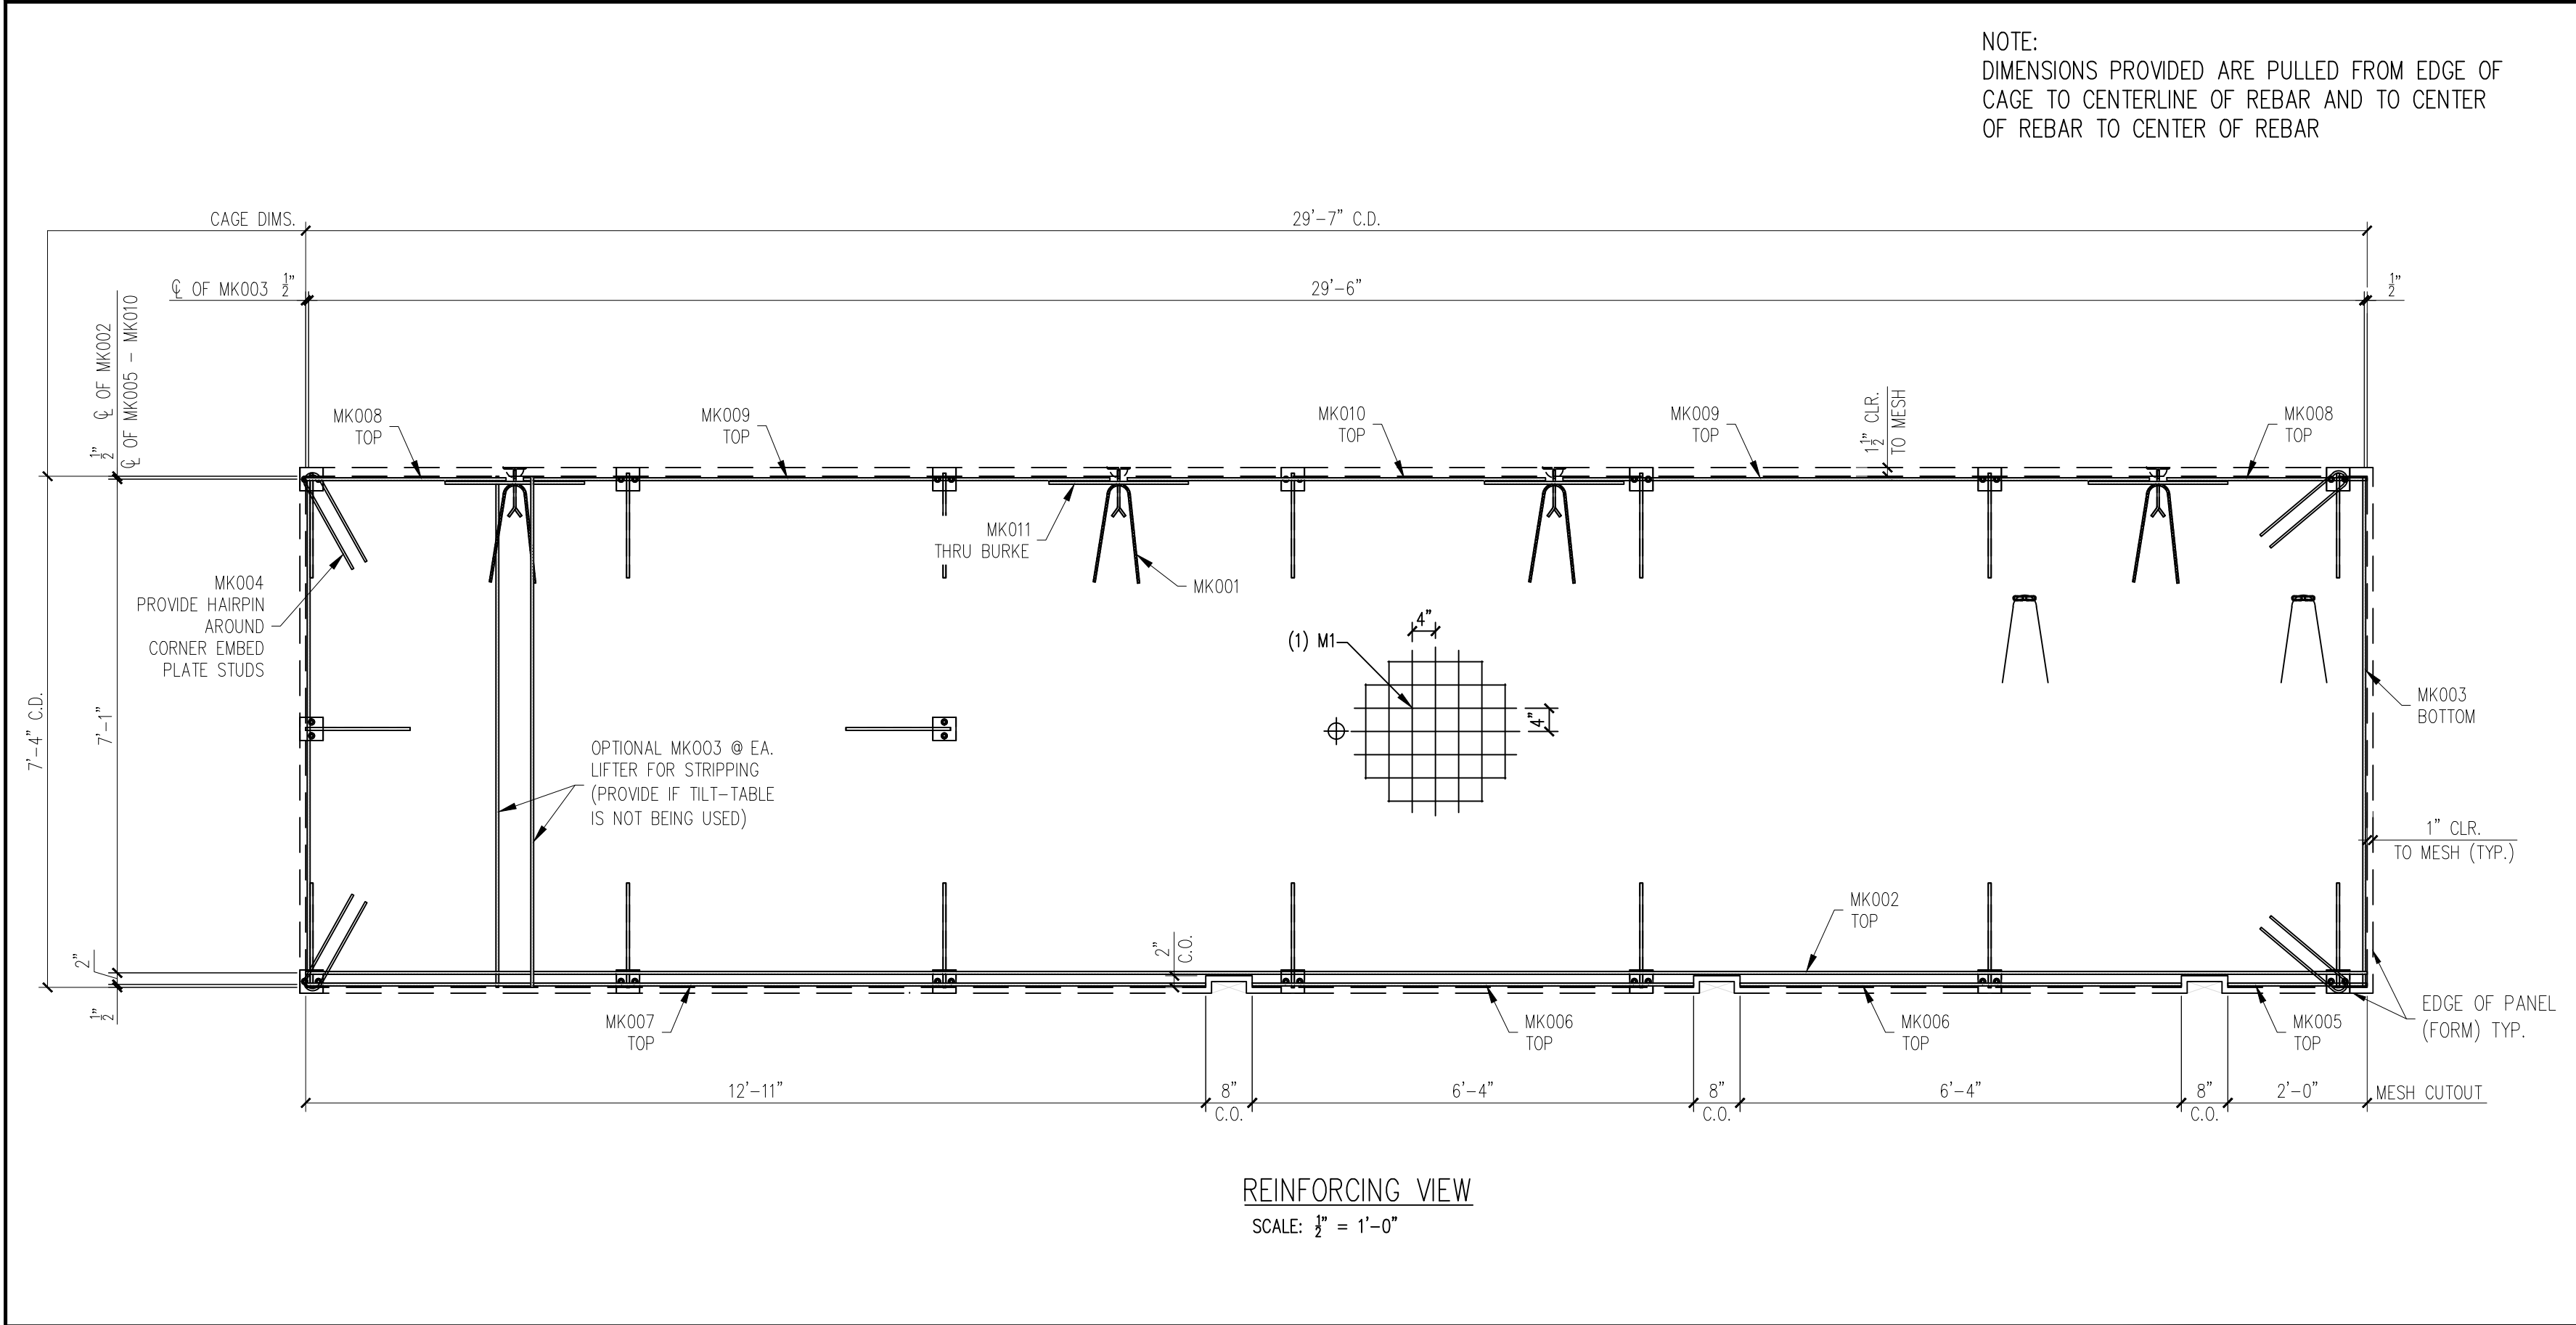

REINFORCING VIEW
SCALE: $\frac{1}{2}$ " = 1'-0"

REINFORCING SCHEDULE		
MARK #	DESCRIPTION	QTY.
MK001	#3 X 3'-0"	6
MK002	#3 X 29'-7"	1
MK003	#3 X 7'-4"	2
MK004	#3 X 3'-1"	4
MK005	#3 X 2'-0"	1
MK006	#3 X 6'-4"	2
MK007	#3 X 12'-11"	1
MK008	#3 X 2'-10 1/2"	2
MK009	#3 X 8'-5"	2
MK010	#3 X 6'-0"	1
MK011	#3 X 2'-0"	4
MESH SCHEDULE		
MARK #	DESCRIPTION	QTY.
M1	W4XW4 4"X4" WWF 29'-7" X 7'-4"	1

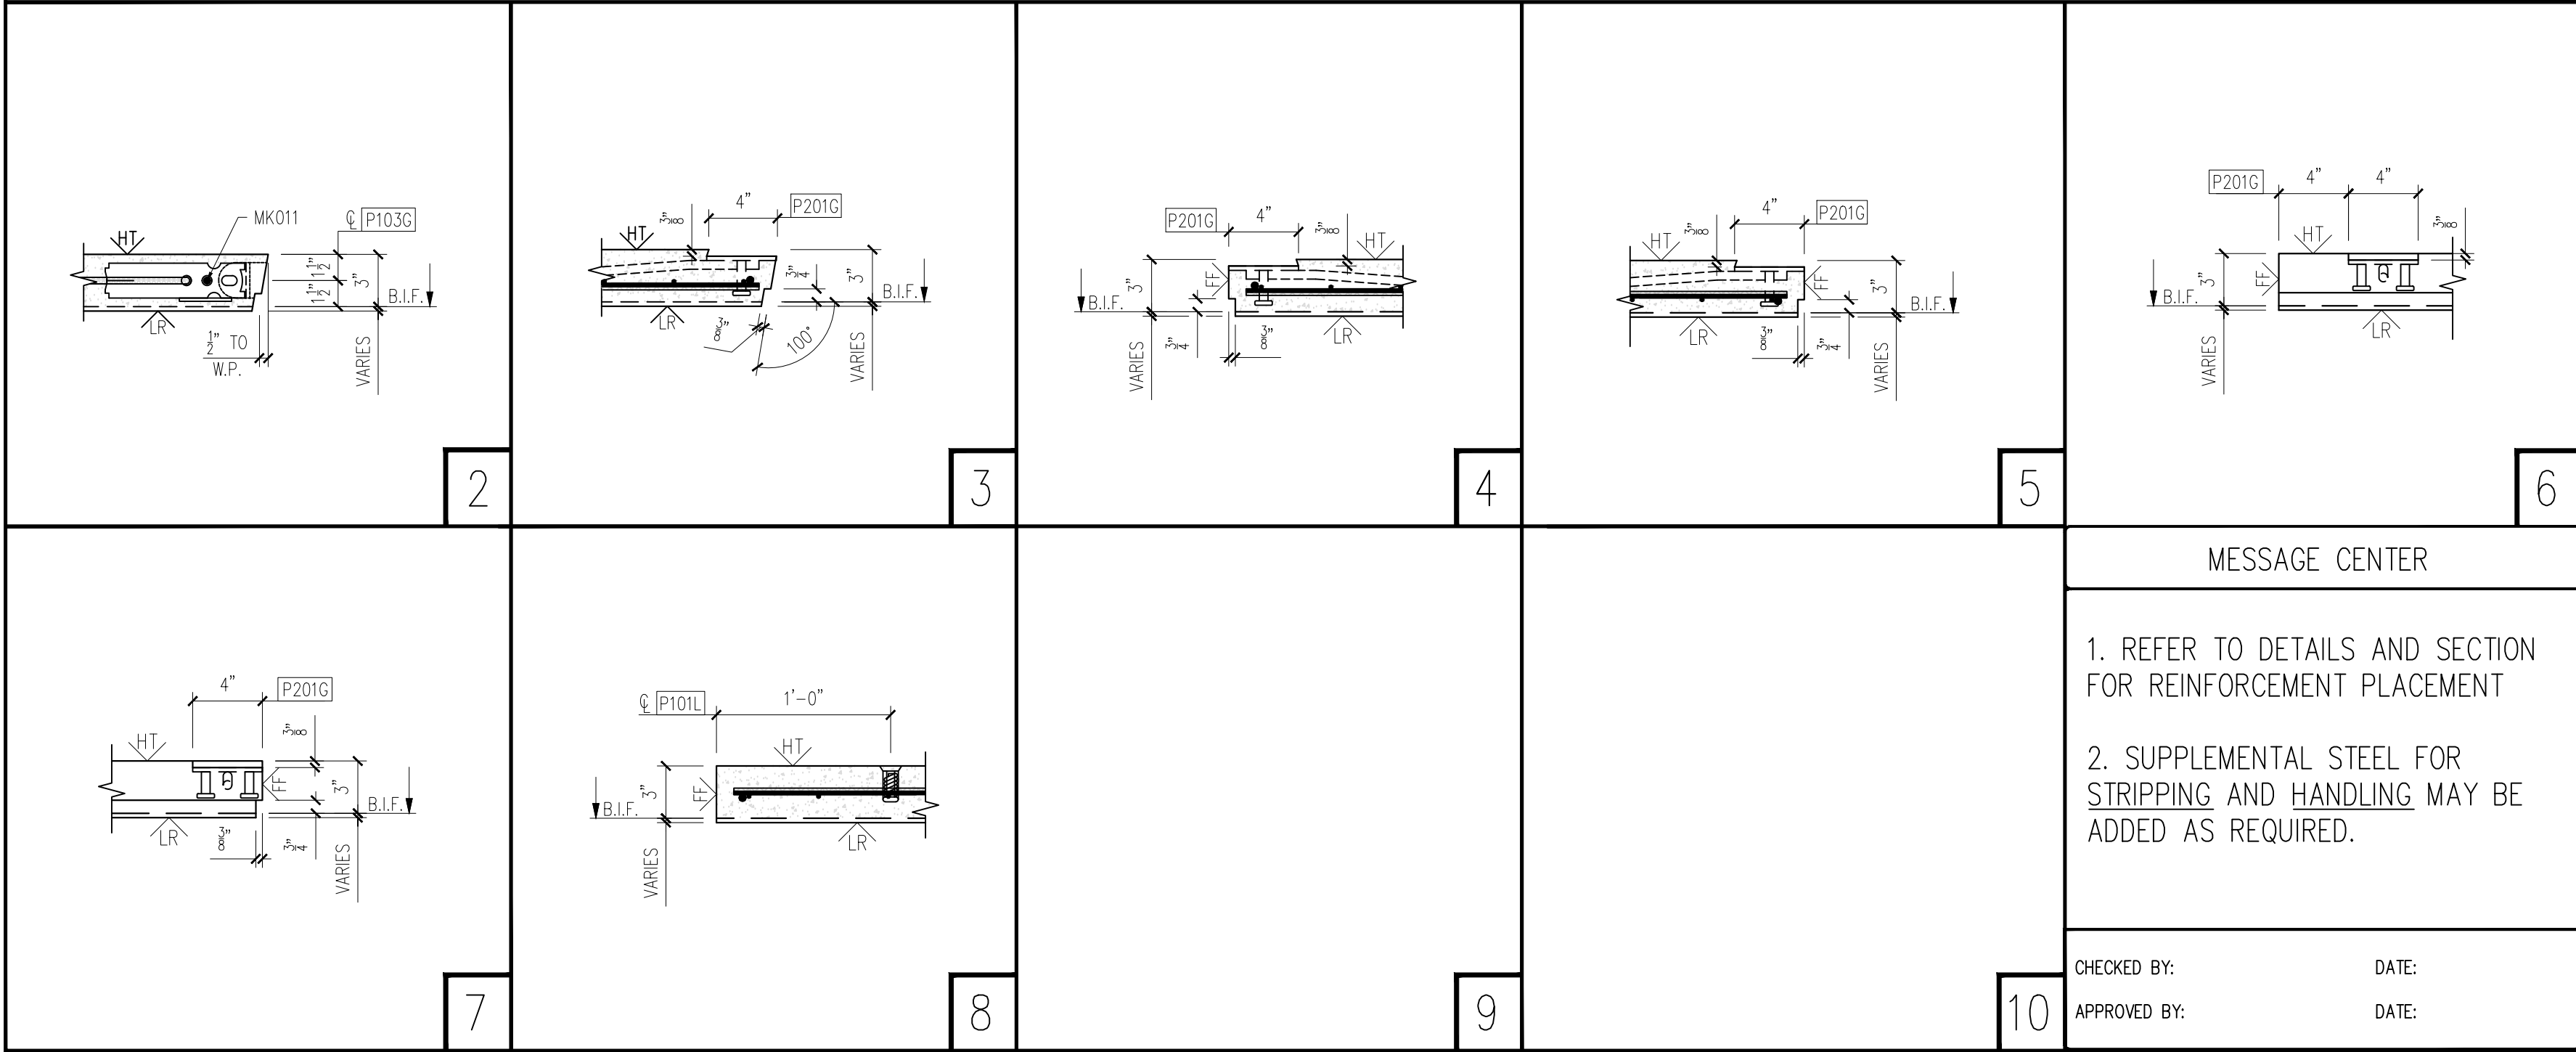

25-3470P6
Baseball Dugout 7B
ID - CVW
Floor - WP-03
Weight - 9,055
1 Required

NOTE:
1. CONSTRUCT REBAR-MESH CAGE
ACCORDING TO THE DRAWINGS. SECURE
LIFTING APPARATUS TO FORM AND ADD
PROPER REINFORCEMENT. PLACE
REBAR-MESH CAGE AND HAIRPINS AT
INSERTS WITH PROPER CLEARANCES
(PER DRAWINGS).

PRODUCT	SALES ORDER NUMBER
BUILDING	-
SHEET NUMBER	NUMBER REQUIRED
2 OF 2	1

EASI-SET® WORLDWIDE

5119 Catlett Rd. • Midland, VA 22728 • info@EasiSet.com
www.EasiSet.com • 800-547-4045 • Fax 540-439-2541

REV	DESCRIPTION	DATE
INI.		
1		
2		
3		
4		
5		
6		
7		
8		
9		
10		

PROJECT: 60'x10'x9'-10" BASEBALL DUGOUT
5185 FORT CAMPBELL BOULEVARD
HOPKINSVILLE, KY 42240
CONTRACTOR: CHRISTIAN COUNTY SCHOOLS

SCALE
NTS

DRAWN BY
FTL

CHECK BY
WCR

ISSUE DATE
07.30.26

PIECE MARK
WP-03
