

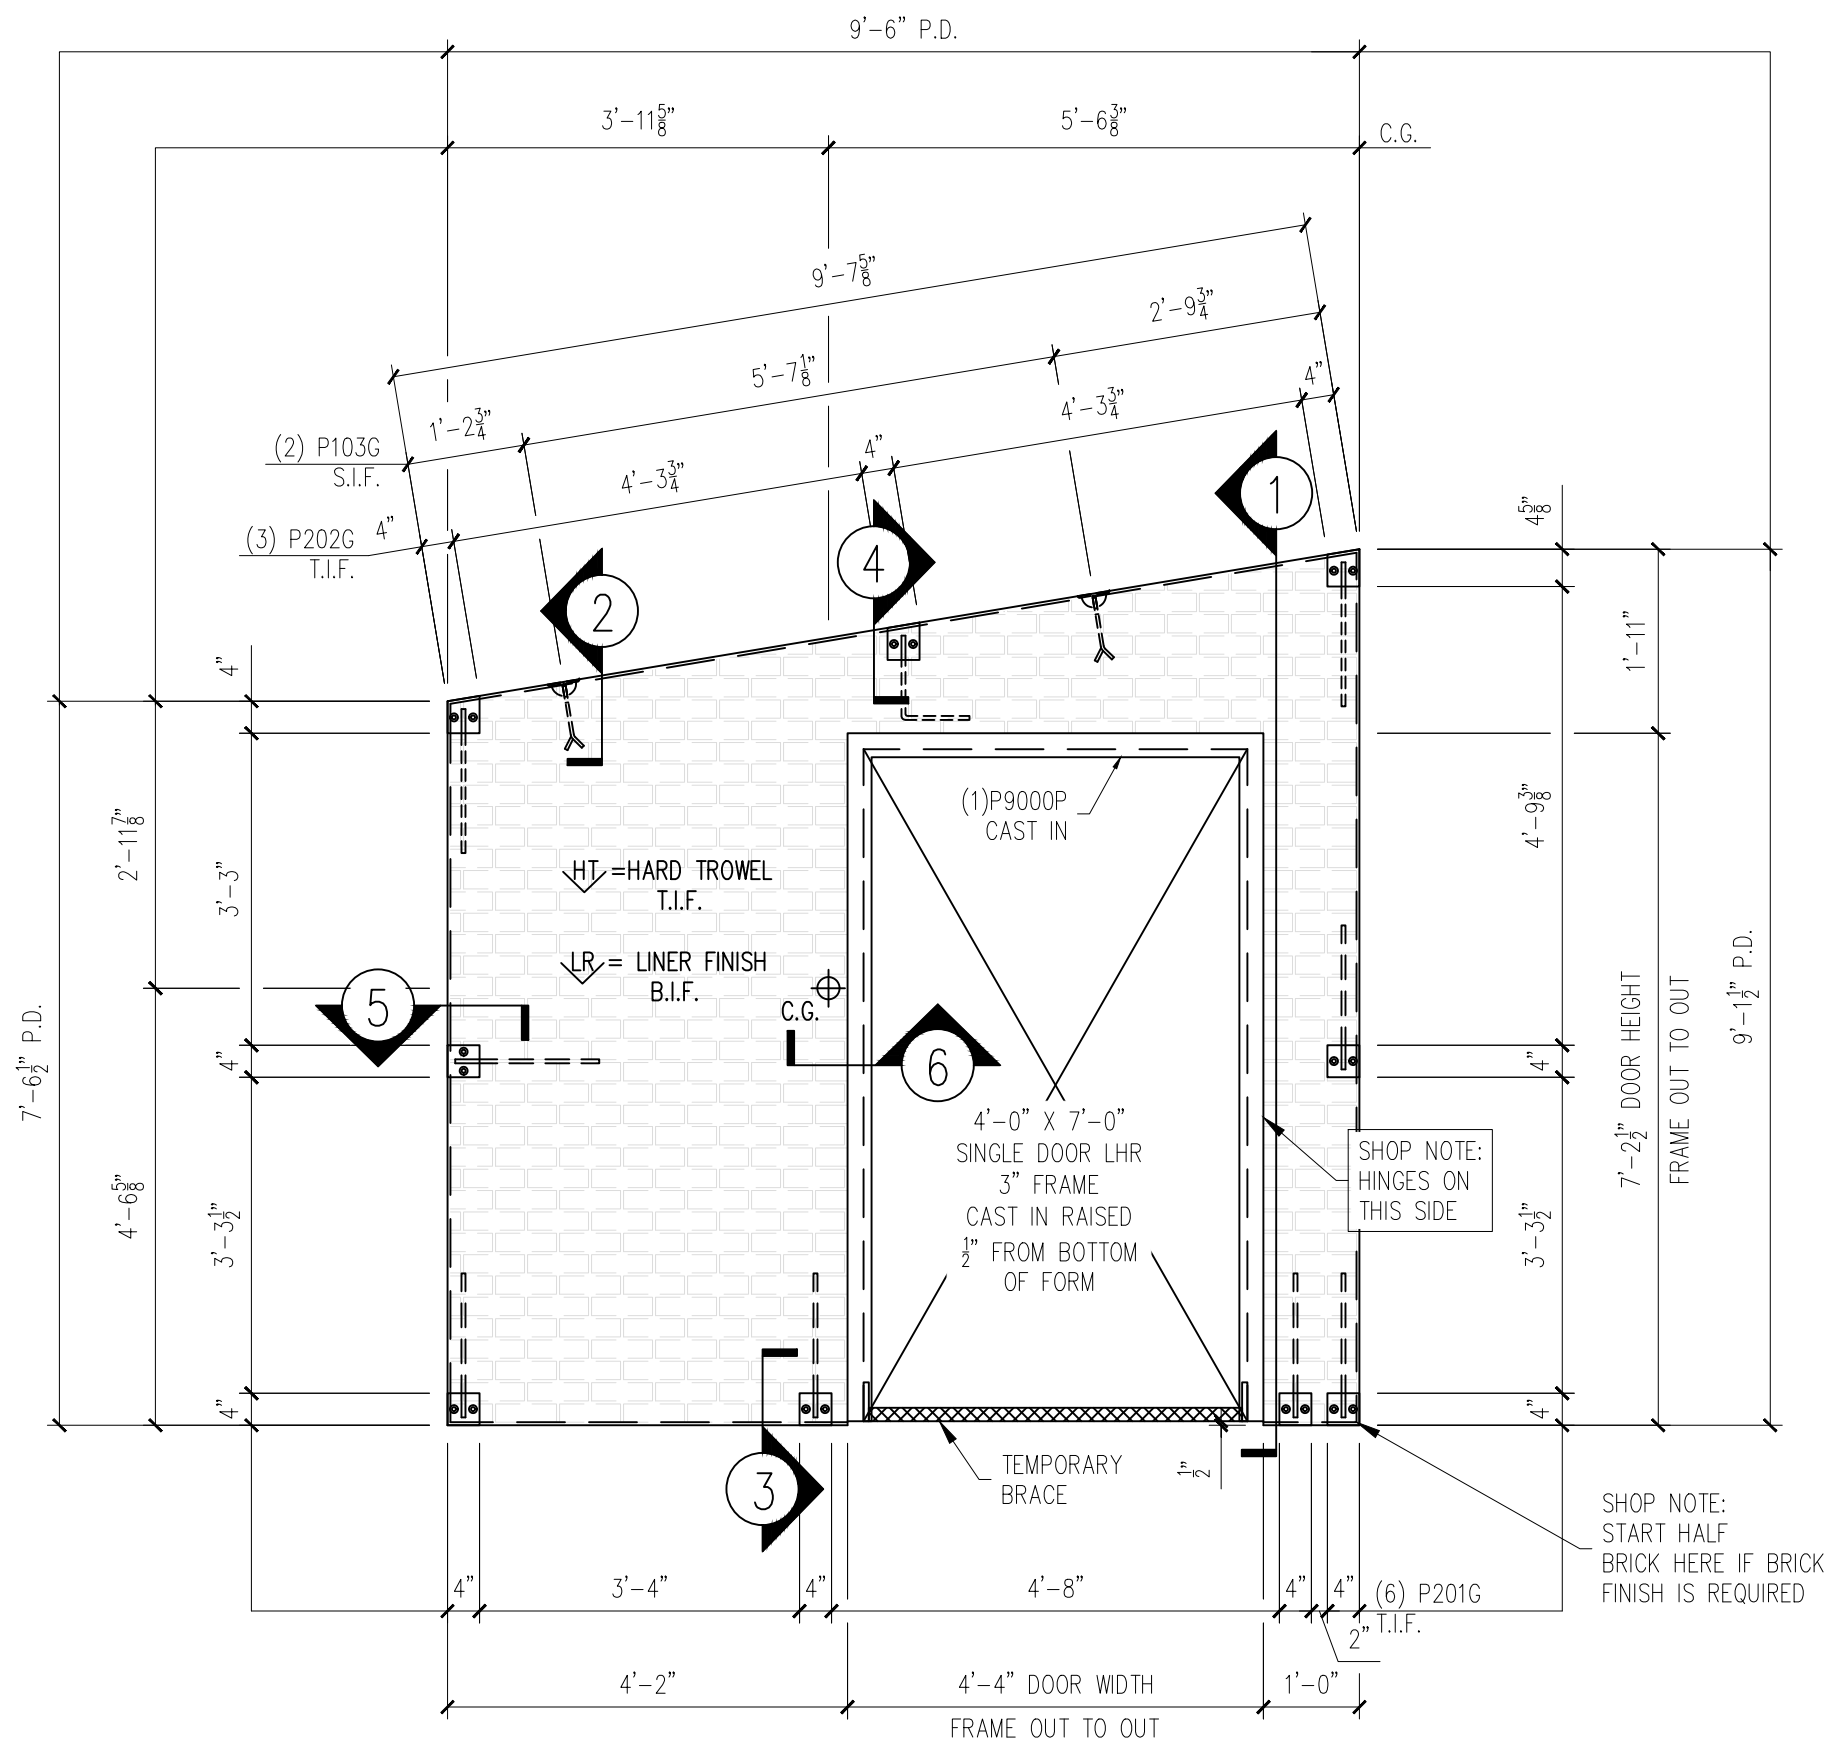
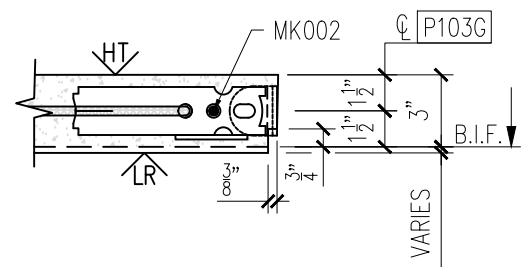
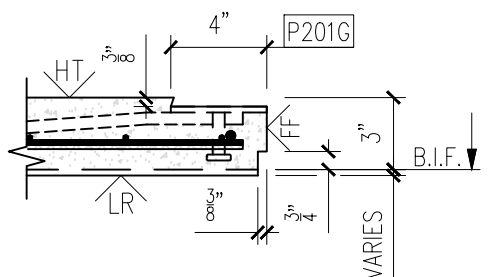
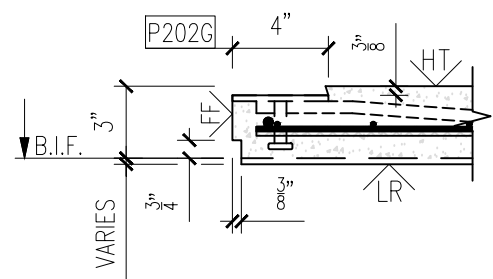


25-3470P6
Baseball Dugout 7B
ID - CVW
Floor - WP-06
Weight - 1,950
1 Required

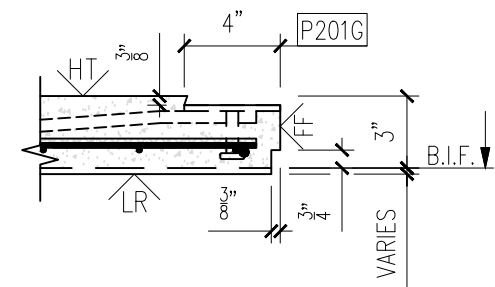

FORM VIEW
SCALE: 1/2" = 1'-0"

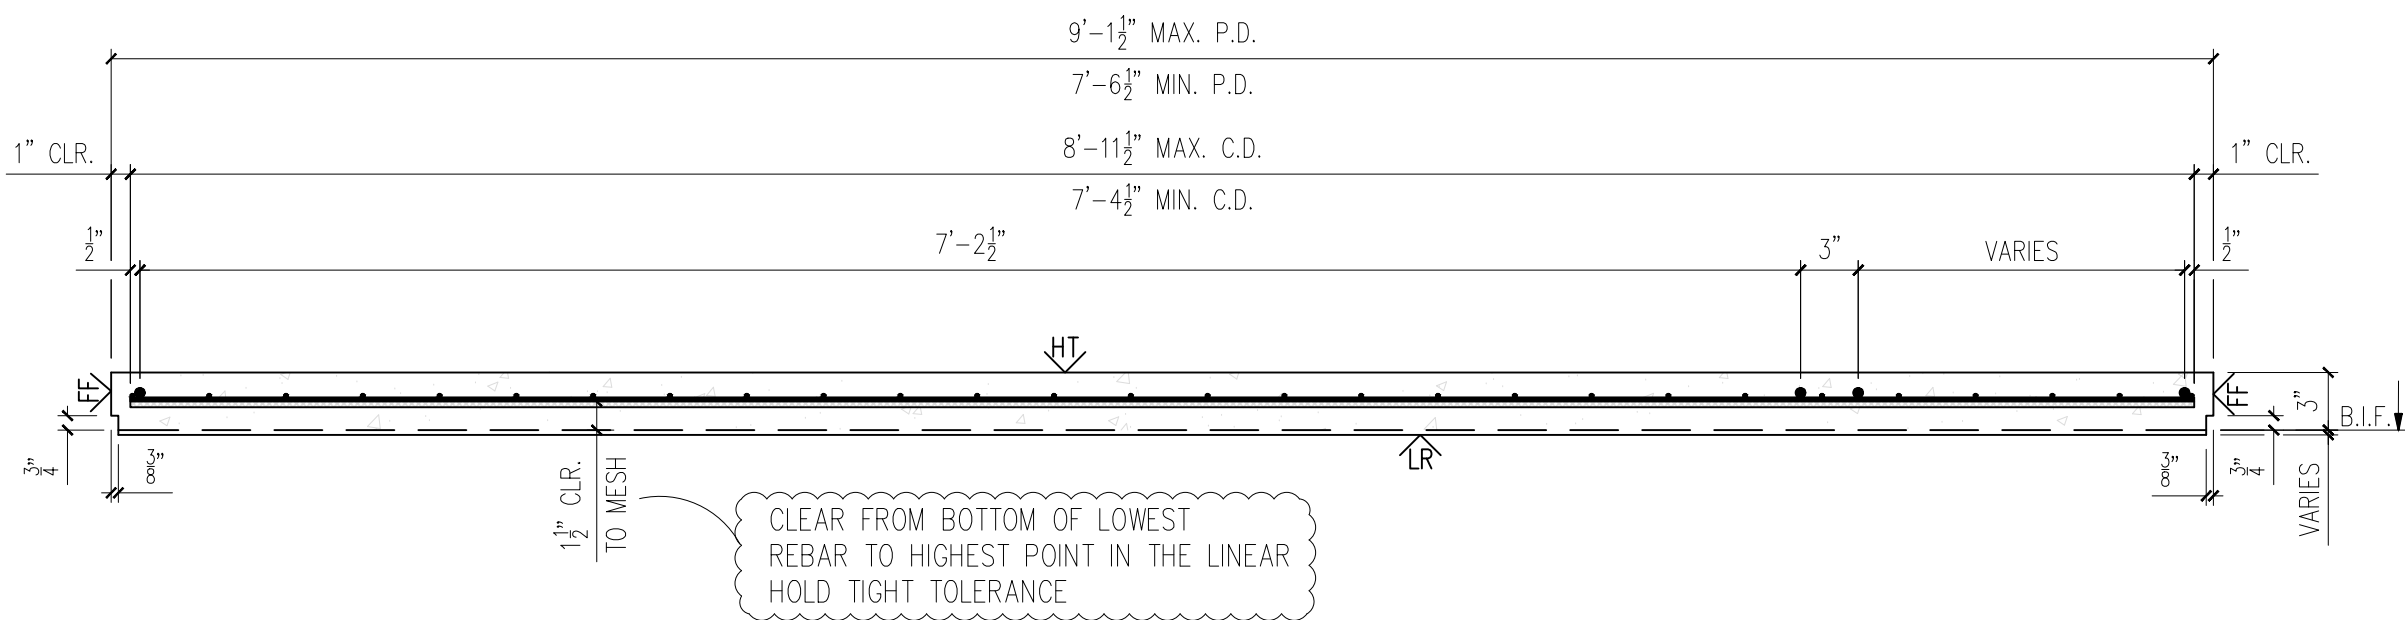

MESSAGE CENTER

1. REFER TO DETAILS AND SECTION FOR REINFORCEMENT PLACEMENT

2. SHOP TICKET SHOWS EXTERIOR FINISH CAST FACE DOWN

CHECKED BY:

DATE:



APPROVED BY:

DATE:



BILL OF MATERIALS

MARK #	DESCRIPTION	QTY.
P103G	2 TON RL-4 TECH ERECTION ANCHOR (79527) (GALV.)	2
P201G	4"X4"X3/8"W/(2) 3/8"Ø X 1 1/2" H.A.S. W/ 1'-4" BENT REBAR (GALVANIZED)	6
P202G	4"X4"X3/8"W/(2) 3/8"Ø X 1 1/2" H.A.S. W/ 1'-4" BENT REBAR (GALV.)	3
P9000P	4'-0" X 7'-0" LHR 3" DOOR FRAME	1

HANDLING INSTRUCTIONS



YARD STORAGE



CONCRETE INSTRUCTIONS

CONCRETE RELEASE @ 2,500 P.S.I.
CONCRETE @ 28 DAYS: 5,000 P.S.I.

CONCRETE MIXES

CONCRETE - GRAY	VOLUME = 0.48 C.Y.
CONCRETE - MIX 1	VOLUME = - C.Y.
CONCRETE - MIX 2	VOLUME = - C.Y.
SOFT SOUND	VOLUME = - C.Y.
TOTALS	VOLUME = 0.48 C.Y.

WEIGHT: 1,950 LBS.

FINISHING INSTRUCTIONS

LR = LINER FINISH

FF = FORM FINISH

HT = HARD TROWEL FINISH

H = 9'-1 1/2" SQ.FT.(T.I.F.) = 47.93

W = 9'-6" SQ.FT.(T.I.F.) = -

D = 3" SQ.FT.(T.I.F.) = -

CONTROL NUMBERS:

-

-

PRODUCT

SALES ORDER NUMBER

BUILDING

-

SHEET NUMBER

NUMBER REQUIRED

1 OF 2

1

PROJECT: 60'x10'x9'-10" BASEBALL DUGOUT
5185 FORT CAMPBELL BOULEVARD
HOPKINSVILLE, KY 42240
CONTRACTOR: CHRISTIAN COUNTY SCHOOLS

DATE	DESCRIPTION	REV	INI.

SCALE NTS
DRAWN BY FTL
CHECK BY WCR
ISSUE DATE 07.30.26
PIECE MARK WP-06

SCALE NTS
DRAWN BY FTL
CHECK BY WCR
ISSUE DATE 07.30.26
PIECE MARK WP-06

5119 Catlett Rd. • Midland, VA 22728 • info@EasiSet.com
www.EasiSet.com • 800-547-4045 • Fax 540-439-2541


SCALE NTS
DRAWN BY FTL
CHECK BY WCR
ISSUE DATE 07.30.26
PIECE MARK WP-06

SCALE NTS
DRAWN BY FTL
CHECK BY WCR
ISSUE DATE 07.30.26
PIECE MARK WP-06


SCALE NTS
DRAWN BY FTL
CHECK BY WCR
ISSUE DATE 07.30.26
PIECE MARK WP-06

25-3470P6
Baseball Dugout 7B
ID - CVW
Floor - WP-06
Weight - 1,950
1 Required

NOTE:
DIMENSIONS PROVIDED ARE PULLED FROM EDGE OF
CAGE TO CENTERLINE OF REBAR AND TO CENTER
OF REBAR TO CENTER OF REBAR

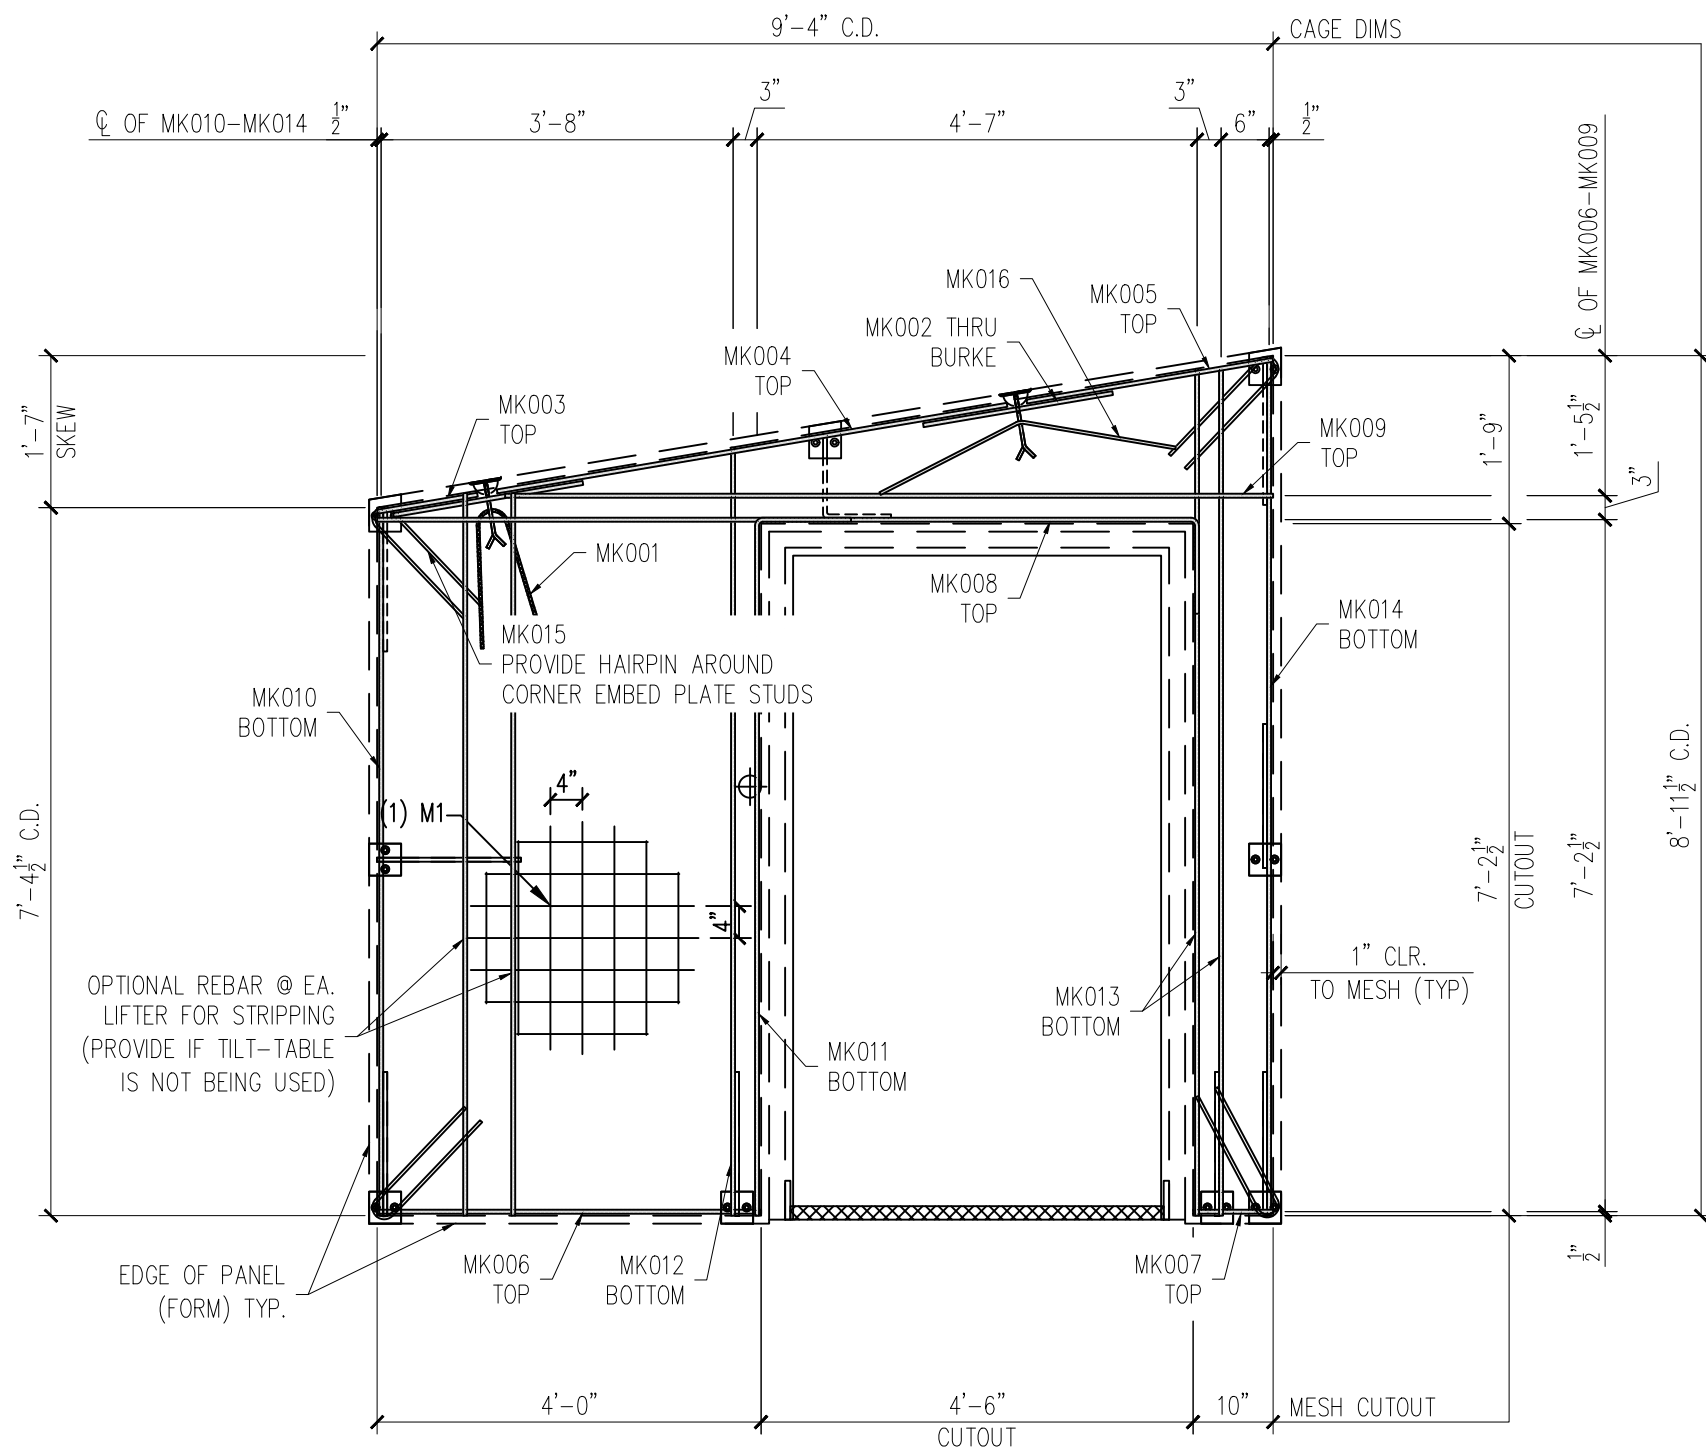

REINFORCING VIEW
SCALE: 1/2" = 1'-0"



MESSAGE CENTER

1. REFER TO DETAILS AND SECTION FOR REINFORCEMENT PLACEMENT
2. SUPPLEMENTAL STEEL FOR STRIPPING AND HANDLING MAY BE ADDED AS REQUIRED.

NOTE:
1. CONSTRUCT REBAR-MESH CAGE ACCORDING TO THE DRAWINGS. SECURE LIFTING APPARATUS TO FORM AND ADD PROPER REINFORCEMENT. PLACE REBAR-MESH CAGE AND HAIRPINS AT INSERTS WITH PROPER CLEARANCES (PER DRAWINGS).

PRODUCT	SALES ORDER NUMBER
BUILDING	-
SHEET NUMBER	NUMBER REQUIRED
2 OF 2	1

12

11

10

REINFORCING SCHEDULE		
MARK #	DESCRIPTION	QTY.
MK001	#3 X 3'-0"	1
MK002	#3 X 2'-0"	2
MK003	#3 X 1'-0 1/2"	1
MK004	#3 X 5'-4 1/2"	1
MK005	#3 X 2'-7"	1
MK006	#3 X 4'-0"	1
MK007	#3 X 10"	1
MK008	#3 X 9'-5 3/4"	1
MK009	#3 X 8'-0"	1
MK010	#3 X 7'-4 1/2"	1
MK011	#3 X 8'-2 1/4"	1
MK012	#3 X 8'-0"	1
MK013	#3 X 8'-9 3/4"	2
MK014	#3 X 8'-11 1/4"	1
MK015	#3 X 3'-1"	4
MK016	#3 X 3'-0"	1

MESH SCHEDULE		
MARK #	DESCRIPTION	QTY.
M1	W4XW4 4"X4" WWF 8'-11 1/2" X 9'-4"	1

EASI-SET® WORLDWIDE
5119 Catlett Rd. • Midland, VA 22728 • info@EasiSet.com
www.EasiSet.com • 800-547-4045 • Fax 540-439-2541

REV	DESCRIPTION	DATE
1		

PROJECT: 60'x10'x9'-10" BASEBALL DUGOUT
5185 FORT CAMPBELL BOULEVARD
HOPKINSVILLE, KY 42240
CONTRACTOR: CHRISTIAN COUNTY SCHOOLS

SCALE NTS
DRAWN BY FTL
CHECK BY WCR
ISSUE DATE 07.30.26
PIECE MARK WP-06
